


**DETAILED PROJECT REPORT
OF
MIDDLE UMLEW & UMPRAH WATERSHED
INTEGRATED WATERSHED MANAGEMENT PROGRAMME,
(IWMP) EAST KHASI HILLS – VIII
UNDER
MAWKYNREW C & R D BLOCK**



**EAST KHASI HILLS DISTRICT
SOIL & WATER CONSERVATION DEPARTMENT,
TERRITORIAL DIVISION, SHILLONG.**

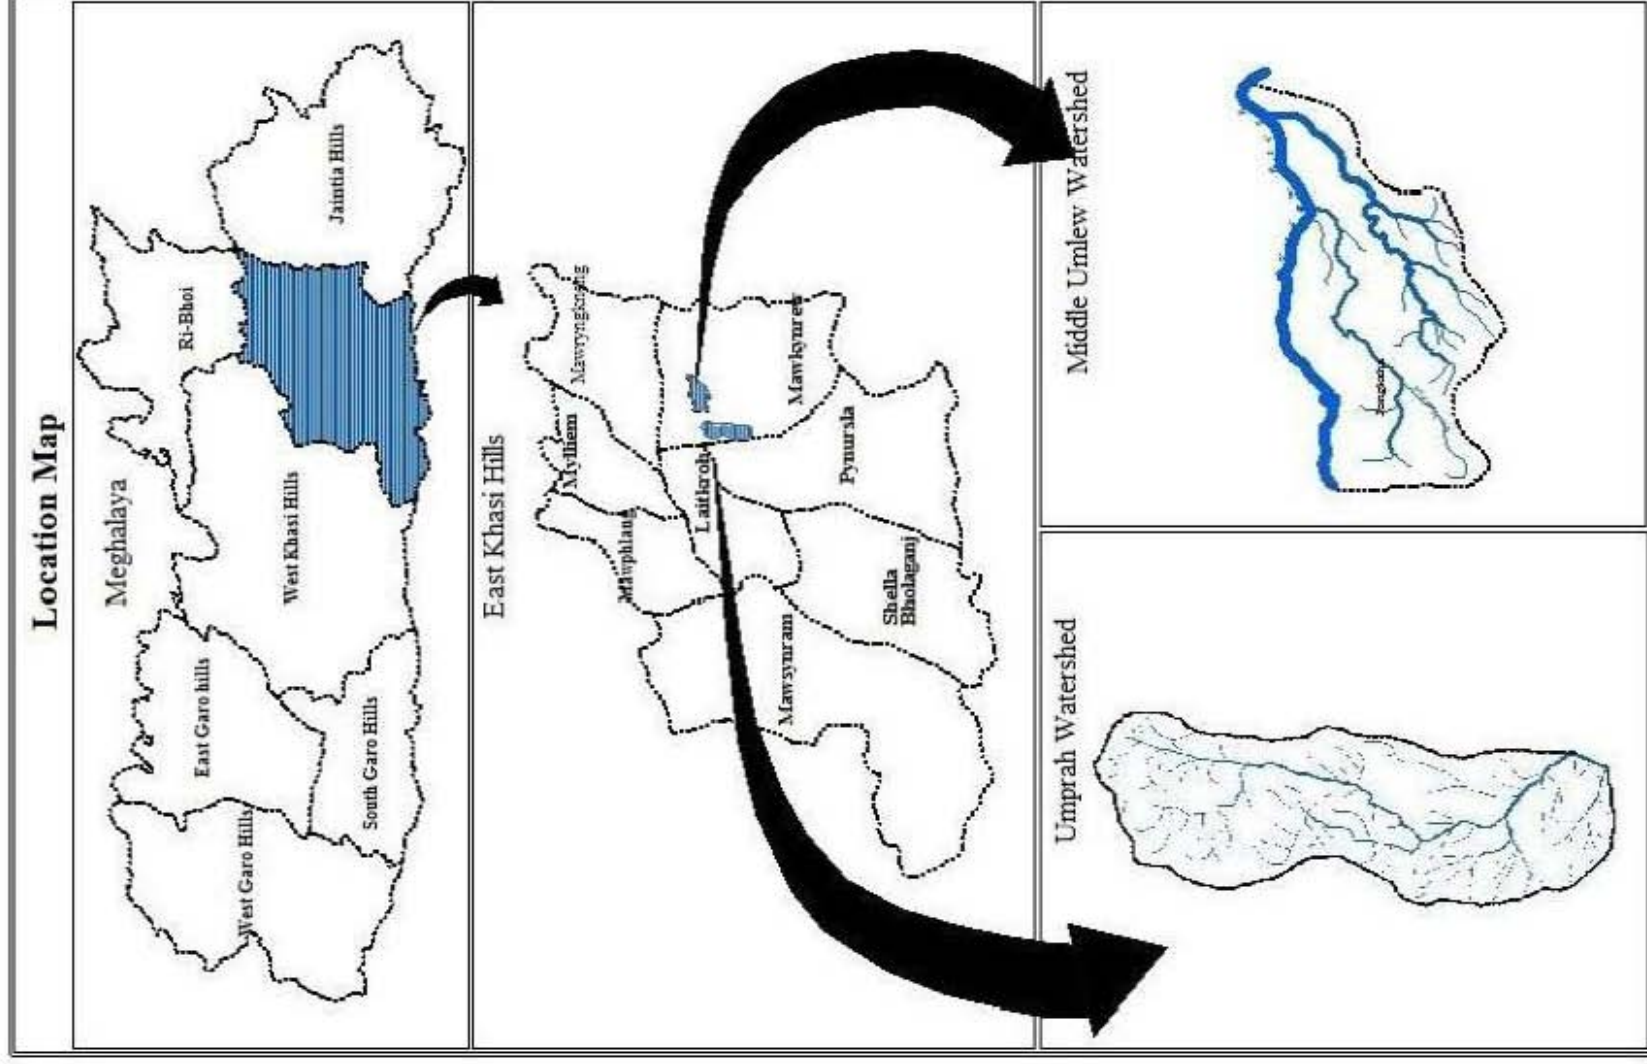

SUMMARY

Name of the Sate	:	Meghalaya
Name of the District	:	East Khasi Hills District
Name of the C&RD Block	:	Mawkynrew C & RD Block
Name of the Villages	:	(i) Jongksha (ii) Laitkyrhong (iii) Laitlum
Name of the Project	:	East Khasi Hills – IWMP – VIII
Total Geographical Area	:	1434 Ha
Total Treatment Area	:	1000 Ha
Total Project Cost	:	150 lakhs
Project Duration	:	5 Years
Project Implementing Agency	:	Soil & Water Conservation Territorial Division, Shillong.

TABLE OF CONTENTS

CHAPTER - I	INTRODUCTION AND BACKGROUND	7
CHAPTER - II	BASIC INFORMATION OF THE PROJECT AREA.....	9
CHAPTER - III	PROJECT PLANNING & INSTITUTION BUILDING.....	19
CHAPTER - IV	PROJECT ACTIVITIES.....	26
CHAPTER - V	PROJECT PHASING & BUDGETING.....	42
CHAPTER - VI	CAPACITY BUILDING.....	55
CHAPTER - VII	EXPECTED OUTCOME.....	60
ANNEXURE I	MAPS.....	78
ANNEXURE II	SOCIO – ECONOMIC SURVEY DETAILS.....	93
ANNEXURE III	COST ESTIMATES.....	121
ANNEXURE IV	CERTIFICATE OF REGISTRATION, N.O.C. ETC.....	139



Panoramic view of Umprah Watershed IWMP – VIII



Panoramic view of Middle Umlew Watershed IWMP - VIII

CHAPTER I

INTRODUCTION AND BACKGROUND

CHAPTER I

INTRODUCTION AND BACKGROUND

1.1 Project Background:

The Middle Umlew & Umprah (IWMP-VIII) project is located in Mawkynrew C&RD Block, East Khasi Hills District of Meghalaya. Consisting of a two micro -watershed. The total area is Ha with 1000 to be treated under the Integrated Watershed Management Programme (IWMP).

The Project area is located at a distance of about 38 km from Shillong the District Headquarter and also the State Capital. A total of three villages are covered under the project. These are –

- 1 Jongksha
- 2 Laitkyrhong
- 3 Laitlum

1.2 Micro-watershed Information:

The micro-watershed code of Middle Umlew is 3C1C2a3e and that of Umprah Micro Watershed is 3C1C2a4h as codified by the North East Space Application Centre (NESAC). The total area of the micro-watershed is 1434Ha, with 1000 hectares to be treated under the Integrated Watershed Management Programme (IWMP).

1.3 Need and Scope for Watershed Development:

The micro-watershed falls under the High Priority category as per the prioritization of watersheds by the North East Space Application Centre (NESAC). The people in the watershed area are mostly marginal farmer and 397 households are below the poverty line, which is 44.25 % of the total households which is of 895 nos. Bun cultivation is practiced by most of the inhabitants of these villages on the slopes.

Even though the area receives ample rainfall during the monsoons, there is acute shortage of water during the dry seasons and the villagers have to travel long distances for fetching water even for domestic use.

1.4 Other developmental projects/schemes running in the Project Area:

The other developmental projects/schemes undertaken in the Project Area are:-

- i. MGNREGS
- ii. Total Sanitation Campaign (TSC)
- iii. Swarnjayanti Gram Swarozgar Yojana (SGSY)
- iv. Indira Awas Yojana (IAY)

CHAPTER II

BASIC INFORMATION OF THE PROJECT AREA

CHAPTER II

BASIC INFORMATION OF THE PROJECT AREA

2.1 Location:

The Project area is located within the area of Khyriem Syiemship under Mawkynrew C&RD Block East Khasi Hills District. It is situated at a distance of about 38 km from Shillong the District Headquarter which is also the State Capital. The geographical location of Middle Umlew Watershed is between $91^{\circ} 57'30''$ to $92^{\circ} 01' 00''$ E Longitude and $25^{\circ} 26'00''$ to $25^{\circ} 29' 00''$ N Latitude., and that of Umprah Watershed is between $91^{\circ} 57'30''$ to $92^{\circ} 01'00''$ E Longitude and $25^{\circ} 24'00''$ to $25^{\circ} 28'30''$

1. Jongksha
2. Laitkyrhong
3. Laitlum

All the three villages are connected by motorable road.

2.2 Physiography:

The physiography of the micro-watershed is composed by undulating tract with moderately gentle sloping land with small pocket to medium valley bottom land. The altitude ranges from a minimum of 1100m to a high of 1600m above mean sea level. The general sloping land of the two Micro – Watershed area is 5° – 10° upto more than 45° .

Table 2.1: Physiographic details

Elevation (metres)	Slope Range (%)	Order of watershed Sub/Micro-watershed	Major streams	Topography
1100 m to 1600 m	5° to 45° .	Micro Watershed	Umlew, Umprah	Undulating tract & gentle Sloping

2.3 Drainage: The major stream draining the two micro- watershed is the Wah Umlew and Umprah Stream which is a 4th and 5th order stream respectfully flowing in a North-East direction. The slopes of these two micro- watershed are dissected by numerous small tributaries flowing to the Wah Umlew and Umprah stream.

2.4 Soil: Soil Texture is clay loam structure. Soil depth varies from very shallow to deep. Soils are permeable and generally acidic in nature. Owing to faulty agricultural cultivation and absence of good vegetation cover, the area is exposed to erosion hazards. The soil nutrient status in the area shows a general trend of low phosphorous content.

Table 2.2: Details of soil erosion in the project areas:

1	2	3	4	5	6	7	8	9
Sl. No.	Names of State	Names of District	Names of Projects	Cause	Types of erosion	Area affected (ha)	Run-off (mm/ year)	Average soil loss (Tonnes/ ha/ year)
1	Meghalaya	East Khasi Hills	East Khasi Hills – IWMP VIII	Water erosion:				
				a	Sheet	1000	2700- 3200	10.50 – 15.00
				b	Rill			
				c	Gully			
				Sub total		1000	2700- 3200	10.50 – 15.00
				Wind erosion		Nil	Nil	Nil

2.5 Climate: The Watershed area is characterized by temperate climate. It falls under the central thermic Plateau Agro-Climatic Zone with cold moisture and cold wet. Maximum temperature ranges 15⁰C to 25⁰ C and minimum temperature is between 5⁰ C upto 17⁰ C. The climate is moderate type with a pleasant summer and Extreme cold in winter season. The annual relative humidity is between 70 to 85% annually.

The average rainfall is 2283mm (approximately). Main rainy months are June, July, August and September. The month of June & July account for the major share of rainfall with a very high intensity of showers.

Table 2.3: Agro-climatic zones of the project areas, soil types, average rainfall and major crops.

1	2	3	4	5	6	7		8	9	
Sl. No.	Name of State	Name of the Agro-climatic zone	Area (in ha)	Names of the districts	Names of the Projects	Major soil types		Average annual rainfall in mm (preceding 5 years' average)	Major crops	
						a)Type	b) Area (ha)		a) Name	b) Area (ha)
1	Meghalaya	Central thermic Plateau	1000 Ha	East Khasi Hills	East Khasi Hills IWMP – VIII	Moderate shallow, excessively drained, fine – loamy soil on moderately steep side slopes of hills having loamy surfaces with severe erosion hazard and strong stoniness associated with moderately Shallow, excessively drained, loamy skeletal soils on gently sloping hill tops with very severe erosion hazard and slight stoniness	1434 Ha	2283 mm	Potato	30
									Cabbage	25
									Tomato	5
								Total		60 Ha

2.6 Agriculture: Agriculture is the primary occupation of the people of the area. The people mostly practice Bun cultivation. The bun plots vary from 0.5 to 1.0 Ha, and are cultivated for 3-4 years. The principal agricultural crops grown of the bun fields are potato, Cabbage, Tomato, Cauliflower, maize and vegetables.

Table 2.4: Crop yield and production

Crops	Area (ha)	Average Yield (Qtl) per ha.	Total Production (Qtl.)
Potato	30	60	1800
Cabbage	25	150	3750
Tomato	5	21	105

2.7 Natural Vegetation: The tree species common to the watershed area includes - *Quercus* spp. *Castanopsis* spp. *Toona ciliata*, *Albizia* spp. *Alnus nepaliensis*, *betula* spp. etc. However, due to bun cultivation the forest cover of the area has reduced considerably.

2.8 Socio-Economic Profile: Economically, the area is perhaps the most backward in the district. The main reason is due to the practice of primitive way of agricultural practices like bun cultivation in the steep slope without any agronomic measures.

Demographic Status: The total households in the watershed project are 895 with a total population of 5058, of which 2471 are male and 2593 are female. The detail of the household in each of the villages in the watershed project is as follows:

1.	Jongksha	-	468 Nos.
2.	Laitkyrhong	-	356 Nos.
3.	Laitlum	-	71 Nos.
			895 Nos.

Infrastructure facilities :

- 2.1.1 *Roads:* All the villages within the Project Area are connected by P.W.D. road.
- 2.1.2 *School:* There are 17 nos. of L.P Schools and 7 nos. of Secondary School within the Project Area run either by the Mission or by the Government.
- 2.1.3 *Electricity:* All the villages in the Watershed area have electricity Connections.
- 2.1.4 *Health:* One Primary Health Centre at Jongksha and the local population have to either depend on facilities available at Smit or Shillong.
- 2.1.5 *Water Supply:* Drinking water supplies have been provided by the PHE Deptt. To all the villages. However, during lean season the entire populations have to depend on springs available in the area as the supply is not sufficient to meet the daily requirement.
- 2.1.6 *Market:* There is no weekly market at the watershed area. However, the main market where the people sell their produce is at Smit and also at Shillong.

Table 2.5: Infrastructure Status.

1	2	3		4			
Name of District	Name of Project	Parameters:		Status			
East Khasi Hills	East Khasi Hills – IWMP VIII	(i)	No. of villages connected to the main road by an all-weather road.	All villages are connected with PWD road.			
		(ii)	No. of village provided with electricity	3 nos. electrified.			
		(iii)	No. of households without access to drinking water	537 nos.			
		(iv)	No. of educational institutions: Primary (P)/ Secondary (S)/ Higher Secondary (HS)/ Vocational institution (VI)	(P)	(S)	(HS)	(VI)
				17 Nos.	7	Nil	Nil
		(v)	No. of village with access to Primary Health Centre	1 no			
		(vi)	No. of village with access Veterinary Dispensary	1 no.			
		(vii)	No. of village with access Post Office	Nil			
		(viii)	No. of village with access Banks	1 no.			
		(ix)	No. of village with access Markets/ mandis	1 no.			
		(x)	No. of village with access Agro-Industries	Nil			
		(xi)	Total quantity of surplus milk	Nil			
		(xii)	No. of milk collection centres (e.g. Union (U)/ Society (S)/ Private agency (PA)/ Others (O))	(U)	(S)	(PA)	(O)
				Nil	Nil	Nil	Nil
		(xiii)	No. of villages with access to Aganwadi Centres	7 Nos.			
		(xiv)	Any other facilities with no. of villages (please specify)	Nil			

2.9 Livestock: there are only 3 kinds of livestock farming being farmed in the area viz. Piggery, Poultry and Bee-Keeping or Apiculture.

Table 2.6: Existing livestock population

Type of Animal	Population
Cow	895
Piggery	838
Poultry	1737
Goatry	664
	4134

2.10 Land ownership: There are primarily two types of land holding system, namely private lands (Ri Kynti i.e. individually owned land) and community lands (Ri Kur i.e. clan land and Ri Raid i.e. village community land).

Table 2.7: Land Holding:

1	2	3	4	5	6		
Name of District	Name of the Project	Types of Farmer	No. of households	No. of BPL households	Land holding (ha)		
					Irrigated	Rainfed	Total
East Khasi Hills	East Khasi Hills – IWMP VIII	(i) Large	-	-			
		(ii) Small	-	-			
		(iii) Marginal	573	297	-	60Ha	60 Ha
		(iv) Landless	170	120	-	-	-
		Sub - Total	743	417		60Ha	60 Ha

Table 2.5: Common Property Resources in the Project Area

1	2	3	4				5			
Name of District	Name of the Projects	CPR Particulars	Total Area (ha) Area owned/ In possession of				Area available for treatment (ha)			
			Pvt. Person	Govt. (specify deptt.)	PRI	Any other (Community)	Pvt. Person	Govt. (specify deptt.)	PRI	Any other (Community)
East Khasi Hills	East Khasi Hills – IWMP VIII	(i) Wasteland/ degraded land	-	-		378 Ha	-	-	-	600Ha
		(ii) Pastures	-	-	-	-	-	-	-	-
		(iii) Private Agriculture land	-	-	-	-	400 Ha			
		(iv) Village woodlot	-	-	-	-				
		(v) Forest	-	-	-	153Ha				
		(vi) Village Ponds/ Tanks	-	-	-	-				
		(vii) Community Buildings	-		-	3 Nos.				
		(viii) Weekly Markets	-	-	-	Smit				
		(ix) Permanent Markets	-	-	-	Smit				
		(x) Temples/ Places of worship	-	-	-	Church- 9 nos.				
		(xi) Others (Pl. specify)	676 Ha	-	-	227 Ha				
		Total	676 Ha	-	-	758 Ha	400 Ha	-	-	600Ha

2.11 Land use and land cover : As per the land use land cover map generated by NESAC, Meghalaya from Satellite Image taken during 2005 – 2006 (LISS – III, Image) the Watershed area has been broadly classified into the following land uses.

a) Built-up Area	=	220 Ha
b) Water bodies-River/Stream-Perennial	=	7 Ha
c) Agricultural land-crop land-kharif crop	=	60 Ha
d) Tree clad Area-close	=	153 Ha
e) Tree clad Area-open	=	616 Ha
f) Wastelands-barren Rocky/Stony waste	=	<u>378 Ha</u>
Total	=	1434 Ha

2.12 Problems of the Area : The primary problems of the area due to the unscientific land and water uses which have adversely affected the carrying capacity of the environment which constitutes the basic life support system and further enhancing the resource gap like sustaining food production and meeting the growing need of the local population.

The other major problems of the area are listed below;

- Reduction of soil – water regime which subsequently lead to drying up of water resources.
- Disturbing and unbalancing soil – water nutrients relationship
- Deceasing soil fertility due to unscientific cultivation in the hill slopes which led to fast depletion of the fertile top soil along with plant nutrients.

CHAPTER III

PROJECT PLANNING & INSTITUTION BUILDING

CHAPTER III

PROJECT PLANNING & INSTITUTION BUILDING

3.1 Scientific Planning

- i) Base Line Survey: To establish a benchmark for assessing the impact of any intervention (pre-project & post project) a baseline survey is essential. The baseline survey included household census & socio-economic survey by using structured and semi –structured questionnaires, bio-physical survey to identify and assess the status of natural resources in the project area.
- ii) Participatory Rural Appraisal: To further obtain information on the project area, the people, resources, various PRA techniques like resource mapping, social mapping, seasonal calendars, matrix ranking, and Venn diagrams were used.
- iii) GIS & Remote Sensing: To facilitate the process of prioritization and planning Geographic Information System was use. The land use and land cover (LULC) maps were prepared by the North Eastern Space Application Centre (NESAC) using the LISS III images (2006). The activities were located on the field by using GPS and accordingly transferred to the maps on GIS platform.

Table 3.1: Details of Scientific Planning and Inputs in IWMP projects:

1	2	2
Sl.No.	Scientific criteria/ inputs used	No. of projects in which scientific criteria were used
A.	Planning	
	Cluster approach	3
	Whether technical back-stopping for the project has been arranged? If yes, mention the name of the Institute.	Yes, NESAC, Nongsder
	Baseline survey	Yes
	Hydro-geological survey	No
	Contour mapping	Yes
	Participatory Net Planning (PNP)	No

1	2	2
	Remote sensing data-especially soil/ crop/ run-off cover	Yes
	Ridge to Valley treatment	Yes
	Online IT connectivity between	
	(1) Project and DRDA cell/ZP	Yes
	(2) DRDA and SLNA	Yes
	(3) SLNA and DoLR	Yes
	Availability of GIS layers	
	1. Cadastral map	No
	2. Village boundaries	No
	3. Drainage	Yes
	4. Soil (Soil nutrient status)	Yes
	5. Land use	Yes
	6. Ground water status	No
	7. Watershed boundaries	Yes
	8. Activity	Yes
	Crop simulation models [#]	No
	Integrated coupled analyzer/ near infrared visible spectroscopy/ medium spectroscopy for high speed soil nutrient analysis	No
	Normalized difference vegetation index (NDVI)#	Yes
	Weather Stations	No
B.	Inputs	
	1. Bio-pesticides	No
	2. Organic manures	Yes
	3. Vermi-compost	Yes
	4. Bio-fertilizer	Yes
	5. Water saving devices	No
	6. Mechanized tools/ implements	No
	7. Bio-fencing	Yes
	8. Nutrient budgeting	Yes
	9. Automatic water level recorders & sediment samplers	No
	Any other (please specify)	-

3.2 Project Implementing Agency:

The PIA is the Soil & Water Conservation Territorial Division, Shillong, East Khasi Hills District of Meghalaya. The Project Manager will be the Divisional Soil and Water Conservation Officer and will be assisted by an Asst. Soil & Water Conservation Officer, Range officer along with WDT members in which expertise is drawn from the relevant fields for achieving smooth and successful implementation of the project.

1	2	3	
Names of Districts	Names of projects	Details of PIA	
East Khasi Hills	East Khasi Hills – IWMP VIII	(i) Type of organization#	Government
		(ii) Name of organization	Soil & Water Conservation (T) Division, Shillong
		(iii) Designation & Address	Divisional Soil & Water Conservation Officer, Polo, Shillong
		(iv) Telephone	0364 – 2591085
		(v) Fax	Do
		(vi) E-mail	Shgt.001@gmail.com

3.3 Institution Building

i) Watershed Committee (WC)

The Watershed Committee of Middle Umlew and Umprah, IWMP - VIII was constituted with the active involvement of the villagers with strong support of the Traditional Institutions (Village Durbar/Council). The two Watershed Committee of IWMP - VIII has been registered under the Meghalaya Societies Registration Act – 12. of 1983.



People's participate in the formation of Middle Umlew Watershed Committee at Jongksha village



People's participate in the formation of Umprah Watershed Committee at Laitkyrhong village

Table 3.2: Details of Watershed Committees (WC):

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18
Names of the Districts	Names of projects	Names of WCs	Date of Registration as a Society (dd/mm/yyyy)	Designation	M/F	SC	ST	SF	MF	LF	Land-less	UG	SHG	GP	Any other	Educational qualification	Function/s assigned#
East Khasi Hills District	East Khasi Hills District – IWMP – VIII	1.Umpra W/C 2.Middle Umlew W/C	11/03/2011	President	M	-	ST							2		Cl – X	A to I
				Secretary	M	-	ST								2	Graduate	A to I
			11/03/2011	Member	26M	-	ST				3	-	-	19		Cl – VI to Graduate	Do
				Member	8F	-	ST					-	4	4			Do
				Member													

- | | | | |
|----|--|----|--|
| A. | PNP and PRA | B. | Planning |
| C. | Maintenance of Accounts | D. | Signing of cheques and making payments |
| E. | Supervision of construction activities | F. | Cost Estimation |
| G. | Verification & Measurement | H. | Record of labour employed |
| I. | Social Audit | J. | Any other (please specify). |

ii) Self Help Group

Awareness programmes were organized in the villages to inform and sensitize the people on the essence of organizing themselves in to homogenous groups for uplifting their livelihood especially for the women and the landless. Discussions were held at length with the WDT on the scope and procedure of group formation, availing credit, grading of the groups and so on.

Table 3.3: Details of Self Help Groups (SHGs) in the project areas:

1	2	3				4				5			6		
Names of the Districts	Names of projects	Total no. of registered SHGs				No. of members				No. of SC/ST in each category			No. of BPL in each category		
		With only Men	With only Women	With both	Total	Categories	M	F	Total	M	F	Total	M	F	Total
East Khasi Hills	EKH. IWMP VIII	-	-	1 no	1 No	(i) Landless									
						(ii) SF									
						(iii) MF	20	10	22	20	10	22	NA	NA	NA
						(iv) LF									

iii) User Group

To manage the assets created and ensure their sustainability User Groups will be formed. The people have been sensitized on the importance of ensuring that the assets created are sustainably used and the essentiality of having User Groups for maintenance and operation of their assets.

Table 3.4: User Group Details

1	2	3				4				5			6		
Names of Districts	Names of Projects	Total no. of Ugs				No. of members				No. of SC/ST in each category			No. of BPL in each category		
		Men	Women	Both	Total	Categories	M	F	Total	M	F	Total	M	F	Total
East Khasi Hills	EKH. IWMP VIII					(i) Landless									
						(ii) SF									
						(iii) MF									
						(iv) LF									
Total		Nil	Nil	Nil	Nil				Nil			Nil			Nil

CHAPTER IV

PROJECT ACTIVITIES

CHAPTER IV PROJECT ACTIVITIES

4.1 Preparatory Phase:

i) Entry Point Activities (EPA)

(Financial – Rs. in lakh)

1	2	3	4	5	6	7	8	9	10	11
Sl. No	State	District	Names of Project	Amount earmarked for EPA	Entry Point Activities planned	Estimated cost	Expenditure incurred	Balance	Expected outcome	Actual outcome
1	Meghalaya	East Khasi Hills	East Khasi Hills – IWMP VIII	6.0 Lakhs	1.Construction of drinking water & washing platform 2. Construction of Check Dam cum washing Platform.	3.00 3.00	6.0	-	N.A	N.A

ii) Other activities of Preparatory Phase:

1	2	3	4	5	6	7	8	9	10	11	12	13
District	Name of Projects	Initiation of village level institution	Capacity building	IEC activities	Baseline survey	Hydro - geological survey	Identifying technical support agencies	Resource agreements	Preparation of DPR	Evaluation of DPR	Any other (please specify)	Cost incurred (Rs. In lakh)
East Khasi Hills	East Khasi Hills – IWMP VIII	2 nos. W/C	3 nos.	2 nos.	Participatory Rural Appraisals	N.A	Done	Done	Done	Done	Entry Point Activity	6.00



Check Dam cum Washing Platform at Laitkyrhong village



Check Dam cum Washing Platform at Laitlum village

4.2 Watershed Works Phase:

4.2.1 Activities related to surface water resources in the project areas:

1	2	3	4	5	6			7													
Sl No	Name of States	Name of District	Name of Projects	Type of structures	Pre Project			Proposed Project													
					No	Area irrigated (ha)	Storage capacity	Augmentation/ repair of existing structures				Construction of new structures				Total target					
								No	Area to be treated (ha)	Storage capacity	Estimated cost (in lakhs)	No	Area to be treated (ha)	Storage capacity (per unit)	Estimated cost (in lakhs)	No	Area to be treated (ha)	Storage capacity (m³)	Estimated cost		
1	Meghalaya	East Khasi Hills	East Khasi Hills – IWM P VIII	(i) Tank	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
(ii) Pond				-	-	-	-	-	-	-	42 nos.	138.00 Ha	2000 m³	9.744	42 nos.	138.00 Ha	84000	9.744			
(iii) Lake				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			
(iv) Check Dam				-	-	-	-	-	-	-	16 nos.	50 Ha	3000 m³	4.784	8 nos.	50 Ha	48000	4.784			
(v) Protection wall				-	-	-	-	-	-	-	30 nos.	60 ha	-	6.849	30 nos.	60 ha	-	6.849			
(vi) Channel				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
(vii) Any others (please specify)																					
Total										-.	-	-	-	88 nos.	248 Ha	5000 m³	21.377	67 nos.	248 Ha	132000	21.377

8											9	10
Achievement due to project												
Augmentation/ repair of existing structures				Construction of new structures				Total achievement			Change in storage capacity (col 8-6)	Change in irrigated area (ha) Col. (8-6)
No	Area irrigated (ha)	Storage capacity	Expenditure incurred (in lakhs)	No	Area irrigated (ha)	Storage capacity	Expenditure incurred (in lakhs)	Area irrigated (ha)	Storage capacity	Estimated incurred		-
-	-	-	-	-	-	-	-	-	-	-	-	-
-	-	-	-	42 nos.	138.00 Ha	2000 m ³	9.744	138.00 Ha	84000 m ³	9.749	84000 m ³	138.00 Ha
-	-	-	-	-	-	-	-	-	-	-	-	-
-	-	-	-	16 nos.	50 Ha	3000 m ³	4.784	50 Ha	48000 m ³	4.784	48000 m ³	50 Ha
				30 nos.	60 Ha	-	6.849	60 ha	-	6.849	-	60 Ha
-	-	-	-	88nos.	248 Ha	5000 m³	21.377	248 Ha	132000 m³	21.377	132000 m³	248 Ha

4.2.2 Activities related to recharging ground water resources in the project areas:

1	2	3	4	5	6		7							8							9		
Sl. No.	Names of States	Names of Districts	Names of projects	Type of structures	Pre-project		Proposed target							Achievement due to project							Change in irrigated area (Col. 8-6) (ha)		
					No.	Area Irrigated (ha)	Augmentation/ repair of existing recharging structures			Construction of new recharging structures			Total target		Augmentation/ repair of existing recharging structures			Construction of new recharging structures				Total achievement	
							No.	Area to be irrigated (ha)	Estimated cost	No	Area to be irrigated (ha)	Estimated cost	Area to be irrigated (ha)	Estimated cost	No	Area irrigated (ha)	Expenditure incurred	No	Area irrigated (ha)	Expenditure incurred		Area irrigated (ha)	Expenditure incurred
	Meghalaya	E.K.H	East Khasi Hills – IWMP VIII	(i)Open wells		Nil		Nil			Nil				Nil			Nil					
				(ii)Bore wells																			
				(iii)Any others (Pl. specify)																			
				Total for the project																			

4.2.3 Activities executed by User Groups in the Project Areas.

1	2	3						
Names of Districts	Names of Projects	Major activities of the UGs –Targets				No. of UGs involved	Estimate d Cost	Amount of WDF to be collected (Rs.)
		Structure/ activity proposed						
		Sl. No.	Type	No.#	Treatment (ha)			
East Khasi Hills	East Khasi Hills – IWMP - VIII		NIL	NIL	-	-	-	-

4.2.4 Activities executed by User Groups in the Project Areas:

4									
Major activities of the UGs – Achievements									
Structure/ activity				No. of UGs involved	Expenditure incurred (Rs.)	No. of mandays			Amount of WDF collected (Rs.)
Sl. No.	Type	No.#	Treated Area (ha.)			SC	ST	F	
1.	Nil	Nil	-	-	-	-	-	-	-
2.									

4.2.5 Activities related to livelihoods by Self Help Groups (SHGs) in the project areas:

1	2	3		
Names of the Districts	Names of projects	Major activities of the SHGs		
		Name of activity	No. of SHGs involved	Average annual income from activity per SHG
East Khasi Hills	East Khasi Hills – IWMP - VIII	1. Pisciculture	6 nos.	180000
		2. Stabilized Mud Block	3 nos.	60000
		3. Piggery Farming	34 nos.	1020000
		4. Grocery Shop	10 nos.	300000
		5. Canes & Handicraft	14 nos.	50000
		6.Processing unit/Rice mill	2 unit	100000
				19.50

4.2.6 Activities related to livelihoods by Self Help Groups (SHGs) in the project areas:

4	5				6	7	8			9	10
No. of SHGs given training	Total assistance received by the SHG (Amount in Rs.)				Total annual Income generated (Rs.)	Total annual Savings (Rs.)	No. of SHGs Graded as			Total Amount of loan sanctioned by the bank(s)	No. of SHGs federated
	Loan from revolving fund	Training	Material	Others (pl. specify)			I	II	III		
-	-	-	-	-	-	-	-	-	-	-	-
-	-	-	-	-	-	-	-	-	-	-	-
-	-	-	-	-	-	-	-	-	-	-	-

4.2.7 Other activities of watershed works phase:

1	2	3		4		5		6		7		8		9		10		11		12		13
District	Names of projects	Ridge area treatment		Drainage line treatment		Nursery raising		Land development		Crop demonstrations		Pasture development		Veterinary services		Fishery development		Non-conventional energy		Any other (please specify)		Total cost incurred (Rs. In lakhs)
		(a)	(b)	(a)	(b)	(a)	(b)	(a)	(b)	(a)	(b)	(a)	(b)	(a)	(b)	(a)	(b)	(a)	(b)	(a)	(b)	
EKH	IWMP -VIII	560 ha	34.21	248 ha	21.377	-	-	192 ha	19.413	-	2.50	-	-	-	18.2	-	1.8	-	-	-	12.00	109.50

4.2.8 Details of engineering structures in watershed works:

1	2	3	4			5			6	7				8								
District	Project	Name of structures	Type of treatment			Type of land			Executing agency	Target				Achievement								
			(i) Ridge area (R)	(ii) Drain age line (D)	(iii) Land Dev. (L)	(i) Private	(ii) Com-munity	(iii) Others pl.specify)	(i) UG (ii)SHG (iii) Others (pl. specify)	No. of units (No./ cum./ rmt)	Estimated cost (Rs. in lakh)				Expected month & year of completion (mm/yyyy)	No. of units (No./ cu.m./ rmt)	Expenditure incurred (Rs. in lakh)				Status of comple-tion	Actual month & year of completion (mm/yyyy)
											M	W	O	T			M	W	O	T		
		Staggered trenching																				
		Contour bund		-	148 ha	Private	-	-	Beneficiary	148 Ha				11.10	3 yrs	-	-	-	-	-	-	-
		Graded bunding																				
		Bench terracing			24 ha				Beneficiary	24 ha				4.80	2 yrs							
		Check dam		50 ha					Beneficiary	50ha				4.784	1 yr							
		Water Harvesting		138ha						138 ha				9.744	3 yrs							
		Gully plug																				
		Protection wall		60 ha						60 ha				6.849	1 yrs							
		Underground dykes																				
		Field bunds			7027 Rm/20 ha	Private			Beneficiary	7027 Rm/20 ha				3.513	3 yrs							
		Any others (pl. specify)																				

Contd.

4.2.9 Details of engineering structures in watershed works.

9																	
Outcomes																	
Reduction in run off (cu.m)	Area treated# (ha)	Water level (m)		Production (quintal)		Income (Rs.)		Mandays generated					No. of beneficiaries				
		Pre- project	Post project	Pre- project	Post project	Pre- project	Post project	SC	ST	Others (Men)	Women	Total	SC	ST	Others	Women	Total
Na	440 ha	Na	-	Na	-	Na	-	-	24473	14683	9790	24473	-	895	446	449	895

4.2.10 Details of activities connected with vegetative cover in watershed works:

1	2	3	4			5			6	7				8			
District	Project	Name of structure/ work	Type of treatment			Type of land			Executing agency	Target				Achievement			
			(i) Ridge area (R)	(ii) Drainage line (D)	(iii) Land dev. (L)	(i) Private	(ii) Community	(iii) Others (pl. specify)	(i) UG (ii) SHG (iii) Others (pl. specify)	Area (ha)	No. of plants	Estimated cost (Rs. in lakh)	Expected month & year of completion (mm/ yyyy)	Area (ha)	No. of plants	Expenditure incurred (Rs. in lakh)	Actual month & year of completion (mm/ yyyy)
		Afforestation															
		Regeneration				✓				360 ha		12.96	3 yrs	-	-	-	-
		Agro-forestry					✓			100 ha		10.10	3yrs	-	-	-	-
		Fuel wood															
		Fodder															
		Agro-Horticulture				✓				100 ha		11.150	3 yrs	-	-	-	-
		Pasture dev.															
		Nursery raising															
		Others (Coffee)				✓								-	-	-	-

in case two or more activities are executed over same area, the figures in area treated should be accounted only once and should reflect only the actual watershed area treated.

4.2.11 Details of vegetative structures in watershed works: Phase – II (contd.):

9														
Outcomes														
Reduction in run off (cu.m)	Production (quintal)		Income (Rs.)		Mandays generated					No. of beneficiaries				
	Pre- project	Post project	Pre- project	Post project	SC	ST	Others	Women	Total	SC	ST	Others	Women	Total

4.2.12 Details of allied / other activities:

1	2	3	4			5	6		7	
District	Project	Name of activity@	Type of land			Executing agency	Target		Achievement	
			(i) Private	(ii) Community	(iii) Others (landless)		Estimate d cost (Rs. in lakh)	Expected month & year of completion (mm/yyyy)	Expendi- ture incurred (Rs. in lakh)	Actual month & year of completion (mm/yyyy)
East Khasi Hills	IWMP VIII	Tailoring	-	-	30 units	SHG's/Individual	2.40	3 yrs.		
		Carpentry/ Basket making etc –	-	-	4 units	SHG's Individual	0.20	3 yrs.	-	-
		Bee keeping/Apiculture	-	-	20 units	Do	1.60	3 yrs.	-	-
		Backyard poultry/Piggery etc	-	-	100 units	Do	8.00	3 yrs.	-	-
		Stabilized Mud Block	-	-	6 units	SHG's	0.30	3 yrs.	-	-
		Piggery Farming	-	-	34 units	SHG's Individual	10.20	3 yrs.	-	-
		Handicraft/Basket making	-	-	14 units	SHG's Individual	3.50	3 yrs.	-	-
		Kitchen gardening	-	-	100 units	Individual	2.50	3 yrs.	-	-
		Grocery Shop	-	-	10 units	SHG's	3.00	2 yrs.	-	-
		Pisciculture	-	-	6 units	SHG's Individual	1.80	2 yrs.	-	-
		Processing unit/ Rice mill	-	-	2 units	SHG's	1.00	1 yrs.	-	-
		.								

(Contd.)

* from column no. 2, no. of States; from column no. 3, no. of Districts; from column no. 4, total no. of Projects; from column no. 5, activity-wise totals, from column no. 6, type-wise totals, from column no. 7, agency-wise totals, from column no. 8, total estimated cost, from column no. 9, total expenditure incurred, structure-wise no. of completed works, from column no. 10, item-wise totals, for the entire country may be indicated at the end of the table

@The activities given in this column are merely indicative and States are free to choose any other activity suited to the project area.

4.2.13 Details of allied / other activities:

8											
Outcomes											
Income (Rs.)		Mandays generated					No. of beneficiaries				
Pre-project	Post project	SC	S T	Others	Women	Total	SC	ST	Others	Women	Total

4.3 Consolidation and withdrawal phase

Details of activities in the CPRs in the project areas:

1	2	3	4	5	6				7						
Names of the Districts	Names of projects	Name(s) of the villages	CPR particulars	Activity proposed	Target				Achievement						
					Target area under the activity (ha)	Estimated expenditure (Rs.)	Expected no. of beneficiaries	Estimated contribution to WDF (Rs.)	Area treated under the activity (ha)	Expenditure incurred (Rs.)	Actual no. of beneficiaries	No. of mandays			WDF collected (Rs.)
												SC	ST	F	
East Khasi Hills	IWMP-VIII	Jongksha	D/Well	Repairing of drinking well	-	1.50	80	7500							
			Washing Platform	Repairing of W/platform		1.00	75	7500							
		Laitkyrhong	C/ dam cum Washing platform	Repairing of C/dam cum washing platform	-	0.875	60	3750							
			Washing Platform	Repairing of washing platform		1.00	34	3750							
		Laitlum	Drinking well	Repairing of drinking well	-	0.50	27	2500							
		TOTAL				5.00		25,000							

CHAPTER V
PROJECT PHASING & BUDGETING

CHAPTER V

PROJECT PHASING & BUDGET

ACTION PLAN OF MIDDLE UMLEW AND UMPRAH WATERSHED IWMP – 2010 – 2011 PROJECT – VIII.

Name of District: East Khasi Hills

No. of villages – 3 nos.

Name of C&RD Block: - Mawkynrew

Project Area – 1000 Ha.

Sl. No	Activities	I st Year		II nd Year		III rd Year		IV th Year		V th Year		Total	
		Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin
1	2	3	4	5	6	7	8	9	10	11	12	13	14
I	MANAGEMENT COST:												
A.	Administrative cost:	-	-	2%	3.00	5%	7.5	3%	4.5	-	-	10%	15.00
			-	Months		months		months		-			
i.	Honourarium of WDT Members @ ` 5000/ month – 1 no.	-		12	0.60	12	0.60	12	0.60	-		3 yrs	1.80
ii.	Hon ^{rm} of Watershed Volunteers @ ` 2500/- month – 2 nos.	-	-	12	0.60	12	0.60	12	0.60	-	-	3 yrs	1.80
iii.	Hon ^{rm} WCO's @ ` 750/ month.	-	-	12	0.09	12	0.09	12	0.09	-	-	3 yrs	0.27
iv.	Hon ^{rm} WCM @ ` 100/members/ month for 25 nos.	-	-	12	0.30	12	0.30	12	0.30	-	-	3 yrs	0.90
v	Hon ^{rm} Office assistance @ ` 5000/- month.	-	-	12	0.60	12	0.60	12	0.60	-	-	3 yrs	1.80
vi	Hon ^{rm} Chartered Accountant	-	-	1.00	0.15	1.00	0.15	1.00	0.15	-	-	3 yrs	0.45
vii	TA/DA of Field Asstt. @ ` 5000/ month	-	-	6.00	0.3	12	0.60	12	0.60	-	-	2.5 yrs	1.50
viii	Hiring charges of office building @ ` 1000	-	-	12	0.12	12	0.12	12	0.12	-	-	3 yrs	0.36
ix.	Hiring charges of vehicle @ ` 5000/ month	-	-	1.00	0.05	12	0.60	12	0.60	-	-	2.5 yrs	1.25
x	Office expenses, POL, Stationeries, printing of SHG's books, pamphlets, tea, snacks etc, cost of camera.	-	-	-	0.19	-	3.84	-	0.84	-	-	-	4.87
	Total of A:	-		2.00%	3.00	5.00%	7.50	3.00%	4.50	0.00%	-	10.00%	15.00

	PREPARATORY PHASE :												
B.	Entry Point Activities:	4%	6.00	-	-	-	-	-	-	-	-	4%	6.00
i.	Construction of Water Tank cum bathroom & Washing place	5 units	6.00	-	-	-	-	-	-	-	-	5 units	6.00
	Total of B:	4%	6.00			-		-		-	-	4%	6.00
C.	Training:	1%	1.50	2%	3.00	1%	1.50	1%	1.50	-	-	5%	7.50
i.	Awareness Campaign & Capacity building	1 no	0.60	-		-						1 no	0.60
ii.	Exposure visits – off. Campus			2 nos	0.60	-		1 no.	0.30	-		3 nos	0.90
iii.	Capacity building of SHG's/ UG's.	2 nos.	0.30	7 nos.	1.00	4 nos.	1.00	2 nos.	0.60	-	-	15 nos.	2.90
iv.	Capacity building of WC Members.	2 nos.	0.30	4 nos.	0.75	1no.	0.25	1 no.	0.30	-	-	8 nos.	1.60
v.	Capacity of WDT/WV	2 nos.	0.30	4 nos.	0.65	1 no.	0.25	1 no.	0.30	-	-	8 nos.	1.50
	Total of C:	1.00%	1.50	2.00%	3.00	1.00%	1.50	1.00%	1.50	-	-	5.00%	7.50
D.	Detailed Project Report:	1%	1.50			-	-	-	-	-	-	1%	1.50
i.	Cost of Resources Inventories works	-	0.25	-	-	-	-	-	-	-	-	-	0.25
ii.	Cost of PRA Exercises	-	0.50	-	-	-	-	-	-	-	-	-	0.50
iii.	Cost of Land use Survey works	-	0.25	-	-	-	-	-	-	-	-	-	0.25
iv.	Cost of formulating	-	0.50	-	-	-	-	-	-	-	-	-	0.50
	Total of D:	1%	1.50			-		-		-	-	1%	1.50
E.	Monitoring & Evaluation:(internal monitoring and social audit)									-	-	2%	3.00
i	Monitoring			0.20%	0.30	0.50%	0.75	0.3%	0.45			1%	1.50
ii	Evaluation	-	-	0.30%	0.45	0.50%	0.75	0.20%	0.30	-	-	1%	1.50
	Total of E:			0.50%	0.75	1.00%	1.50	0.50%	0.75	-	-	2.00%	3.00
	Total of I (A to E)	6.00%	9.00	4.50%	6.75	7.00%	10.50	4.50%	6.75	-	-	22.00%	33.00

II	PROJECT COST/WATERSHED WORKS PHASE :												
A.	Arable Land Treatment:												
i.	Bench Terrace @ ` 20000/ ha for 24 ha	-	-	8 Ha	1.60	16 Ha	3.20	-	-	-	-	24 Ha	4.80
ii	Contour Bunds @ ` 7500/ha for 148 ha	-	-	16 Ha	1.20	120 Ha	9.00	12 Ha	0.90			148 Ha	11.10
iii.	Agro-Horticulture(temperate plum)@ `11150/ ha for 100 ha	-	-	100 Ha	1.10	100 Ha	7.68	160 Ha	2.37	-	-	160 Ha	11.15
	Total of A :	-	-	-	3.90	-	19.88	-	3.27	-	-	-	27.05
B.	Non- Arable Land Treatment:									-	-		
i.	Afforestation 100 Ha @ ` 10,100	-	-	100 Ha	1.70	100 Ha	5.51	100	2.89	-	-	80 Ha	10.10
ii	Improvement of existing Degraded Forest 360 ha @ `3600/-	-	-	360 Ha	5.32	360 Ha	5.32	110 Ha	2.32	-	-	110 Ha	12.960
iii	Peripheral bunding @ ` 50/Rm 7027 m			656 Rm	0.328	6005 Rm	3.0025	366 Rm	0.183	-	-	7027 Rm	3.513
	Total of B:	-	-	-	7.348	-	13.833	-	5.393	-	-	-	26.573
C	Drainage Line Treatment:									-	-		
i.	Water Harvesting Structures -18 nos BA-78ha	-	-	-	-	12 Ha	3.936	6.00	1.968	-	-	18 Ha	5.904
ii.	Check Dam, 16 Nos BA-50 ha	-	-	-	-	15 Ha	4.485	1.00	0.299	-	-	16 Ha	4.784
iii	Protection wall - 30 Nos BA - 60ha	-	-	-	-	30 Ha	6.849	-	-	-	-	30 Ha	6.849
iv	Dug out Pond @ ` 16000/unit for 24 units BA-60 ha	-	-	-	-	22 Ha	3.52	2.00	0.32	-	-	24 Ha	3.84
	Total of C :	-	-	-	-	-	18.79	-	2.587	-	-	-	21.377
	Total of A + B + C	-	-	7.50%	11.25	35.00%	52.50	7.50%	11.25	-	-	50.00%	75.00

D	Livelihood Activities for landless persons:												
i.	Tailoring @ ` 8,000	-	-	4 units	0.32	10 units	0.800	16 units	1.28	-	-	30 units	2.40
ii.	Carpentry/ @ ` 5000	-	-	-	-	2 units	0.100	2 units	0.10			4 units	0.20
iii	Apiculture @ ` 8000	-	-	-	-	-	-	20 units	1.60	-	-	20 units	1.60
iv	Masonry/ Hallow block making @ ` 5000/-	-	-	-	-	-	-	6 units	0.30	-	-	6 units	0.30
v	Poultry / Piggery @ ` 8,000/-			6 units	0.48	34 units	2.720	60 units	4.80	-	-	100 units	8.00
vi	Kitchen Gardening @ ` 2500/-			28 units	0.70	35 units	0.875	37 units	0.93	-	-	100 units	2.50
	Total of D:	-	-	1.00%	1.50	3.00%	4.50	6.00%	9.01	-	-	10.0%	15.0
E.	Production System and Micro Enterprises (SHG's):	- -											
i.	Processing unit/rice mill @ ` 50,000/-	-	-	-	-	2 units	1.00	-	-	-	-	2 units	1.00
ii	Pisciculture @ ` 30,000/	-	-	-	-	4 units	1.20	2 units	0.6	-	-	6 units	1.80
iii	Piggery / Poultry @ ` 30,000/	-	-	-	-	10 units	3.00	24 units	7.2	-	-	34 units	10.20
iv	Canes & Handicrafts @ ` . 25,000/	-	-	6 units	1.50	2 units	0.50	6 units	1.5	-	-	14 units	3.50
v	Grocery shop @ ` 30,000/-	-	-	-	-	6 units	1.80	4 units	1.2	-	-	10 units	3.00
	Total of E :			1.00%	1.50	5.00%	7.50	7.00%	10.5			13.00%	19.50
F.	Consolidation & Exit Phase:												
i.	Repairs, Maintenance of CPR's.	-	-	-	-	-	-	-	-	-	3.00	-	3.00
ii.	Improving the sustainability of various Interventions	-	-	-	-	-	-	-	-	-	2.00	-	2.00
iii.	Documentation of successful experiences & Preparation of Completion Report	-	-	-	-	-	-	-	-	-	2.50	-	2.50
	Total of F:	-	-	-		-	-	-	-	-	7.50	-	7.50
	Total of II (A+B+C+D+E+F)			9.50%	14.25	43.0%	64.50	20.50%	30.750	5%	7.50	78.00%	117.00
	Grand Total (I + II)	6%	9.00	14%	21.00	50%	75.00	25.0%	37.50	5%	7.50	100%	150.0

VILLAGE WISE ACTION PLAN OF PROJECT – VIII, IWMP (2010-11)
TERRITORIAL DIVISION: SHILLONG.

Name of District: East Khasi Hills

No. of Villages – 3 nos.

Name of C & RD Block : Mawkyntew C & RD Block

Project Area - 1000 Ha

Sl. No	Activities		JONGKSHA		LAITKYRHONG		LAITLUM		Total	
			Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin
1	2		3	4	5	6	7	8	9	10
I	WATERSHED WORKS PHASE :	-							-	-
i.	Bench Terrace @ ` 20,000/ ha for 24 ha	-	12ha	2.40	9 ha	1.80	3ha	0.60	24 ha	4.800
ii	Contour Bunds @ ` 7500/ ha for 148 ha	-	74 ha	5.55	52 ha	3.9	22 ha	1.65	148 ha	11.100
iii.	Agro-Horticulture(temperate plum) @ ` 11150 for 100 Ha	-	50 ha	5.575	35 ha	3.9025	15 ha	1.6725	100 ha	11.150
	TOTAL OF "A"		136Ha	13.525	96Ha	9.6025	40Ha	3.9225	272Ha	27.05
B.	Non- Arable Land Treatment:	-								
i.	Agro-Forestry Devt. works @ ` 10,100/ ha for 100 ha (IWMP)	-	50 ha	5.05	35 ha	3.535	15 ha	1.515	100 ha	10.100
	(NREGA)	-				10.2				
	TOTAL	-				13.735				
ii	Improvement of existing Degraded Forest @ ` 3600/ ha for 360 ha	-	180 ha	6.48	126 ha	4.536	54 ha	1.944	360 ha	12.960
iii.	Peripheral Bunding @ ` 50/Rm for		3512Rm/10ha	1.756	2500 Rm /7ha	1.25	1015 Rm /3ha	0.506	7027 Rm /20ha	3.513
	TOTAL OF "B"	-	240Ha	13.286	168Ha	9.321	72Ha	3.965	480Ha	26.573
C	Drainage Line Treatment:	-								
i.	Water Harvesting Structures-BA 78 Ha (IWMP)	-	9 nos./38 ha	2.952	6nos./30 ha	1.968	3nos./10 ha	0.984	18nos./78 ha	5.904
	(NREGA)	-				3.444				
	TOTAL	-				5.412				
ii.	Check dam – BA 50 ha IWMP		8nos./24 ha	2.392	6 nos/16 ha	1.794	2nos./10 ha	0.598	16nos./50 ha	4.784
iii.	Protection Wall (505 Rm)- BA 60 Ha	-	15nos./30 ha	3.4245	10nos./35 ha	2.283	5nos./5 ha	1.1415	30nos./60ha	6.849
	Dug-out Pond @ ` 16,000/unit 60 Ha	-	12nos/30 ha	1.92	8 nos./20 ha	1.28	4 nos./10 ha	0.64	24 nos./60 ha	3.840
	TOTAL OF "C"	-	122Ha	10.689	91Ha	7.325	35Ha	3.364	248Ha	21.377
	Total of benefitted area	-	498Ha		355Ha		147Ha		1000Ha	
	Total of I:	-		37.50		26.2485		11.2515	50%	75.00

1	2		3	4	5	6	7	8	9	10
II.	Livelihood Activities for landless persons :(10%)									
i.	Tailoring @ ` 8,000/- (30)	-	15 units	1.20	11 units	0.88	4 units	0.32	30 units	2.40
ii.	Carpentry/ Agri- Implements/ Basket Making etc @ ` 5000/- (20)	-	2 units	0.10	1 units	0.05	1 units	0.05	4 units	0.20
iii.	Piggery/Poultry @ ` 8000/ unit (90)	-	50 units	4.00	35 units	2.80	15 units	1.20	100 units	8.00
iv.	Apiculture @ ` 8000/- (20)	-	10 units	0.80	7 units	0.56	3 units	0.24	20 units	1.60
v.	Kitchen Gardening @ ` 2500/- (102)	-	50 units	1.25	35 units	0.875	15 units	0.38	100 units	2.50
vi	Masonry / Hollow block making @ ` 5,000/ (10)		3 units	0.15	2 units	0.1	1 units	0.05	6 units	0.30
	Total of II.	-		7.50		5.25		2.25	10%	15.00
III.	Production System and Micro Enterprises (SHG's):	-								
i.	Processing unit/rice mill @ ` 50,000/-	-	1 units	0.50	1 units	0.50	-	-	2 units	1.00
ii	Pisciculture @ ` 30,000/	-	3 units	0.90	2 units	0.60	1 units	0.30	6 units	1.80
vi	Piggery / poultry @ ` 30,000/	-	17 units	5.10	12 units	3.60	5 units	1.50	34 units	10.20
vii	Grocery shop @ ` 30,000/		5 units	1.50	4 units	1.20	1 units	0.30	10 units	3.00
viii	Canes & Handicrafts @ ` 25,000/ unit	-	7 units	1.75	5 units	1.25	2 units	0.50	14 units	3.50
	Total of III:	-		9.75		7.15		2.60	13.00%	19.50
	Grand Total (I+II+111) -IWMP	-		54.75		38.65		16.10	73.00%	109.50
	TOTAL (NREGA)									13.64

Details of the types of areas covered under the IWMP Programme:

1	2	3	4	5	6		7	8	9	10				11				
Sl No	Name of State	Name of Districts	Names of Projects	Year of sanction	Project duration (dd/mm/yyyy)		Area of the projects	Project cost (Rs. In lakh)	Names of Micro watersheds & Code nos. (as per DoLR's unique codification)	Area (ha) of the projects				Area details (ha) (falling within the projects)				
					From	To												
										Cultivated rainfed area	Cultivated irrigated area	Uncultivated wasteland		Pvt. Agri. Land	Forest land	Comm unity land	Others (pl. specify)	Total area (ha)
												a) Tempora ry fallow	b) Per manent					
1	Meghalaya	East Khasi Hills	East Khasi Hills IWMP VIII	2010 - 2011	2010 - 2011	2014 - 2015	1000 Ha	150 Lakhs	Middle Umlew & Umprah Watershed	60 Ha	Nil	616	378	60	153	576	645	1434 ha

Fund provision for the IWMP projects from all sources:

1	2	3		4										5
District	Name of Projects	IWMP Fund		Funds from other sources in addition to IWMP funds										Total
				Convergence funds		PPP		Community		Institutional finance		Others (Pl. specify)		
		Central Share	State Share	Name of Scheme	Amount (Lakhs)	Name of private sector	Financial contribution	Name	Financial contribution	Name	Financial contribution	Name	Financial contribution	
East Khasi Hills	East Khasi Hills – IWMP VIII	135 lakhs	15 lakhs	NREGS	13.644	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	163.64

Details of Project Fund Accounts of Distt. Agency and Watershed Committees:

1	2	3	4	5				6				
Sl. No.	Names of States	Name of Districts	Names of Projects	Distt. Agency's Project Account details				Watershed Committee (WC) account details:				
				Name of the Bank and Branch where project account has been opened	Account Number (to be obtained confidentially)	Account type (Savings/ Current/ Others)	Name & Designation of authorized persons who operate the account.	Name of Watershed Committee	Name of the Bank and Branch where project account has been opened	Account number (to be obtained confidentially)	Account type (Savings/ current others)	Name & Designation of authorized persons who operate the account.
1	Megha laya	East Khasi Hills	East Khasi Hills – IWMP VIII	State Bank of India, Polo Branch	31641749416	Saving	Shri A.S Kharlukhi, DS&WCO	i) Middle Umlew, Watershed Committee ii) Umprah Watershed Committee	Meghalaya Co-operative Apex Bank, Smit Branch - do -	0.743 0.744	Saving	Chairman W.C, Secretary W.C, Project Leader / WDT

Details of Convergence of IWMP with other Schemes:

	1	2	3	4	5	6	7
Sl. No.	District	Names of projects	Names of Departments with Schemes converging with IWMP	Fund made available to IWMP due to convergence (Rs. in lakh)	Name of activity/task/structure undertaken with converged funds	Reference no. of activity/ task/ structure in DPR@	Level at which decision for convergence was taken\$
					(a) Structures (b) livelihoods (c) Any other (pl. specify)#		
1	East Khasi Hills	East Khasi Hills – IWMP VIII	* Community Rural Development Department NREGS	13.644	i) Construction of water Harvesting structure ii) Afforestation	-	Block Level & District Level
2				n.a		-	

TO WHOM IT MAY CONCERN

This is to certify that a decision has been taken in principle to converge the IWMP projects proposed by the Divisional Officer, Soil & Water Conservation, Shillong (T) Division, Shillong with MGNREGS.




Deputy Commissioner
&
District Programme Co-Ordinator(MGNREGS)
East Khasi Hills District
Shillong

Public-Private Partnership in the IWMP projects: NIL

1	2	3	4			5		6	7	8	9
District	Name of project	Name of Private Sector Partner Agency	Type of agreement signed			Financial contribution		Partnership Interventions	Expected Outcomes	Actual Outcomes	Comments
			a)MoU	b)Contract	c) Any other (pl. specify)	IWMP	Private sector				

* from Column no. 2, total no. of States implementing the programme, from Column no. 3, total no. of Districts; from Column no. 4, total no. of projects under PPP; from Column no. 5, total no. of private companies/ agencies, from column no. 7, total amounts may be mentioned at the end of the table for the entire country.

CHAPTER VI

CAPACITY BUILDING

CHAPTER VI CAPACITY BUILDING

Capacity Building is a process to systematically upgrade the skill of individuals or groups for achieving a specific target. Capacity building in the project has been planned for all the stake holders involved i.e. State Level, District Level, Project Level and Village Level. The relevant details pertaining to Capacity Building has been shown below.

Table 6.1: List of approved Training Institutes for Capacity Building:

1	2	3	4	5	6	7	8	9				
S. No	State	Name of the Training Institute	Full Address with contact no., website & e-mail	Name & Designation of the Head of Institute	Type of Institute [#]	Area(s) of specialization ^{\$}	Accreditation details	Performance				
								Reference Year	No. of trainings assigned	No. of trainees to be trained	No. of trainings conducted	No. of trainees trained
1	Meghalaya	NIRD (NER)	Guwahati	Director	Central Govt.	Remote Sensing, Rural Devt.	NA	-				
2		SIRD	Nongsder	Director	State Govt.	Capacity Building	NA	-				
3		RRTC	Umran	Director	Don-Bosco	Agri-Horti, Animal Husbandry, Entrepreneurship	NA					
4		ICAR	Umiam	Director	Central Govt.	Do	NA					
5		VTC	Kyrdem Kulai	Director	State Govt.	Animal Husbandry	NA					
6		Fruit Garden	Shillong	Director	State Govt.	Agri-Horti, Fruit Processing	NA					

- From Column no. 2, total no. of States implementing the programme, from Column no. 3, no. of training institutes, from column No. 9, total no. of category-wise trainings and trainees may be given at the end of the table for the entire country

- [#] Central govt. Dept./ State govt. Dept./ Autonomous Body/ Research Institutes/ Universities/ Others (pl. specify)

^{\$} Capacity Building/ Agriculture/ Horticulture/ Animal Husbandry/ Pisciculture/ Remote Sensing/ Water conservation/ Ground water/ Forestry/ livelihoods/ entrepreneurship development/ others (pl. specify)

[@] The training institutes must fulfill the conditions mentioned in the operations guidelines.

- (i) Technical experts in fields required by IWMP
- (ii) Past experiences
- (iii) Annual Turnover
- (iv) Receives funds either from the Central or State Government
- (v) Publications
- (vi) Not blacklisted by any Govt. organizations
- (vii) Audited accounts
- (viii) Organizational structure

Table 6.2: Capacity Building activities for the year 2010 – 11 as on 31/03/2011(dd/mm/yyyy)*

1	2	3	4	5	6		7	
Project Stakeholders	Total no. of persons	No. of persons trained so far	No. of persons to be trained during current financial year	No. of persons trained during current financial year	Sources of funding for training		Funds utilized (Lakhs)	
					a) DoLR	b) Any other (Pl. specify)	a) DoLR	b) Any other (Pl. specify)
SLNA			400 Nos.	-	1.50	-	1.50	-
DRDA/ZP cell			-	-				
PIAs			25 Nos.	-				
WDTs			120 Nos.	-				
UGs			20 Nos.	-				
SHGs			30 Nos.	-				
WCs			16 Nos.	-				
GPs			15 Nos.	-				
Community			250 Nos.	-				
Others Pl. specify)								



Peoples taking in PRA exercise at Jongksha village under Middle Umlew Watershed.



Peoples taking part in drawing the Resource map at Laitkyrhong Village under Umprah Watershed.

Table 6.3: Information, Education & Communication (IEC) activities for the year 2010 - 11 as on 31/03/11 (dd/mm/yyyy)*

	1	2	3	4	5
	Activity	Executing agency	Estimated expenditure (Rs.)	Expenditure incurred (Rs.)	Outcome (may quantity, wherever possible)
1.	Awareness	S&WC (T) Division	0.50	0.50	
2.	Capacity Building	S&WC (T) Division	1.00	1.00	

CHAPTER VII
EXPECTED OUTCOME

CHAPTER VII

EXPECTED OUTCOME

Table 7.1 Employment related outcomes:

Sl No	Name of Village	1										2				
		Wage employment										Self employment				
		No. of mandays					No. of beneficiaries					No. of beneficiaries				
		SC	ST	Others	Women	Total	SC	ST	Others	Women	Total	SC	ST	Others	Women	Total
1.	Jongksha	-	27000	10920	16380	27300	-	450	200	300	450	-	40	20	20	40
2.	Laitkyrhong	-	18300	7320	10980	18300	-	309	234	75	309	-	68	23	45	68
3.	Laitlum	-	7560	3024	4536	7560	-	71	46	25	71	-	22	7	15	22
	TOTAL		53160	21264	31896	53160	-	830	480	400	830	-	130	50	80	130

Table 7.2 Migration Details:

1	2	3	4	5	6	7	8	9	10	
Names of the Districts	Names of Projects	Name of village	No. of persons migrating	No. of days per year of migration	Major reason(s) for migrating	Distance of destination of migration from the village (km)	Occupation during migration	Income from such occupation (Rs. in lakh)	For reduced migration identify major activities of IWMP responsible	
									(a) Structures	(b) Livelihoods
				N	I	L				

* From column no. 2, total number of States; from column no. 3, total no. of Districts; from column no. 4, total no. of projects; from column no. 5, total no. of villages; from column no. 6, total no. of persons migrating; from column no. 7, average no. of days for annual migration; from column no. 9, average distance of migration from the village and from column no. 11, average income from occupation during migration, for the entire country may be given at the end of the Table.

Table 7.3 Economic benefits accrued to women:

1		2		3		4
Wages		Training		Livelihoods		Total (Rs. in lakh)
Woman days	Amount (Rs. in lakh)	No. of women participants	Amount (Rs. in lakh)	No. of women beneficiaries	Value of assistance provided (Rs. in lakh)	
31896	31.896	400	0.60	80 nos.	8.00	8.60

* from Column no. 2, total no. of States implementing the programme, from Column no. 3 to 6, category-wise totals, may be mentioned at the end of the table for the entire country.

Table 7.4 Details of rights conferred in the CPRs of the project areas:

1	2	3	4	5	6	7				8
Names of the Districts	Names of the projects	Names of the villages	Particular of CPR	Nature of right	Period of right	Beneficiary details (no. of families)				User Charges (Rs.)
						SC	St	Others	Total	
East Khasi Hills District	EKH-IWMP-VIII	Jongksha	Community Forest	Fw	6 months	-	473	-	423	Nil
		Laitkyrhong	Community Forest	Fw	6 months	-	327	-	327	Nil
		Laitlum	Community Forest	Fw	6 months	-	65	-	65	Nil

* From column no. 2, no. of States; from column no. 3, no. of Districts; from column no. 4, no. of projects; from column no. 5, no. of villages; from column nos. 9 & 10, particular-wise totals for the entire country may be given at the end of the table.

@ In column no. 6, the categories given in table no. M(SP) 10, column 5 may be filled as required.

In column no. 7, only the letter assigned to each type, as given below, needs to be typed.

F	for right to	fishing [culture, harvest and sale]
Fw	for right to	collect firewood for domestic purposes
G	for right to	grazing for cattle and
MFP	for right to	collect and sell minor forest produces
P	for right to	passage across the CPR
Rd	for right to	construct a road for access to individual property
S/M	for right to	collect and sell sand and minerals
T	for right to	collect timber for construction of house
Wd	for right to	collect/ use water for drinking
Wi	for right to	use water for irrigation
O	for any right other than indicated above (please specify)	

Table 7.5 Water related outcomes:

Table 7.5.1 Details of average ground water table depth in the project areas of the Country: State-wise * (in metres)

1	2	3	5				
Sl.No	Names of Village	Sources	Pre-Project level (Meters from Ground Level)		Expected Post-Project level (Meters from Ground Level)		Remarks
			Rainy Season	Non – Rainy Season	Rainy Season	Non – Rainy Season	
1	Jongksha	Open Wells	-	-	-	-	-
2	i) Laitkyrhong ii) Laitlum	Open Wells	-	-	-	-	-
TOTAL							

* From column no. 2, total number of States; from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column nos. 6 to 9, the average measurements, category-wise, for the entire country may be given at the end of the table. The data must be based on the average of the Ground Water Table collected by PIA with the help of concerned technical expert in the same sample of 10 % of selected wells and bore wells in the villages in the watershed project area during pre-project, mid-term and post-project periods.

Table 7.5.2 Status of Drinking water:

1	2	3			4			5
District	Name of the project	Availability of drinking water (no. of months in a year)			Quality of drinking water			Comments
		Pre-project	Post-project	Change in availability	Pre-project	Post-project	Change in quality	
East Khasi Hills District	EKH-IWMP - VIII	7 – 9 months	About 12 months	10 – 12 months	Moderate portable	Portable	Improved	-

* From column no. 2, total number of States implementing the programme, from column no. 3, total no. of Districts; from column no. 4, category-wise no. of projects, from column no. 5, average no. of months may be given at the end of the table for the entire country.

Table 7.5.3 Water Use efficiency:

1	2	3	4			
District	Name of the project	Name of major crop	Water savings in cu.m.			
			through water saving devices ^{\$}	through water conserving agronomic practices [#]	Any other (pl specify)	Total
East Khasi Hills District	EKH-IWMP - VIII				-	-

* From column no. 2, total number of States implementing the programme, from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column no. 6, practice-wise totals may be mentioned at the end of the table for the entire country.

^{\$} Sprinkler, Drip, PVC pipe, etc.

[#] Vermi-compost, organic manuring, Mulching, Check basin, Alternate furrow, Ridges & furrow & other scientific practices.

Table 7.6: Vegetation/ crop related outcomes:

Table 7.6.1 Details of Kharif crop area and yield in the project areas:

1	2	3	4					5					6							
Names of the Districts	Name of Projects	Name of crops	Pre-project					Mid-term					Post-project							
			Area (ha)		Average Yield (Qtl) per ha.		Total Production (Qtl)		Area (ha)		Average Yield per ha (Qtl)		Total Production (Qtl)		Area (ha)		Average Yield per ha (Qtl)		Total Production (Qtl)	
			Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.
		Cabbage	-	35	-	150		5250	130	-	180	-	23400	-	220	-	180	-	39600	

* From column no. 2, total number of States; from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column no. 5, total no. of crops; from column no. 6 to 8, the totals for the area, average yield per ha and total production, category-wise, for the entire country may be given at the end of the Table.

Irri. – Irrigated Rf – Rainfed

Table 7.6.2 Details of Rabi crop area and yield in the project areas:

1	2	3	4	5	6						7						8					
SI No.	Names of States	Names of the Districts	Name of Projects	Name of crops	Pre-project						Mid-term						Post-project					
					Area (ha)		Average Yield (Qtl) per ha.		Total Production (Qtl)		Area (ha)		Average Yield per ha (Qtl)		Total Production (Qtl)		Area (ha)		Average Yield per ha (Qtl)		Total Production (Qtl)	
					Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.
	Meghalaya	East Khasi Hills District	EKH-IWMP VIII	Tomato	-	35	-	21	-	735	80	-	30	-	2400	-	125	-	30	-	3750	-
				Potato	-	50	-	60	-	3000	200	-	100	-	20000	---	250	-	100	-	25000	-
			Total for the District																			

* From column no. 2, total number of States; from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column no. 5, total no. of crops; from column no. 6 to 8, the totals for the area, average yield per ha and total production, category-wise, for the entire country may be given at the end of the Table.

Irri. – Irrigated Rf – Rainfed

Table 7.6.3 Details of Zaid crop area and yield in the project areas of the Country: State-wise:

1	2	3	4	5	6						7						8					
Sl No	Names of States	Names of the Districts	Name of Projects	Name of crops	Pre-project						Mid-term						Post-project					
					Area (ha)		Average Yield (Qtl) per ha.		Total Production (Qtl)		Area (ha)		Average Yield per ha (Qtl)		Total Production (Qtl)		Area (ha)		Average Yield per ha (Qtl)		Total Production (Qtl)	
					Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.	Irri	Rf.
	Meghalaya	East Khasi Hills District	EKH-IWMP VIII	Potato	-	80	-	60	-	4800	180	-	100	-	18000	-	200	-	100	-	20000	-
				Tomato	-	40	-	25	-	1000	120	-	30	-	3600	-	125	-	30	-	3750	-
			Total for the District																			

* From column no. 2, total number of States; from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column no. 5, total no. of crops; from column no. 6 to 8, the totals for the area, average yield per ha and total production, category-wise, for the entire country may be given at the end of the Table.

Irri. – Irrigated Rf – Rainfed

Table 7.6.4 Increase/ Decrease in area under fodder:

1	2	3	4			5		
District	Name of project	Duration of Project	Existing area under fodder (ha)			Achievement (ha)		
			Source/Name of report	Year of reference	Area already under fodder	Area under fodder proposed to be covered through IWMP	Area under fodder actually covered through IWMP	Change in area under fodder
East Khasi Hills District	EKH-IWMP - VIII	5 yrs	NA	NA	NA	nil	nil	nil

* From column no. 2, total number of States implementing the programme, from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column nos. 6 & 7, total area in ha may be given at the end of the table for the entire country.

Table 7.6.5 Increase/ Decrease in Forest/vegetation cover:

1	2	3	4			5		
District	Name of project	Duration of Project	Existing area tree cover (ha)			Achievement (ha)		
			Source/Name of report	Year of reference	Area already under forest/vegetative cover	Forest/vegetative cover area proposed to be covered under IWMP	Forest/vegetative cover area actually covered under IWMP	Change in forest/vegetative cover area
East Khasi Hills District	EKH-IWMP - VIII	5 yrs	As per LULC Map	2006 - 07	153 Ha	360 Ha	360 Ha	360 Ha

* From column no. 2, total number of States implementing the programme, from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column nos. 6 & 7, total area in ha may be given at the end of the table for the entire country.

Table 7.6.6 Increase/ Decrease in area under horticulture:

1	2	3	4			5		
District	Name of project	Duration of Project	Existing area under horticulture (ha)			Achievement (ha)		
			Source/Name of report	Year of reference	Area already under horticulture	Area under horticulture proposed to be covered through IWMP	Area under horticulture actually covered through IWMP	Change in area under horticulture
East Khasi Hills District	EKH-IWMP - VIII	5 yrs	-	-	-	100 Ha	100 Ha	100 Ha

* From column no. 2, total number of States implementing the programme, from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column nos. 6 & 7, total area in ha may be given at the end of the table for the entire country.

Table 7.6.7 Increase/ Decrease in area under fuel-wood:

1	2	3	4			5		
District	Name of project	Duration of Project	Existing area under fodder (ha)			Achievement (ha)		
			Source/Name of report	Year of reference	Area already under fuel-wood	Area under fuel-wood proposed to be covered under IWMP	Area under fuel-wood actually covered under IWMP	Change in area under fuel-wood
East Khasi Hills District	EKH-IWMP - VIII	5 yrs	-	-	-	100 Ha	100 Ha	100 Ha

* From column no. 2, total number of States implementing the programme, from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column nos. 6 & 7, total area in ha may be given at the end of the table for the entire country.

Table 7.7 Livelihood related outcomes:

Table 7.7.1 Details of livestock in the project areas (for fluids please mention in litres, for solids please mention in kgs. and income in Rs.):

1	2	3	4			5			6			7
Names of the Districts	Name of Projects	Type of Animal	Pre-project			Mid-term			Post-project			Remarks
			No.	Yield	Income	No.	Yield	Income	No.	Yield	Income	
		Piggery	838 nos.	-	64.92	1200	-	76.80				
		Poultry	1737	-	6.60	2258	-	13.20				
		Grocery	664	-	37.84	796	-	6368				
	Total for all projects		-	-	91.36	-	-	153.68				
Total for all Districts												

* From column no. 2, total number of States; from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column nos. 5 to 8, the total nos. of animals and the average yield and incomes, category-wise, for the entire country may be given at the end of the Table.

Table 7.7.2 Details of other livelihoods created for landless people:

1	2	3	4	5				6	7					8				
District	Project	Name of activity	Fund required for the activity (Rs.)	Sources of funding (Rs.)				Actual Expenditure incurred on activity (Rs.)	No. of beneficiaries trained					No. of beneficiaries taking up activity				
				Project Fund	Beneficiary	Others (pl. specify)	Total		SC	ST	Others	Women	Total	SC	ST	Others	Women	Total
East Khasi Hills District	EKH-IWMP VIII	Tailoring	10000/-	8000/-	2000/-	-	10000/-	12000/-	-	20	10	10	20	-	20	10	10	20
		Hollow Block making	8000/-	5000/-	3000/-	-	8000/-	8000/-	-	3	3	-	-	-	3	3	-	3
		Apiculture	8000/-	5000/-	3000/-	-	8000/-	8000/-	-	10	10	-	10	-	10	10	-	10
		Carpentry	8000/-	5000/-	3000/-	-	8000/-	8000/-	-	4	4	-	4	-	4	4	-	4
		Piggery/Poultry	12000/-	8000/-	400/-	-	12000/-	4000/-	-	50	25	25	50	-	50	25	25	50

(Contd.)

* From column no. 2, total number of States; from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column no. 5, total no. of activities; from column no. 6, total funds required for the activity, from column no. 7 to 12, category-wise totals, from column no. 13, category-wise totals, for the entire country may be given at the end of the Table.

Table 7.7.3 Details of other livelihoods created for landless people:

9		10	11				12
No. of persons employed indirectly in the activity		Annual increase in income due to activity (Rs.)	Impact of livelihoods programme				Any other information (pl. Specify)
			Migration (No. of beneficiaries)		Development of backward-forward linkages		
Total	Grand Total (8+9)		Pre-project	Post-project	Pre-project	Post-project	
(i) 15	35		-	-	-	-	
(ii) 7	10	-	-	-	-	-	-
(iii) 16	26	-	-	-	-	-	-
(iv) -	50	-	-	-	-	-	-
(v) 6	10	-	-	-	-	-	-
(vi) 40	90	-	-	-	-	-	-

Table 7.7.4 Details of other livelihoods created for farmers:

1	2	3	4	5				6	7				8			
District	Project	Name of activity	Fund required for the activity (Rs.) in lakhs	Sources of funding (Rs.) in Lakhs				Actual Expenditure incurred on activity (Rs.)	No. of farmers trained				No. of farmers taking up activity			
				Project Fund	Beneficiary	Others (pl. specify)	Total		SF	MF	LF	Total	SF	MF	LF	Total
East Khasi Hills District	EKH-IWMP-VIII	i) Kitchen gardening	5000	2500	2500	-	5000	5000	-	62	10	72	-	62	10	72
		ii) Apiculture	8000	5000	3000	-	8000	8000	-	20	-	20	-	20	-	20
		iii) Tailoring	10000	8000	2000	-	10000	10000	-	7	3	10	-	7	3	10
		iv) Piggery	12000	8000	4000	-	12000	12000	-	17	13	30	-	17	13	30

* From column no. 2, total number of States; from column no. 3, total no. of Districts; from column no. 4, total no. of projects, from column no. 5, total no. of activities; from column no. 6, total funds required for the activity, from column no. 7 to 12, category-wise totals, from column no. 13, category-wise totals, for the entire country may be given at the end of the Table.

Table 7.7.5 Details of other livelihoods created for farmers * (contd.)

9		10	11				12
No. of persons employed indirectly in the activity		Annual increase in income due to activity (Rs.)	Impact of livelihoods programme				Any other information (pl. Specify)
			Migration (No. of beneficiaries)		Development of backward-forward linkages		
Total	Grand Total (8+9)		Pre-project	Post-project	Pre-project	Post-project	
(i) -	22	-	-	-	-	-	-
(ii) 5	25	-	-	-	-	-	-
(iii) 10	20	-	-	-	-	-	-
(iv) 30	30	-	-	-	-	-	-

**Table 7.8 Marketing related outcomes:
Backward-Forward linkages ***

1	2	3	4	5	6
District	Project	Type of Marketing Facility	Pre-project (no.)	During the project (no.)	Post-project (no.)
East Khasi Hills District	EKH-IWMP - VIII	(A) Backward linkages			
		(i) Seed certification	-	-	-
		(ii) Seed supply system	-	-	-
		(iii) Fertilizer supply system	-	-	-
		(iv) Pesticide supply system	-	-	-
		(v) Credit institutions	-	4	10
		(vi) Water supply	-	-	2
		(vii) Extension services	-	20	30
		(viii) Nurseries	-	-	1 no.
		(ix) Tools/machinery suppliers	-	2	2
		(x) Price Support system	-	-	-
		(xi) Labour	-	4000	6000
		(xii) Any other (please specify)	-	-	-
		(A) Forward linkages		-	-
		(i) Harvesting/threshing machinery	-	-	-
		(ii) Storage (including cold storage)	-	-	-
		(iii) Road network	-	-	-
		(iv) Transport facilities	-	-	-
		(v) Markets / Mandis	-	1 no.	1 no.
		(vi) Agro and other Industries	-	20 nos.	30 nos.
		(vii) Milk and other collection centres	-	-	-
		(viii) Labour	-	6000	8000
		(ix) Any other (please specify)	-	-	-

* from column no. 2, total no. of States implementing the programme, from column no. 3, total no. of Districts; from column no. 4, total no. of projects; from column no. 6, 7 & 8, category-wise totals may be given at the end of the table for the entire country.

Table 7.9 Abstract of outcomes:

1	2	3	4	5	6	7
Sl. No.	State	Item	Unit	Pre-project Status	Post-project Status	Remarks
		Status of water table		-	-	
		Ground water structures repaired/ rejuvenated			10 nos.	
		Quality of drinking water		Moderate potable	Improved	
		Availability of drinking water		Insufficient	Sufficient	
		Increase in irrigation potential		-	nos.	
		Change in cropping/ land use pattern		-	-	
		Area under agricultural crop				
		i Area under single crop		-	-	
		ii Area under double crop		60 ha	100 ha	
		iii Area under multiple crop		-	-	
		Net increase in crop production area				
		Increase in area under vegetation		-	360ha	
		Increase in area under horticulture		-	100 ha	
		Increase in area under fuel & fodder		-	100 ha	
		Increase in milk production		-	-	
		No. of SHGs		10nos.	30 nos.	
		Increase in no. of livelihoods		-	-	
		Increase in income		-	45,000	
		Migration		-	-	
		No. of school going children		-	-	
		SHG Federations formed		-	-	
		Credit linkage with banks		-	25 nos.	
		Resource use agreements		-	12 nos.	
		WDF collection & management		-	2nos.	
		Summary of lessons learnt	May be attached as a separate file			

Table 7.10 Cost effectiveness of structures/ activities*


1	2	3	4	5	6	7	8	9	10
District	Name of project	Name of WC	Name of structure/ activity	Estimated cost (Rs.)	Expected quantifiable benefits (Rs.)	Expenditure incurred (Rs.)	Actual quantifiable benefit (Rs.)	Benefit: Cost ratio [#]	IRR
East Khasi Hills District	EKH-IWMP - VIII	i) Middle Umlew & ii) Umprah Watershed	As per Treatment Plan	117.0 lakhs	179.01 lakhs	117.0 lakhs	-	1.53	-


* from column no. 2, total no. of States implementing the programme, from column no. 3, total no. of Districts; from Column no. 4, no. of projects, from column no. 5, no. of WCs, from column no. 6, no. of structures/ activities, from column no. 7 to 10, category-wise# totals, may be mentioned at the end of the table for the entire country.


[#] B:C ratio more than 1 – cost effective
less than 1 – Not cost effective


ANNEXURE I


MAPS

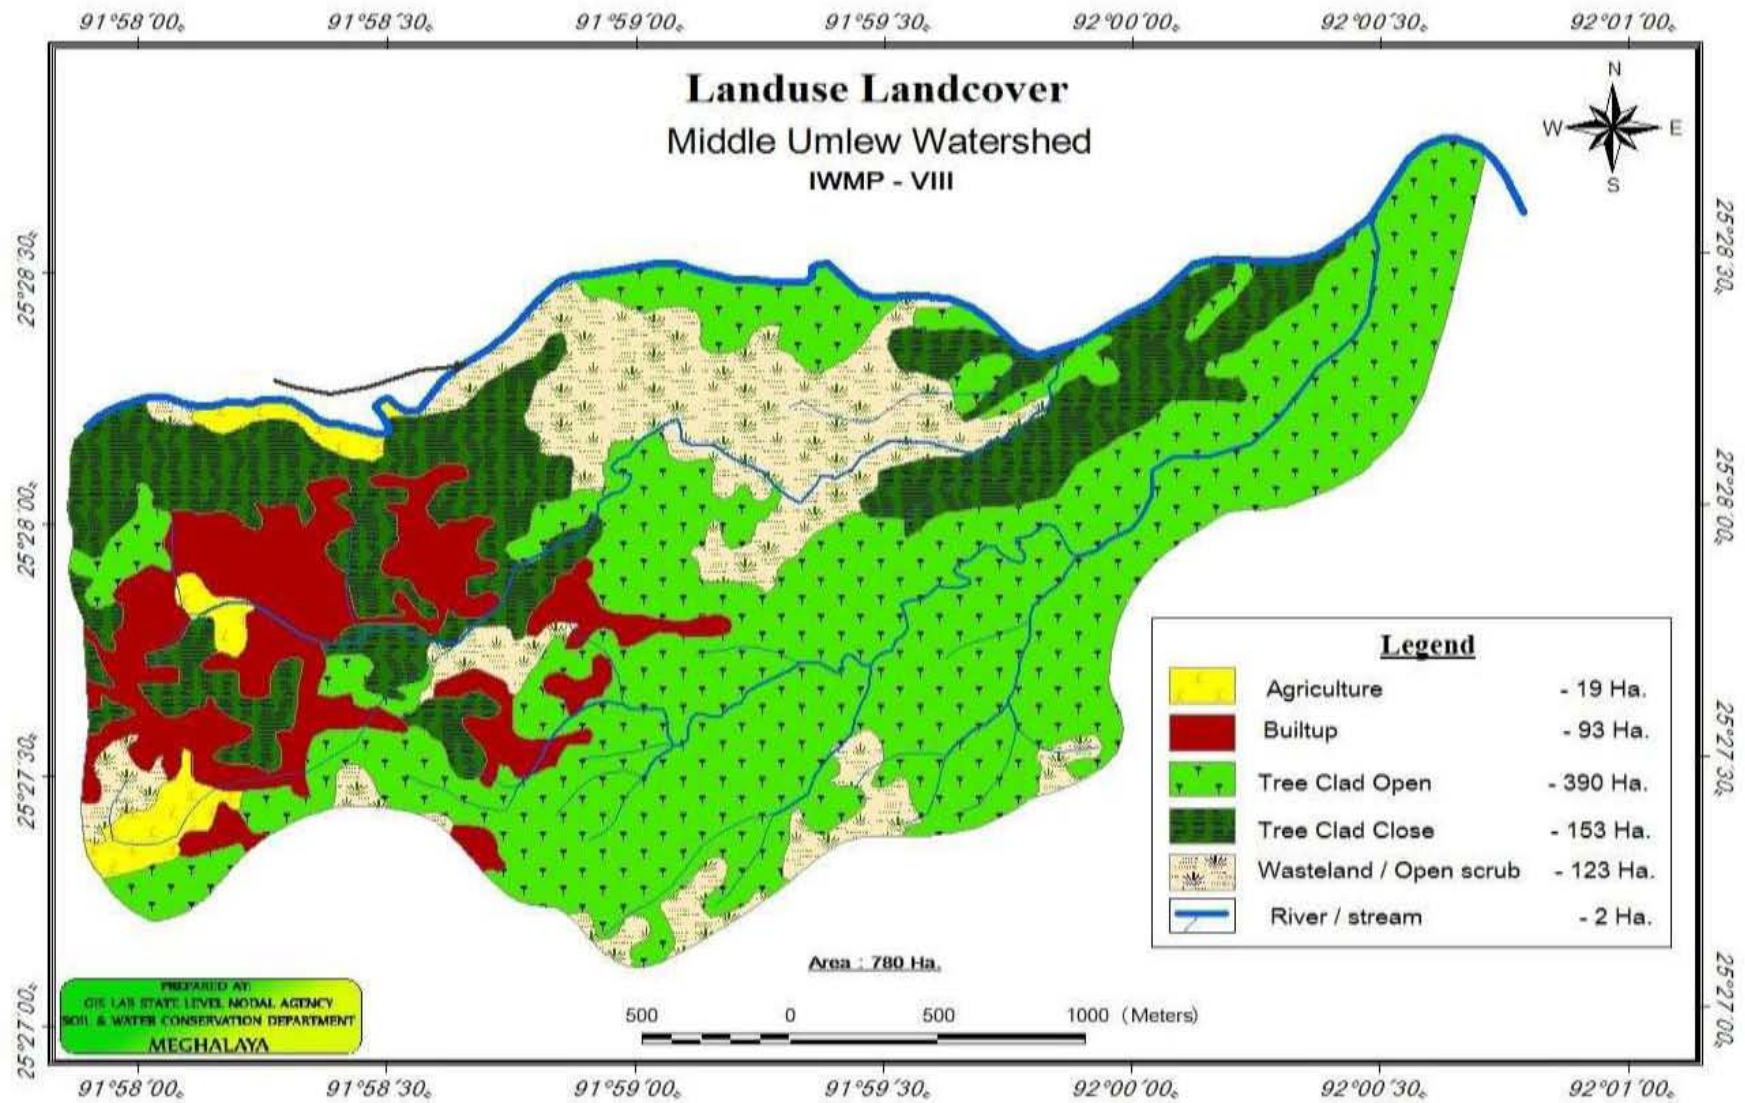


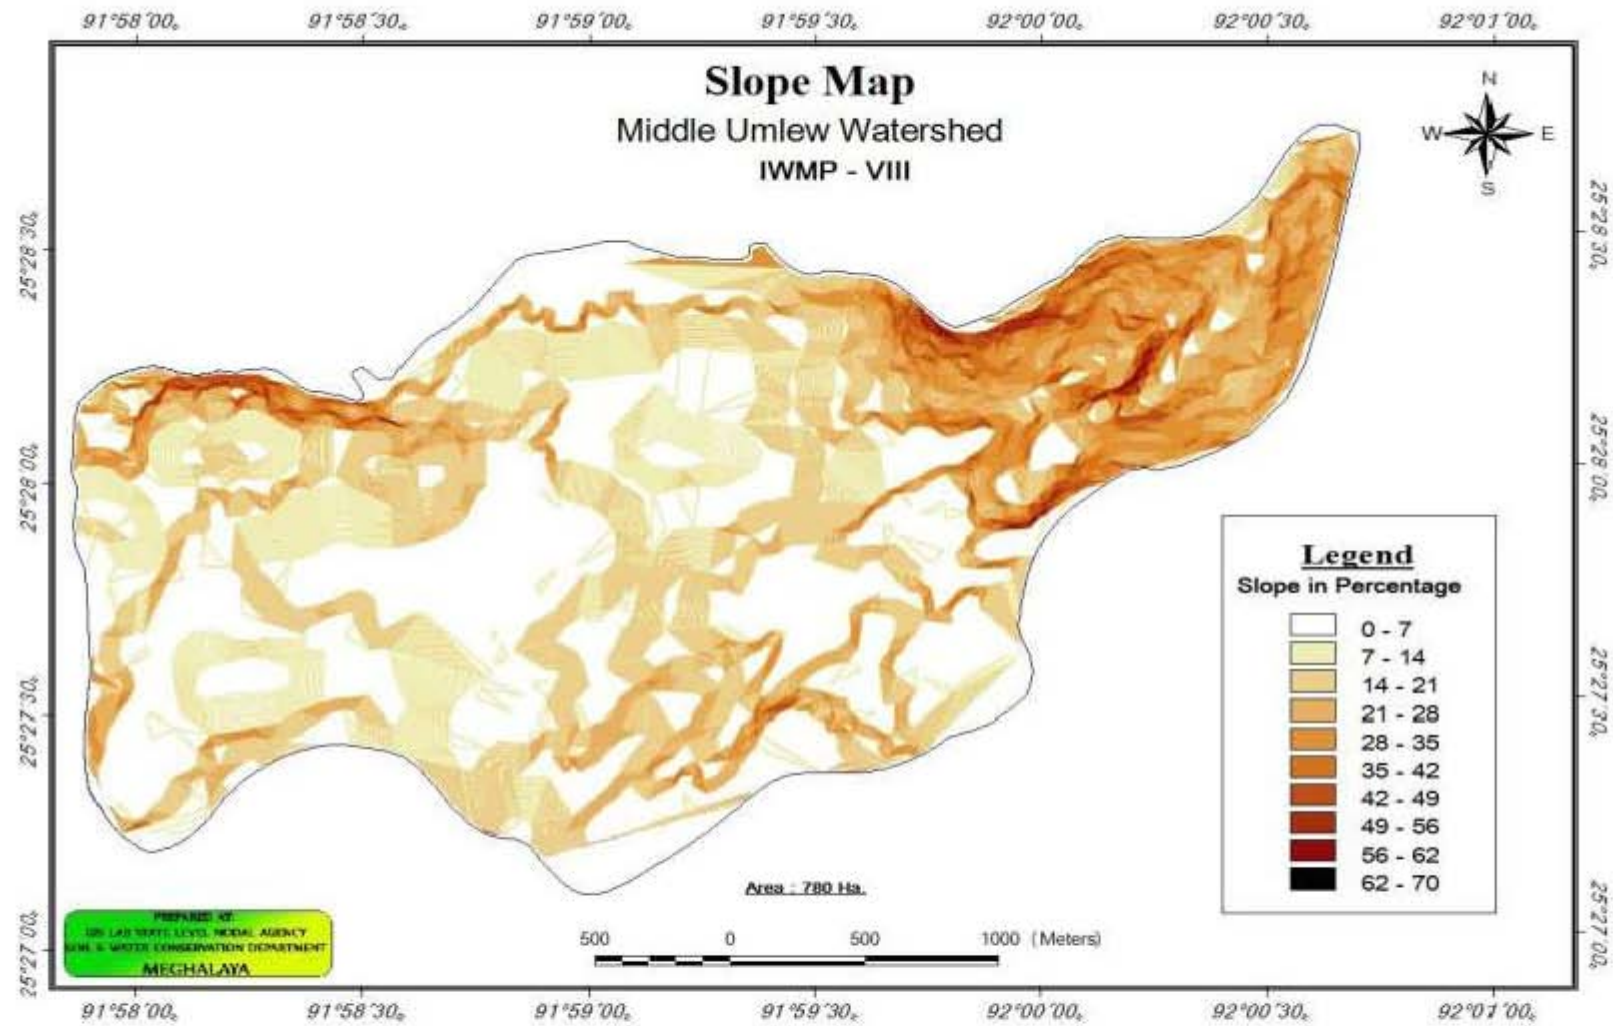


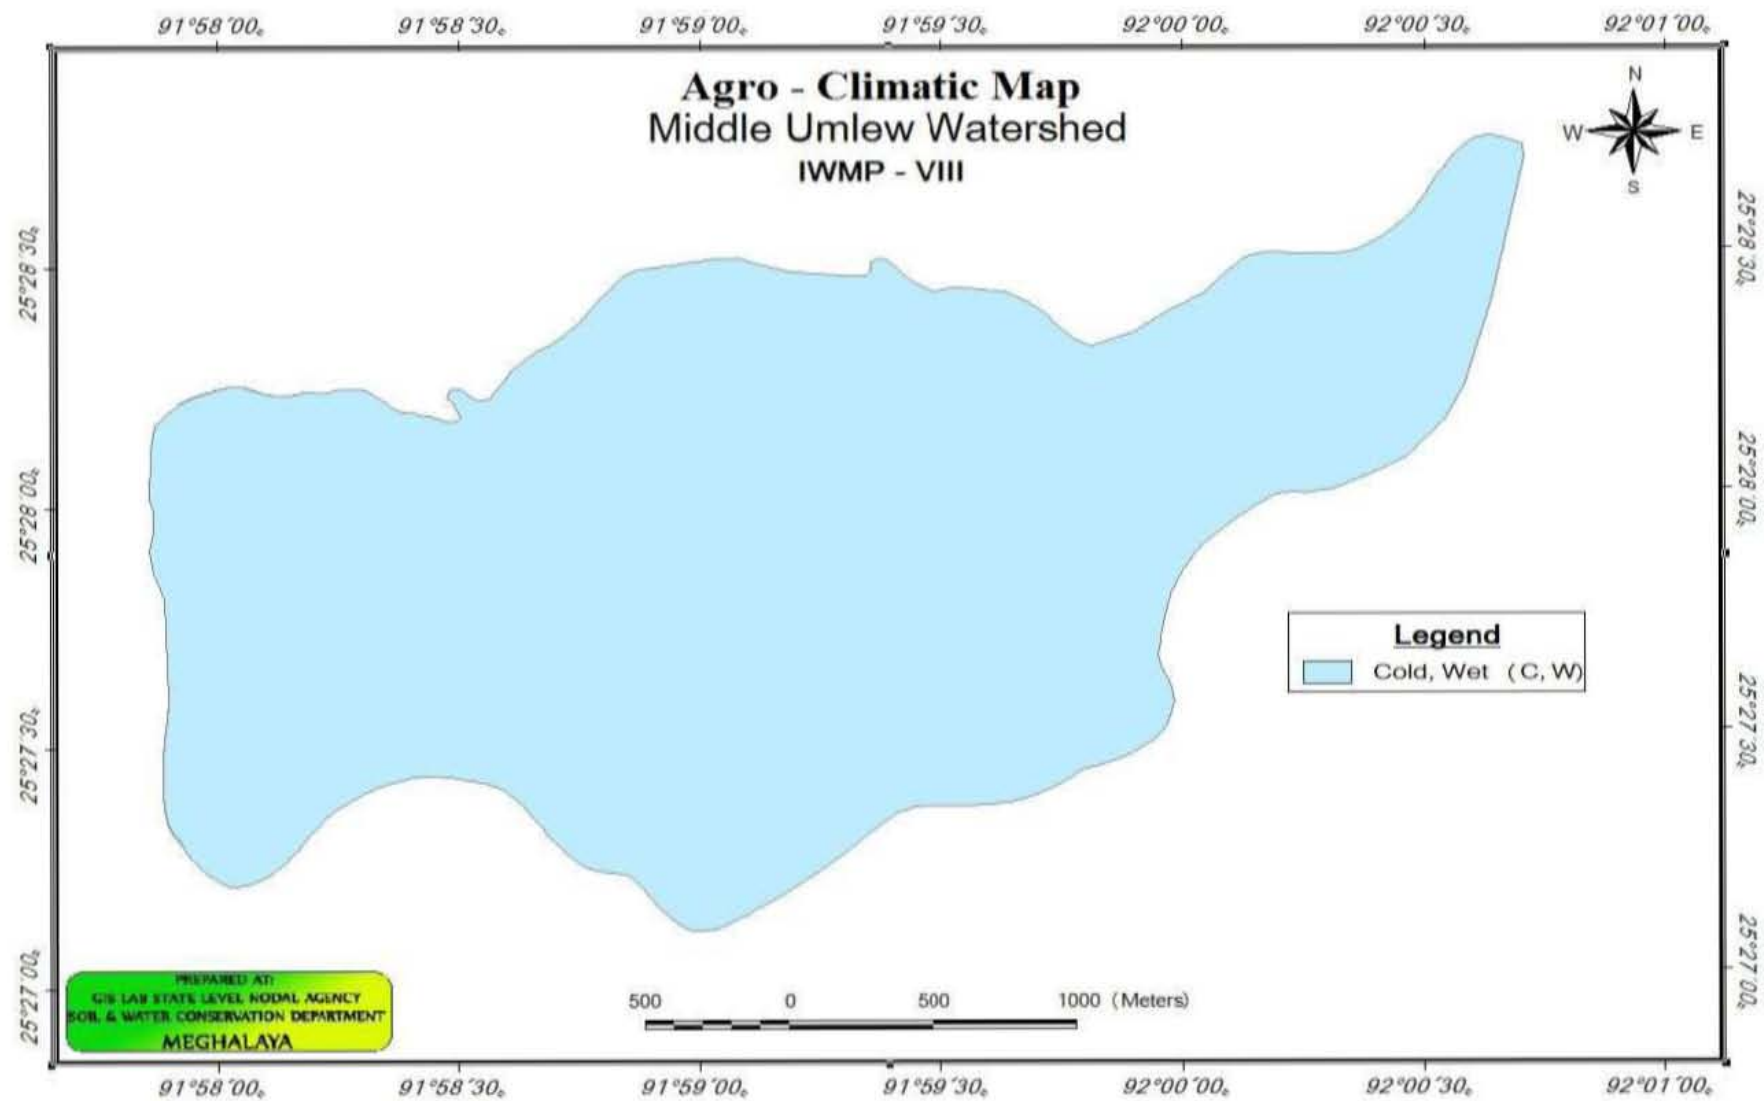


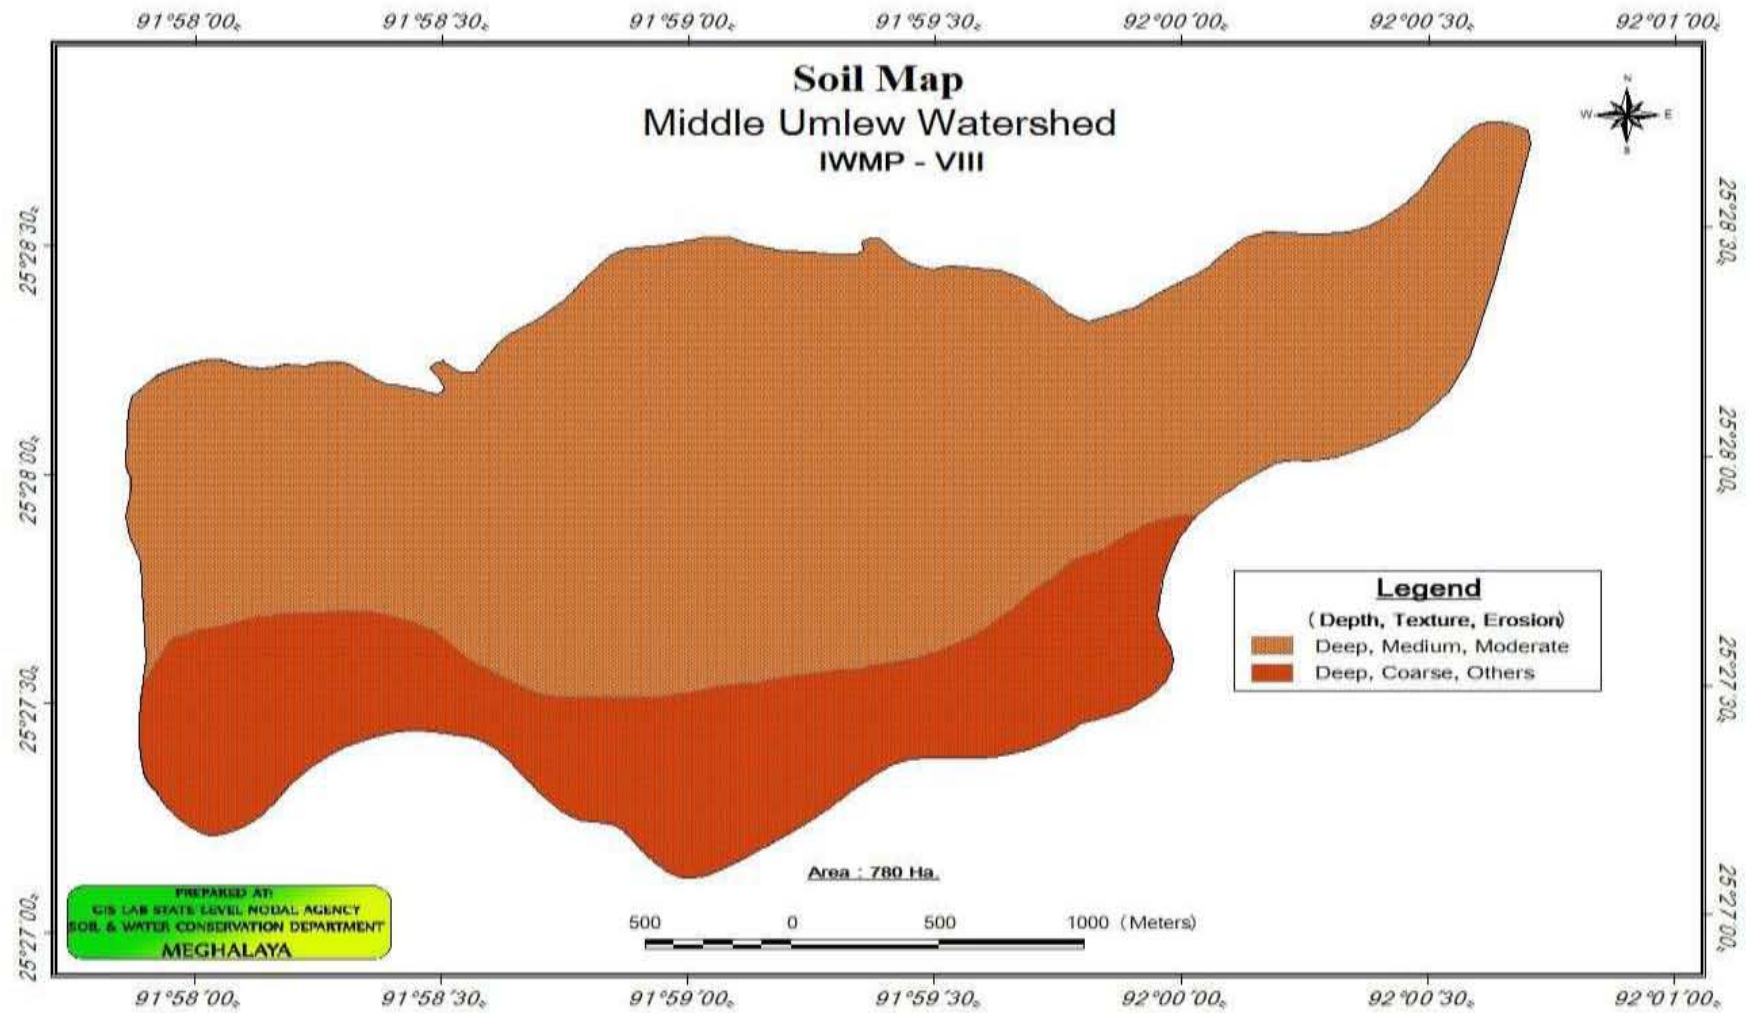


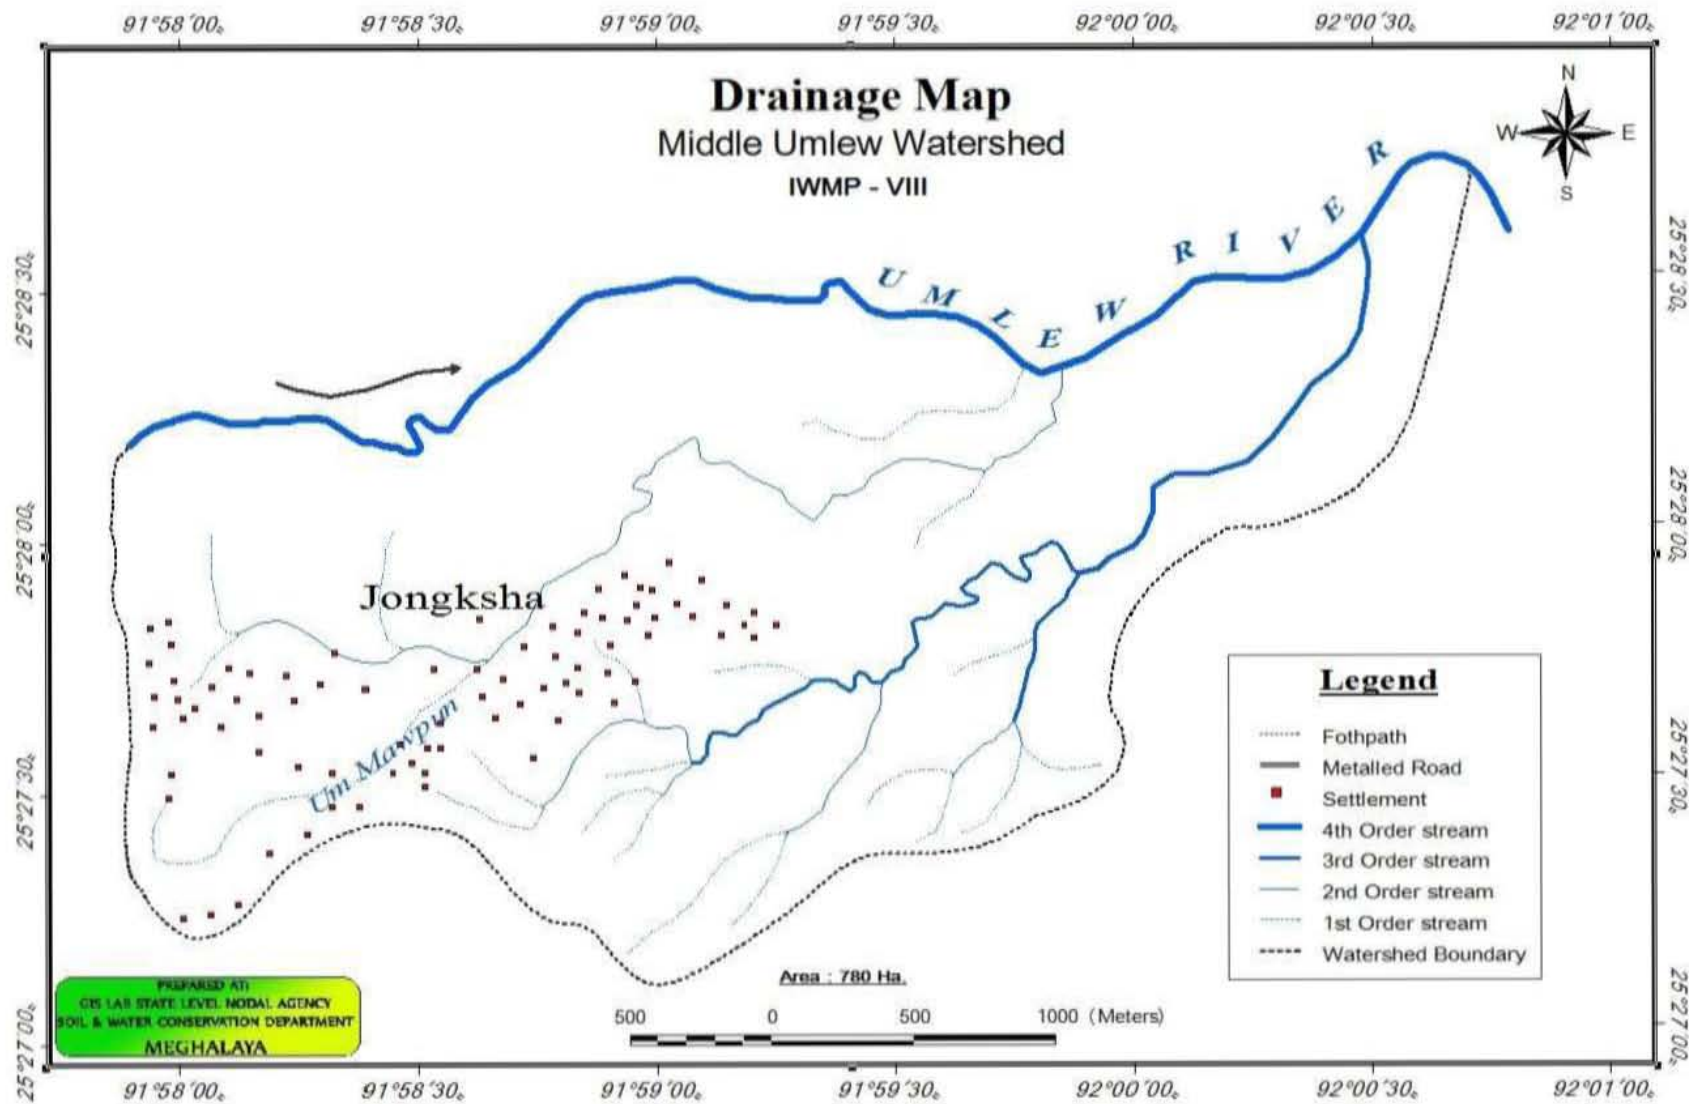


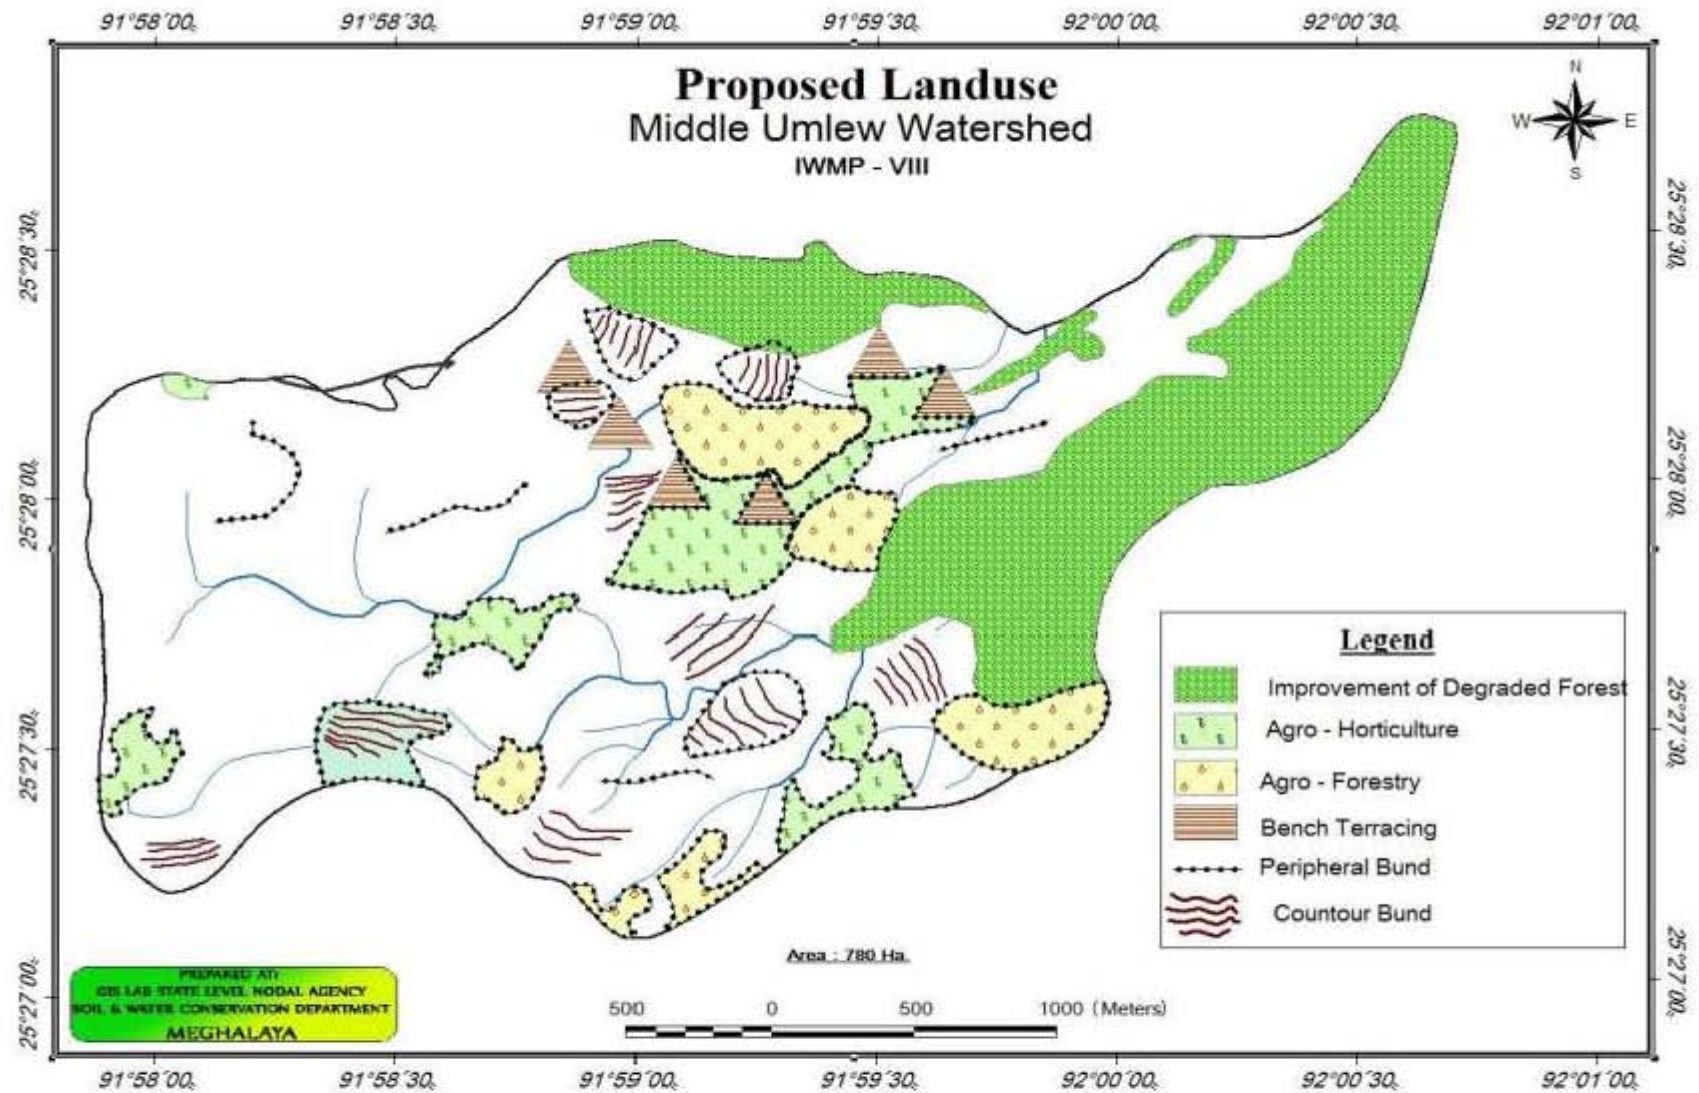


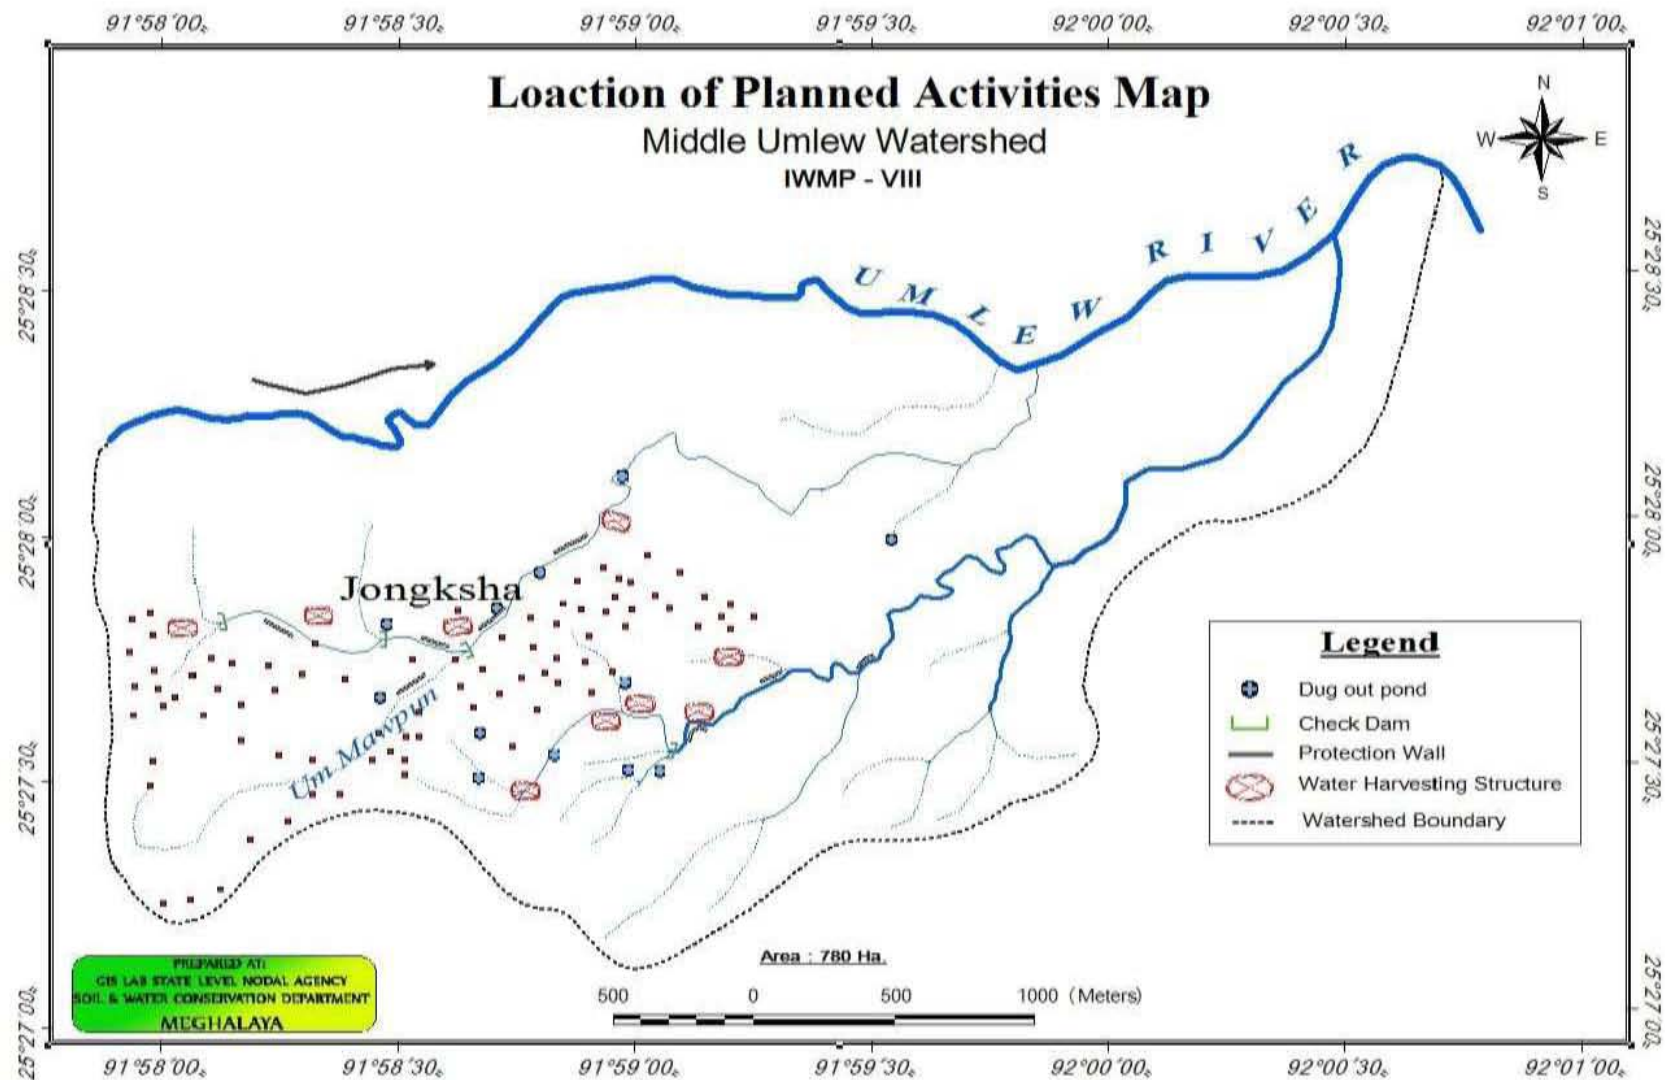


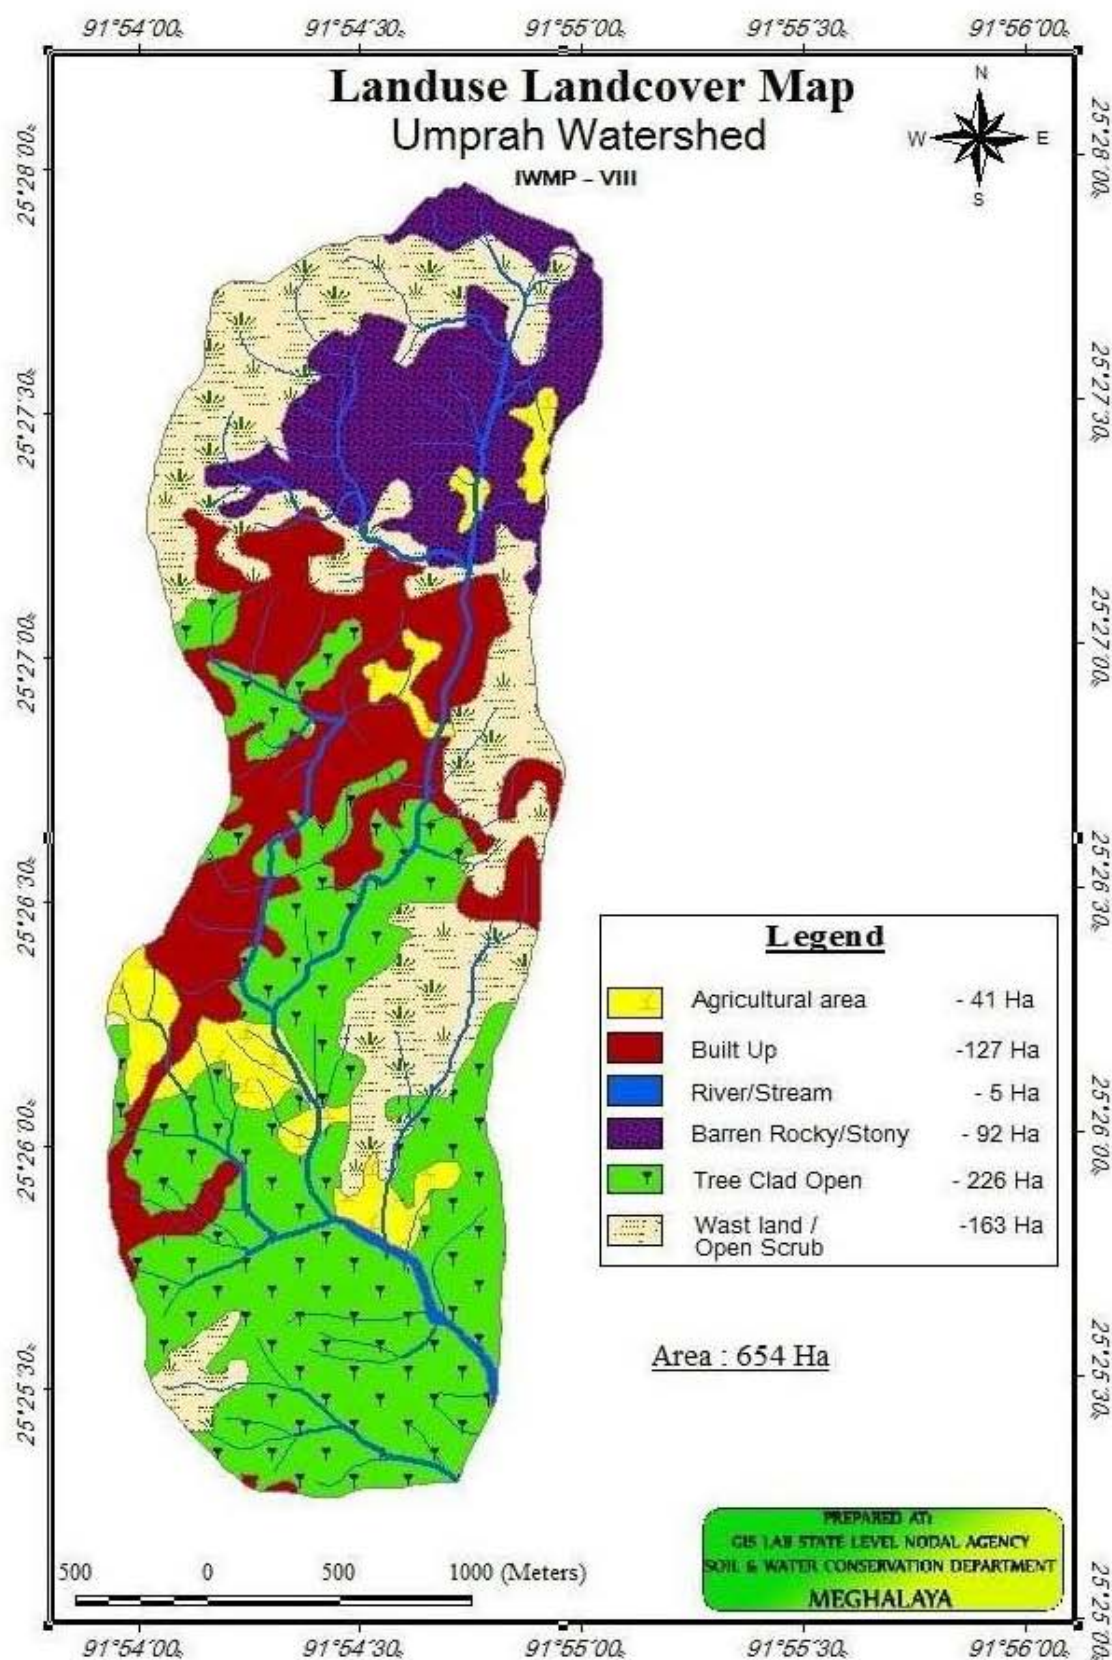


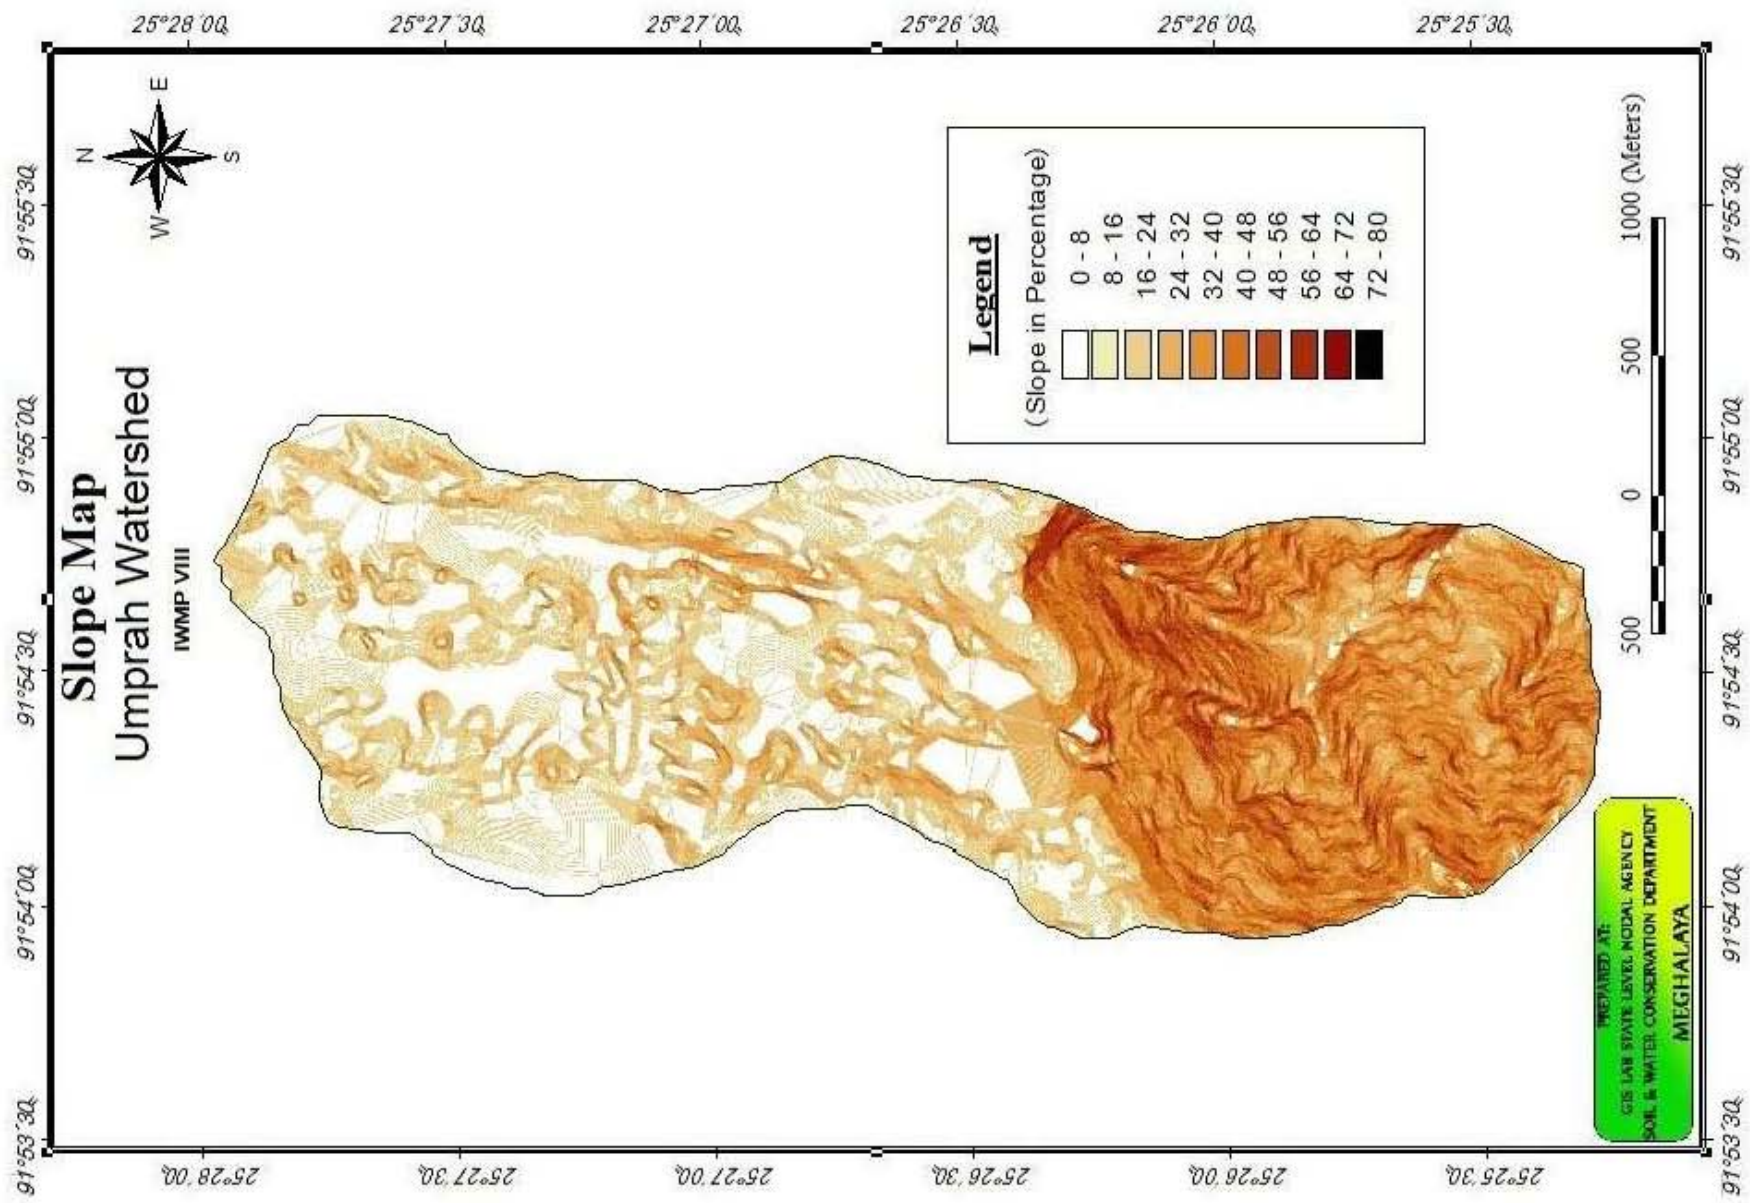


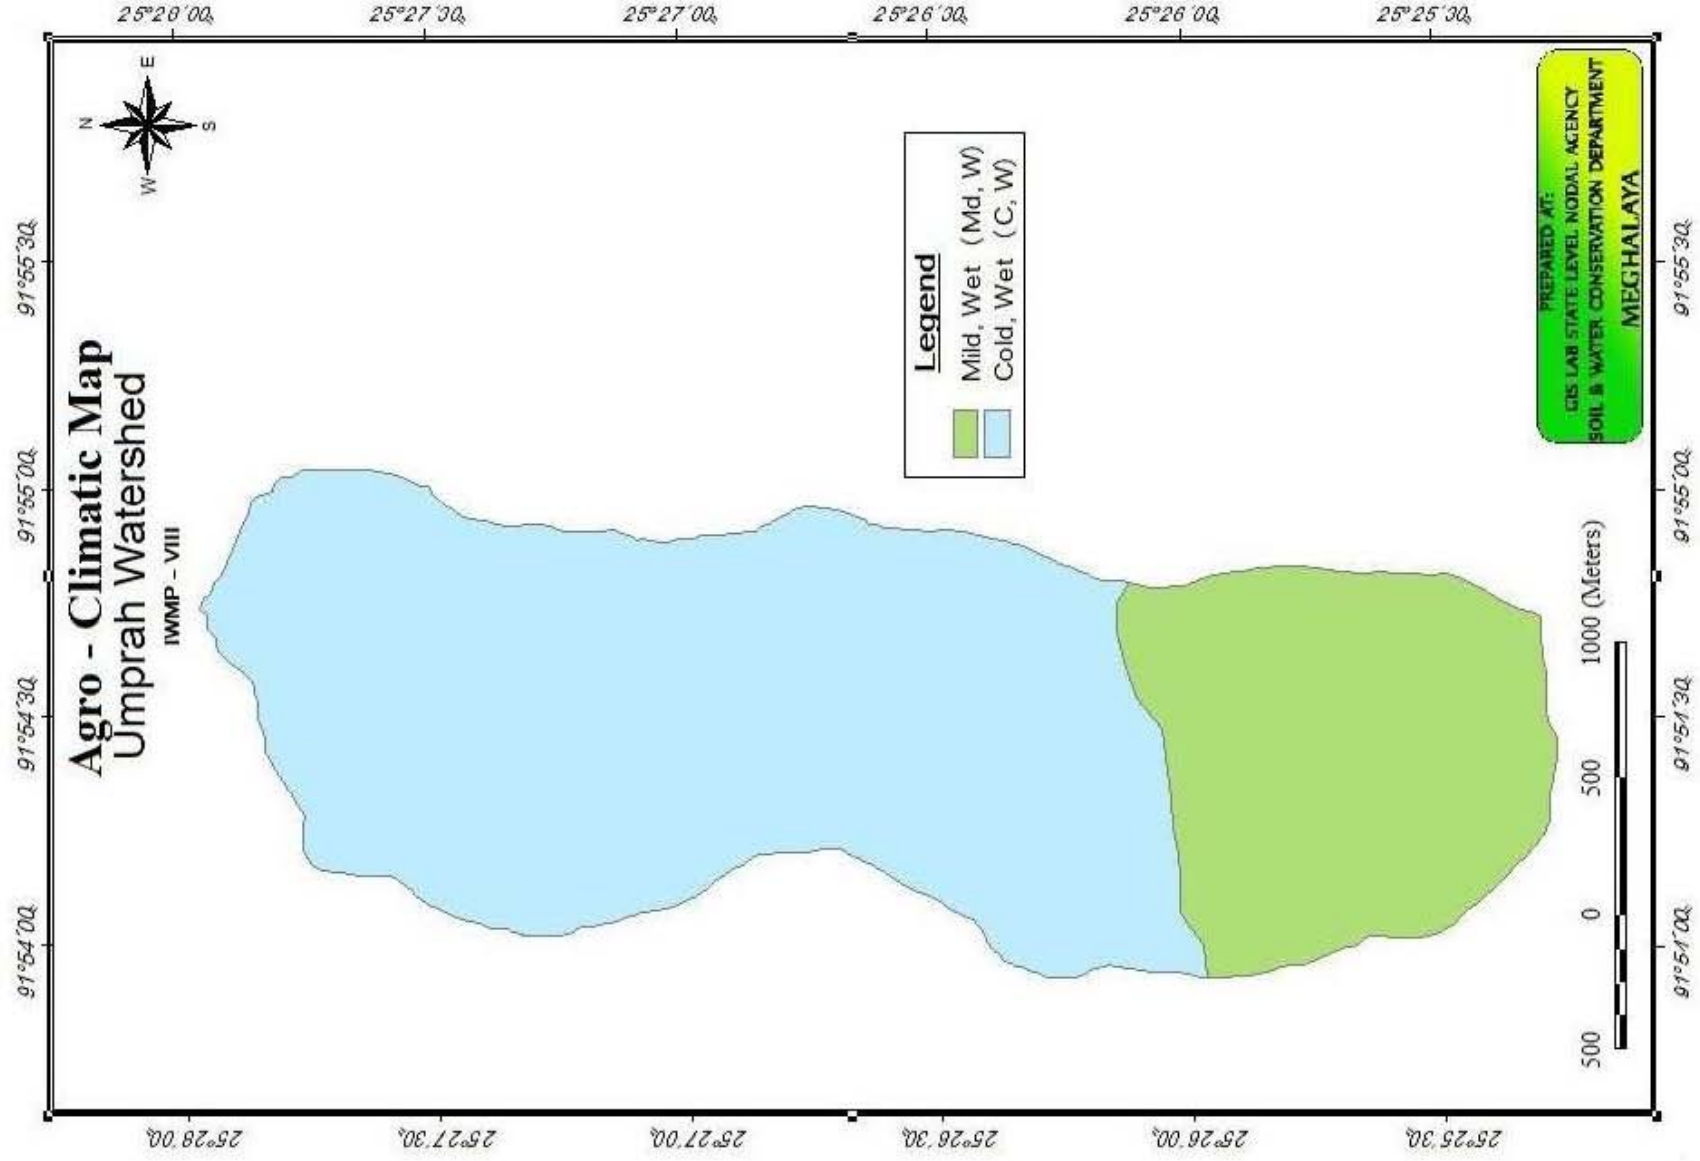

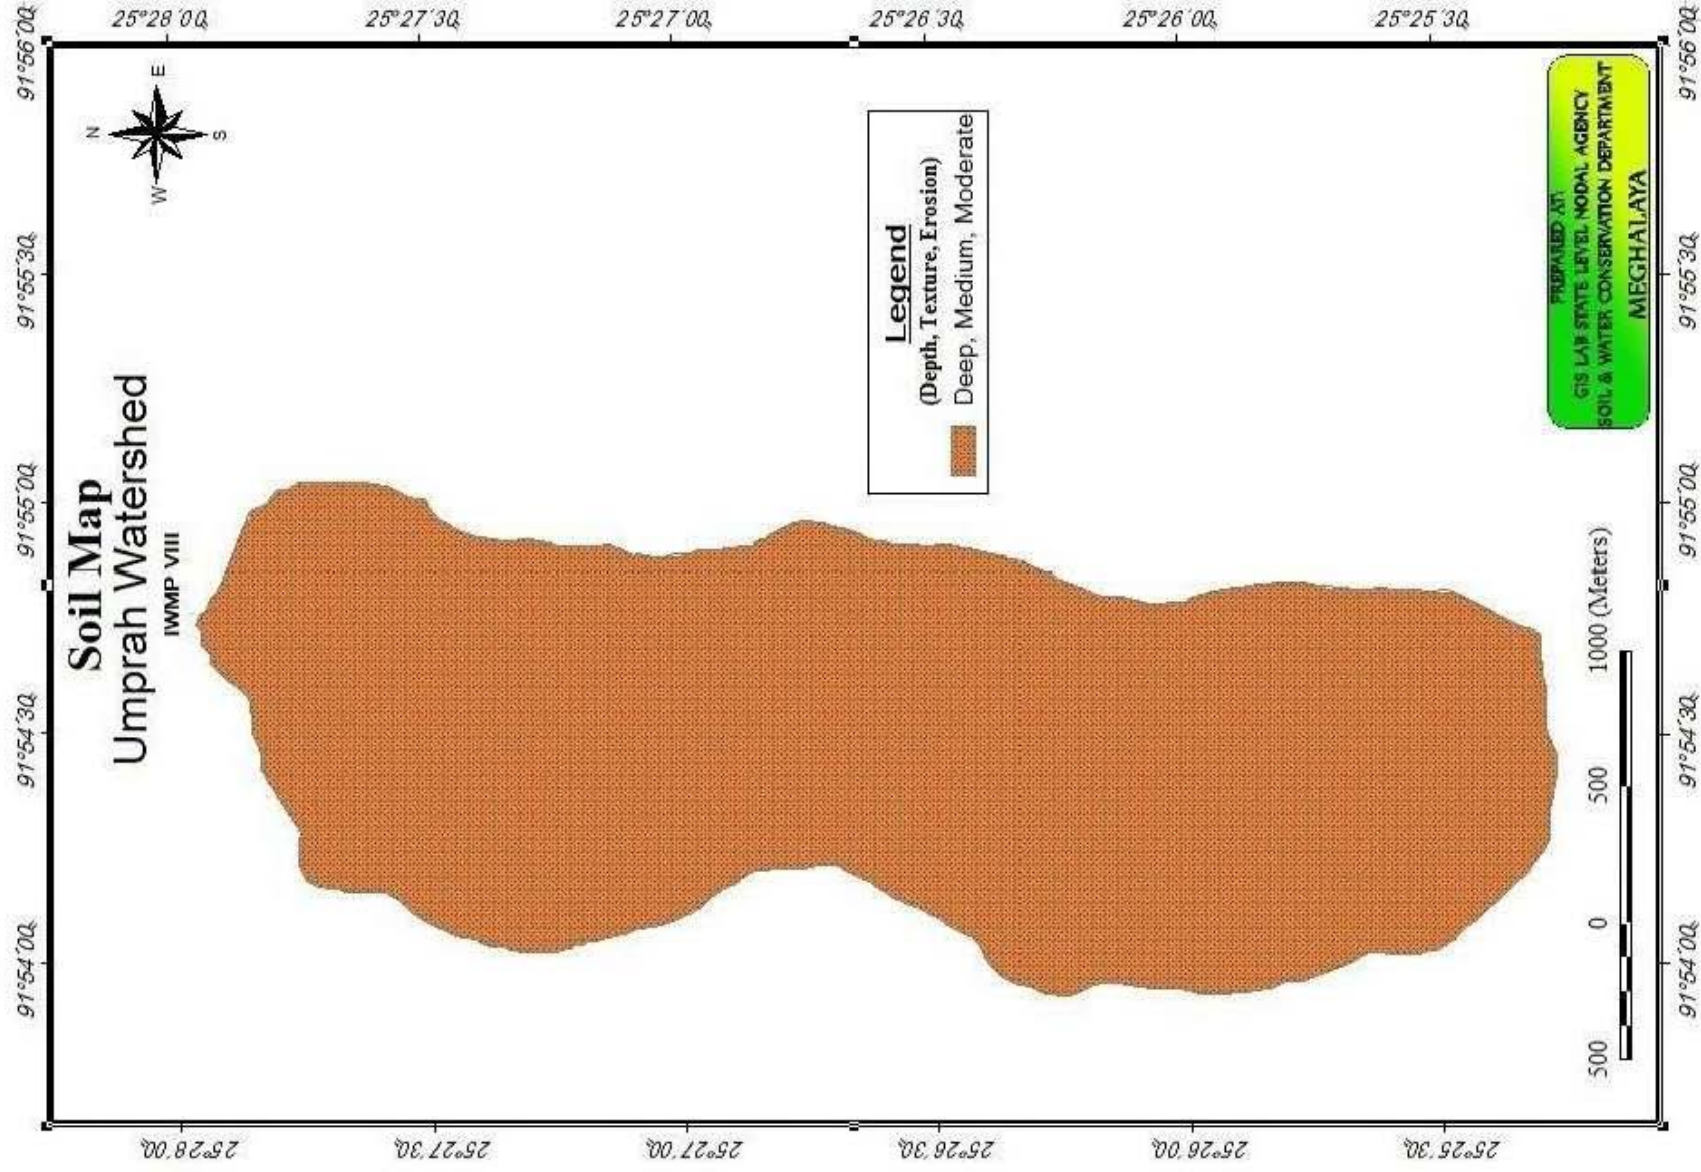

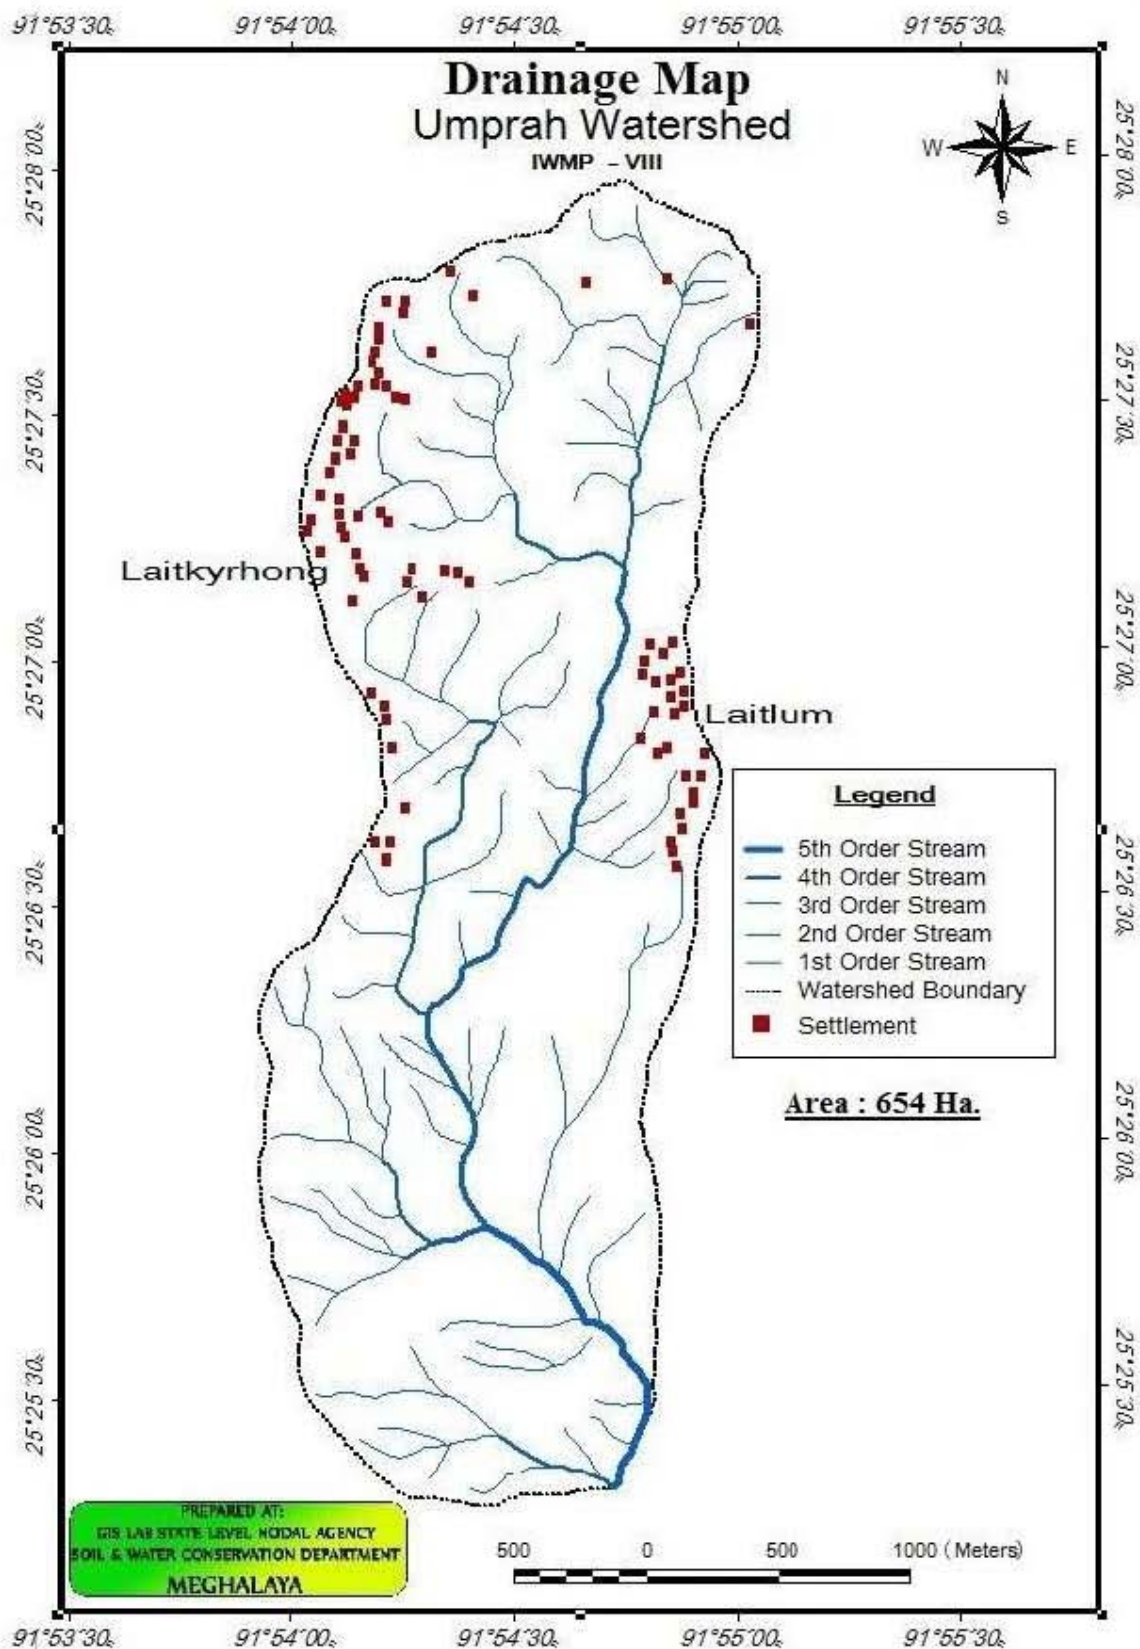

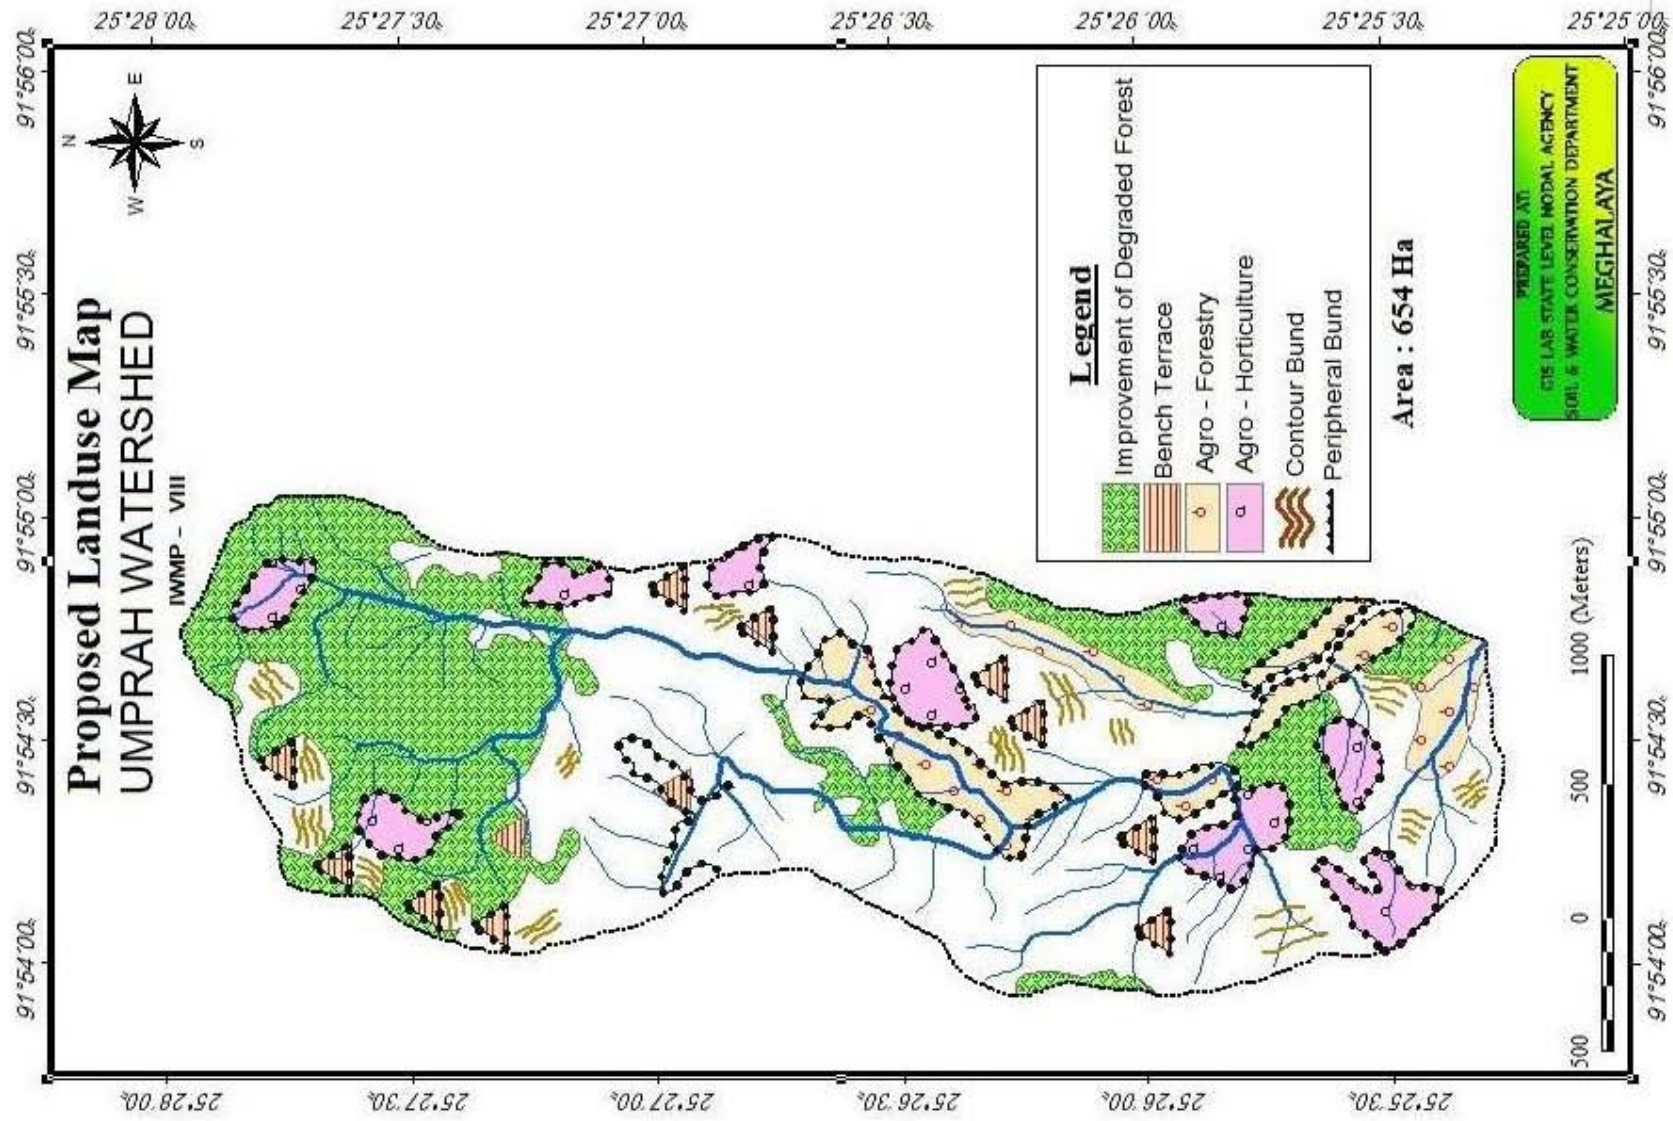

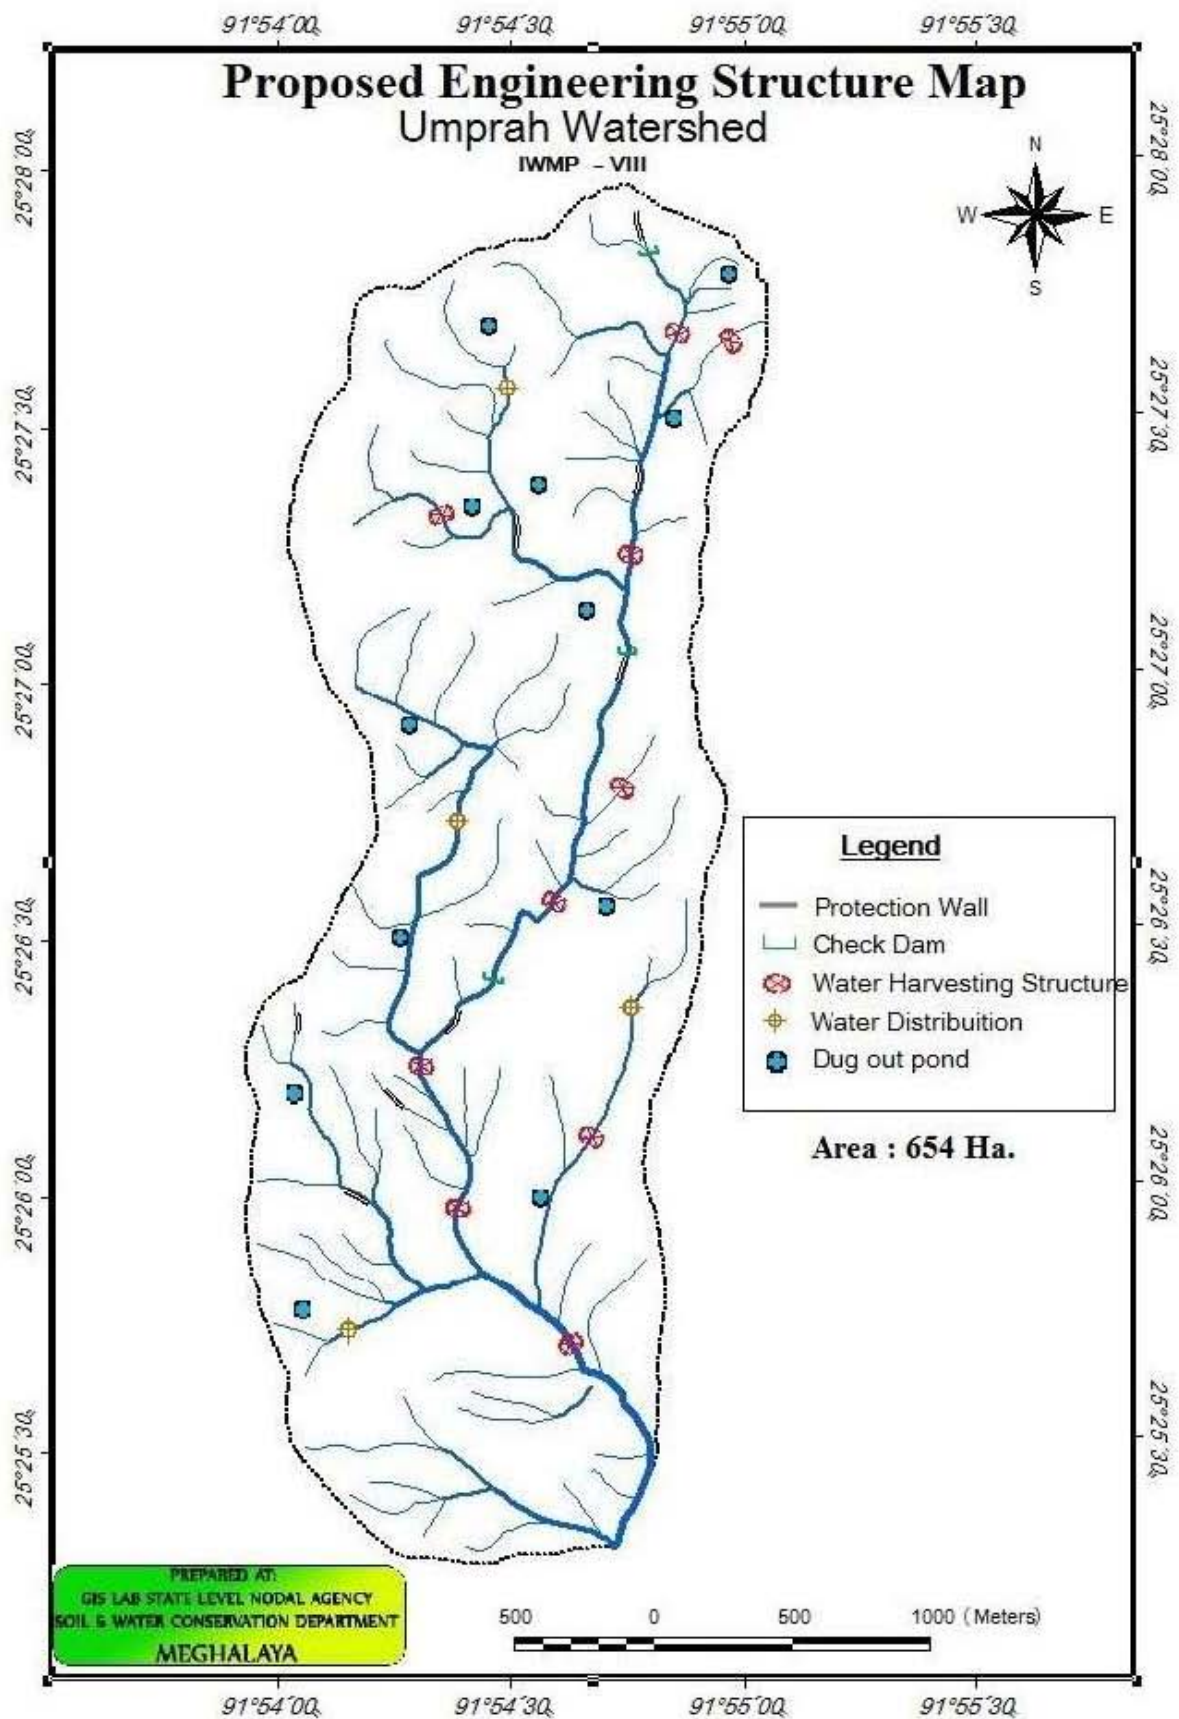

ANNEXURE II

SOCIO-ECONOMIC SURVEY DETAILS

SOCIO – ECONOMIC DATA OF JONGKSHA VILLAGE UNDER MIDDLE UMLEW WATERSHED (2010-2011) P-VIII

Sl No	Name of the Head of the Family	Population			Literacy			Occupation	Agriculture Area		Livestock					Annual Income
		Male	Female	Total	Literate	Illiterate	Total		Settled	Jhum	Cow	Pig	Goat	Poultry	Horse	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
	MISSION															
1	K. Swer Pyngrope	2	3	5	1	4	5	Farmer	-	.50	-	-	-	-	-	16000
2	Hepdeng Pyngrope	2	2	4	-	4	4	-do-	-	.30	-	-	-	-	-	13000
3	Sidret Kharsohnoh	3	3	6				-do-	-	.20	2	1	-	5	-	8000
4	Jermen Rynjah	7	2	9				-do-	-	0.30	-	-	3	3	-	8500
5	Bitalis Mynsong	4	3	7				-do-	-	-	3	-	-	5	-	12000
6	Thoris Mynsong	6	2	8				-do-	-	1.00	-	-	-	4	-	10000
7	Rita Mynsong	2	2	4				-do-	-	-	-	3	-	6	-	8000
8	Sesilia Lyngdoh	1	7	8				-do-	-	-	-	-	-	-	-	9000
9	Darwin Mynsong	2	2	4				-do-	-	-	-	1	-	3	-	8500
10	Bisiona Kharmuti	2	4	6				-do-	-	0.40	-	-	-	7	-	9200
11	Philinda Rynjah	2	3	5				-do-	-	-	-	-	5	6	-	12000
12	Sunta Kharmuti	3	6	9				-do-	-	0.20	-	-	-	-	-	13000
13	Dwina Kharmuti	3	6	9				-do-	-	0.50	-	-	-	3	-	9000
14	Drina Kharmuti	3	2	5				-do-	-	-	2	4	-	5	-	10000
15	Instura Mynsong	1	3	4				-do-	-	0.20	-	3	-	8	-	11000
16	Loreto Mynsong	2	5	7				-do-	-	-	-	3	-	7	-	9000
17	Harbel Suting	3	1	4				-do-	-	0.30	-	1	-	5	-	9500
18	Thwun Nongrum	2	4	6				-do-	-	1.00	-	2	-	3	-	13000
19	Beril Kharmuti	3	3	5				-do-	-	-	-	1	-	9	-	10200
20	Plis Shadap	2	2	4				-do-	-	0.20	-	-	-	8	-	11000
21	Suklin Lyngdoh	1	2	3				-do-	-	0.30	-	2	-	7	-	12000
22	Sakharius Rynjah	3	3	6				-do-	-	0.40	5	3	-	5	-	13000
23	Bless Star Nongrum	3	3	6				-do-	-	0.30	-	3	-	6	-	9000
24	Phillip Mynsong	3	4	7				-do-	-	0.20	-	-	-	3	-	13000
25	Spiam Nongrum	3	2	5				-do-	-	0.20	-	-	1	3	-	10000
26	Basilla Lawai	3	4	7				-do-	-	0.50	-	1	-	6	-	11000
27	Evansius Nongrum	3	5	8				-do-	-	0.20	-	1	-	3	-	13000
28	Rangstar Kharmulieh	1	3	4				-do-	-	3.00	-	1	-	6	-	10000
29	Masilin Warjri	2	7	9				-do-	-	-	-	-	-	4	-	8000
30	Ioanis Lawai	8	3	11				-do-	-	0.70	-	-	-	4	-	8000
31	Probina Nongspung	3	4	7				-do-	-	0.30	-	2	-	6	-	10000
32	Bisten Kharsohnoh	1	5	6				-do-	-	0.20	-	-	-	8	-	9000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
33	Icydora Mynsong	-	1	1				-do-	-	-	-	-	-	5	-	11000
34	Aquila Nongrum	1	3	4				-do-	-	-	-	-	-	4	-	14000
35	Helen Songthiang	1	5	6				-do-	-	-	-	1	-	3	-	13000
36	Korina Kharmulieh	3	4	7				-do-	-	0.20	-	-	-	7	-	12000
37	Rosemary Kharrymmai	4	2	6				Farmer	-	0.20	5	3	-	10	-	13000
38	Jenus Nongrum	4	3	7				-do-	-	0.20	-	-	-	4	-	10000
39	Lukas Pyngrope	2	4	6				-do-	-	0.50	-	1	-	-	-	11000
40	Gabornor Nongspung	3	3	6				-do-	-	0.20	-	-	-	-	-	13000
41	Aklinda Kharmulieh	2	1	3				-do-	-	3.00	-	-	-	6	-	10000
42	Spier Nongspung	1	2	3				-do-	-	0.30	-	-	-	5	-	8000
43	Khirian Kharmulieh	1	2	3				-do-	-	0.70	-	-	-	3	-	8000
44	Torin Pyngrope	2	3	5				-do-	-	0.30	-	4	-	-	-	10000
45	Khrinda Rynjah	2	3	5				-do-	-	0.20	-	3	-	3	-	9000
46	Rilis Rynjah	3	3	6				-do-	-	-	-	3	-	-	-	11000
47	Sidalin Rynjah	2	2	4				-do-	-	-	-	1	-	5	-	14000
48	Samiion Rynjah	3	3	6				-do-	-	-	-	2	-	6	-	13000
49	Irla	2	5	7				-do-	-	0.20	-	1	-	-	-	12000
50	Bandro Khongsngi	4	4	8				-do-	-	0.30	-	-	-	-	-	10000
51	Iebon Kharsahnoh	3	3	6				-do-	-	0.55	-	2	4	10	-	10000
52	Wandalang Kharsohnoh	1	1	2				-do-	-	-	5	3	5	-	-	13000
53	Jrod Kharsahnoh	3	2	5				-do-	-	0.30	8	3		-	-	10000
54	Tiak Kharsohnoh	3	2	5				-do-	-	0.20	-	3	5	4	-	10000
55	Ling Mynsong	2	1	3				-do-	-	2.00	-	1	-	6	-	12000
56	Sambor Surong	4	1	5				-do-	-	0.30	-	3	-	2	-	10000
57	Skar Pyngrope	4	3	7				-do-	-	2.00	-	2	-	5	-	13000
58	Drom Kharsohnoh	2	2	4				-do-	-	0.20	-	2	5	-	-	12000
59	Henry Songthiang	2	2	4				-do-	-	0.30	-	3	14	-	-	13000
60	Wellesly Suting	1	2	3				-do-	-	0.40	-	-	10	5	-	10000
61	Ringkhuid Kharsohnoh	2	1	3				-do-	-	0.20	-	-	12	-	-	11000
62	Driak Suting	2	4	6				-do-	-	1.00	-	3	-	3	-	13000
63	Trila Suting	2	3	5				-do-	-	0.20	-	2	-	8	-	10000
64	Broi Songthiang	3	3	6				-do-	-	1.00	-	-	-	5	-	8000
65	Mon Songthiang	1	2	3				-do-	-	0.20	5	-	-	4	-	8000
66	San Songthiang	2	3	5				-do-	-	-	-	-	-	-	-	10000
67	Rosina Songthiang	-	3	3				-do-	-	-	-	3	-	-	-	9000
68	Rising Songthiang	1	2	3				-do-	-	-	-	-	-	-	-	11000
69	Ling Kharsohnoh	1	3	4				-do-	-	-	5	1	-	2	-	14000
70	Ablessius Lawai	1	3	4				-do-	-	-	-	-	-	-	-	13000
71	Kwisna Songthiang	1	2	3				-do-	-	-	-	-	-	-	-	12000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
72	Jaintia Songthiang	2	4	6				-do-	-	-	-	-	-	3	-	10000
73	Hando Kharbangar	2	2	4				-do-	-	-	1	-	-	-	-	10000
74	Markus Rynjah	3	3	6				-do-	-	-	-	4	-	-	-	13000
75	Bihrit Kharmylliem	2	2	2				-do-	-	-	-	3	-	3	-	10000
	TOTAL	179	221	400					-		41	89	64	269	-	
	MAWPUN								-							
76	Edmund Songthiang	3	3	6	2	4	6	Farmer	-	0.20	5	3	-	10	-	10000
77	Olet Kharsohnoh	1	4	5	2	3	5	-do-	-	0.20	-	-	-	4	-	25000
78	Debora Pyngrope	3	1	4	2	2	4	-do-	-	0.50	-	1	-	-	-	15000
79	Shidalang Nongbri	5	1	6	3	3	6	-do-	-	0.20	-	-	-	-	-	15000
80	Khrer Songthiang	7	1	8	3	5	8	-do-	-	3.00	-	-	-	6	-	20000
81	Sibistian Kharmuti	6	2	8	3	5	8	-do-	-	0.30	-	-	-	5	-	20000
82	Liansirda Songthiang	7	2	9	5	4	9	-do-	-	0.70	-	-	-	3	-	25000
83	Wanisha Songthiang	2	1	3	-	3	3	-do-	-	0.30	-	4	-	-	-	25000
84	LArilang Songthiang	2	1	3	1	2	3	-do-	-	0.20	-	3	-	3	-	15000
85	Horen Songthiang	5	6	11	7	4	11	-do-	-	-	-	3	-	-	-	25000
86	Indameri Kharmuti	7	2	9	4	5	9	-do-	-	-	-	1	-	5	-	25000
87	Helina War	4	4	8	2	6	8	-do-	-	-	-	2	-	6	-	20000
88	Airalin Nongspung	6	4	10	7	3	10	-do-	-	0.20	-	1	-	-	-	15000
89	Tiewlinda Songthiang	6	2	8	4	4	8	-do-	-	0.30	-	-	-	-	-	20000
90	Lambor Suting	4	3	7	3	4	7	-do-	-	0.55	-	2	4	10	-	25000
91	Kosen Kharsohnoh	4	4	8	4	4	8	-do-	-	-	5	3	5	-	-	15000
92	Kyntiewmon Kharrmai	2	3	5	2	3	5	-do-	-	0.30	8	3		-	-	20000
93	M. N. Massar	3	3	6	4	2	6	-do-	-	0.20	-	3	5	4	-	25000
94	Dinor Nongpluh	2	3	5	2	3	5	-do-	-	2.00	-	1	-	6	-	20000
95	Biorsen Kharmuti	1	-	1	-	1	1	-do-	-	0.30	-	3	-	2	-	15000
96	Wingson Marak	5	5	10	5	5	10	-do-	-	2.00	-	2	-	5	-	50000
97	Anjelina Kharmuti	7	2	9	4	5	9	-do-	-	0.20	-	2	5	-	-	25000
98	Nerila Nongkhlaw	1	4	5	4	1	5	-do-	-	0.30	-	3	12	-	-	25000
99	Sweetsida Songthiang	2	2	4	3	1	4	-do-	-	0.40	-	-	10	5	-	25000
100	Akwila Mynsong	7	2	9	7	2	9	-do-	-	0.20	-	-	11	-	-	25000
101	Shaibatstar Khriam	1	1	2	1	1	2	-do-	-	1.00	-	3	-	3	-	20000
102	Dralin Mynsong	-	-	-	-	-	-	-do-	-	0.20	-	2	-	8	-	25000
103	Ista Kshiar	4	1	5	-	5	5	-do-	-	1.00	-	-	-	5	-	20000
104	Monlang Kharsohnoh	1	1	2	1	1	2	-do-	-	0.20	5	-	-	4	-	25000
105	Klaren Kharmulieh	6	2	8	6	2	8	-do-	-	-	-	-	-	-	-	20000
106	Riten Kharsohnoh	1	3	4	4	-	4	-do-	-	-	-	2	-	-	-	20000
107	Kobel Rynjah	2	4	6	4	2	6	-do-	-	-	-	-	-	-	-	25000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
108	Bloiti Nonglyer	3	1	4	-	4	4	-do-	-	-	5	1	-	2	-	15000
109	Jrin Nonglyer	-	-	-	-	-	6	-do-	-	-	-	-	-	-	-	20000
110	Marius Mawlkhieng	4	1	5	-	5		-do-	-	-	-	-	-	-	-	25000
111	Jopsing Khriam	3	2	5	4	1	5	-do-	-	-	-	-	-	3	-	25000
112	Jecinta Suting	1	3	4	-	4	-	-do-	-	-	1	-	-	-	-	25000
113	Sunita	1	2	3	-	3	-	-do-	-	-	-	3	-	-	-	20000
114	Sabina Mylliem	1	2	3	-	3	-	-do-	-	-	-	3	-	3	-	20000
115	Lingstar Nongrum	1	1	2	-	2	-	-do-	-						-	25000
116	Erilis Songthiang	1	6	7	2	5	-	Farmer	-	0.20	5	3	-	10	-	20000
117	Dram Suting	4	2	6	2	4	-	-do-	-	0.20	-	-	-	4	-	20000
118	Kophi Kharmuti	4	2	6		6	-	-do-	-	0.50	-	1	-	-	-	20000
119	Shiningstar Mynsong	1	2	3		3	-	-do-	-	0.20	-	-	-	-	-	25000
120	Markus Pyngrope	1	2	3		3	-	-do-	-	3.00	-	-	-	6	-	25000
121	Ribarmon Kharsohnoh	2	1	-	1	1	-	-do-	-	0.30	-	-	-	5	-	25000
122	Anlet Lyngdoh	1	3	4	2	2	-	-do-	-	0.70	-	-	-	3	-	20000
123	Makrin Kharmulieh	7	2	9	4	5	-	-do-	-	0.30	-	3	-	-	-	20000
124	Ereen Kharmuti	2	3	5	3	2	-	-do-	-	0.20	-	2	-	3	-	20000
125	Phillip Suting	3	2	5	-	5	-	-do-	-	-	-	3	-	-	-	20000
126	Kanwanlang Lyngdoh	1	2	3	1	2	-	-do-	-	-	-	1	-	5	-	25000
127	Nicholas Lyngdoh	3	2	5	3	2	-	-do-	-	-	-	2	-	6	-	25000
128	Dromsing Kharbyngar	1	3	4	2	2	-	-do-	-	0.20	-	1	-	-	-	25000
129	N. Suting	-	2	2	1	1	-	-do-	-	0.30	-	-	-	-	-	20000
130	P. Suting	2	1	3	2	1	-	-do-	-	0.55	-	2	4	10	-	25000
131	S. Mylliempdah	1	3	4	2	2	-	-do-	-	-	5	3	5	-	-	20000
132	B. Kharbuli	1	1	2	-	2	-	-do-	-	0.30	8	3		-	-	20000
133	Kostan Songthiang	3	3	6	3	3	-	-do-	-	0.20	5	3	-	10	-	20000
134	Beldingstar Lyngdoh	5	2	7	4	3	-	-do-	-	0.20	-	-	-	4	-	15000
135	Reginal Mynsong	4	6	10	5	5	-	-do-	-	0.50	-	1	-	-	-	15000
136	Wandalang Suting	1	2	3	1	2	-	-do-	-	0.20	-	-	-	-	-	20000
137	Brosswel Songthiang	1	2	3	-	3	-	-do-	-	3.00	-	-	-	6	-	25000
138	Lili Thabah	2	1	3	2	1	-	-do-	-	0.30	-	-	1	5	-	25000
139	Mishal Thabah	1	1	22	-	2	-	-do-	-	0.70	-	-	-	3	-	20000
140	Tobias Kharsohnoh	5	4	9	5	4	-	-do-	-	0.30	-	3	-	-	-	25000
141	Robel Warbah	4	2	6	3	3	-	Govt.servant	-	0.20	-	-	-	3	-	25000
142	Mary Thabah	3	2	5	-	5	-	Farmer	-	0.50	-	1	-	6	-	25000
143	Ailinda lyngdoh	-	2	2	1	1	-	-do-	-	0.20	-	1	-	3	-	20000
144	Phew Songthiang	3	4	7	2	5	-	-do-	-	3.00	-	1	-	6	-	20000
145	Phroi Songthiang	2	5	7	3	5	-	-do-	-	-	-	-	-	4	-	25000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
146	Wanaiboklang Nongdhar	2	1	3	-	3	-	-do-	-	0.70	-	-	-	4	-	25000
147	Shembhalang K. Bihkhiew	3	2	5	1	4	-	-do-	-	0.30	-	2	-	6	-	25000
148	Blet Songthiang	1	4	5	2	3	-	-do-	-	0.20	-	-	-	8	-	25000
149	Slomina Songthiang	-	1	1	-	1	-	-do-	-	-	-	-	-	5	-	25000
150	Prothomlin K. peing	4	2	6	3	3	-	-do-	-	-	-	-	-	4	-	20000
151	Stelin Mynsong	2	2	4	1	3	-	-do-	-	-	-	1	-	3	-	15000
152	Elkin Kharumnuid	3	3	6	4	2	-	-do-	-	0.20	-	-	-	7	-	20000
153	Shanbok K. mynmai	6	3	9	6	3	-	-do-	-	0.20	-	-	1	3	-	25000
154	Dasain Kharsohnoh	1	5	6	3	3	-	-do-	-	0.50	-	1	-	6	-	20000
155	Daren Sohtun	3	5	8	2	2	-	Farmer	-	0.20	5	2	-	10	-	20000
156	Koswel Rynjah	6	1	7	5	2	-	-do-	-	0.20	-	-	-	4	-	20000
157	Kalip	4	3	7	5	2	-	-do-	-	0.50	-	1	-	-	-	25000
158	Ribhalin Lyngdoh	1	1	2	-	2	-	Teacher	-	0.20	-	-	-	-	-	20000
159	Phroly Surong	6	3	9	7	2	-	-do-	-	3.00	-	-	-	6	-	20000
160	Skim Nongrum	6	5	11	7	4	-	-do-	-	0.30	-	-	-	5	-	25000
161	Tikoswell Songthiang	2	2	4	2	2	4	-do-	-	0.70	-	-	-	3	-	100000
162	Tiswell Warjri	4	3	7	3	3	6	-do-	-	0.30	-	3	-	-	-	20000
163	Drop Nongpluh	6	5	11	7	4	4	-do-	-	0.20	-	3	-	3	-	20000
164	Lina Lyngdoh	6	1	7	3	4	-	-do-	-	-	-	2	-	-	-	25000
165	Risilia Lyngdoh	3	3	6	4	1	-	-do-	-	-	-	1	-	5	-	25000
166	Risenda Lyngdoh	3	2	5	2	3	-	-do-	-	-	-	2	-	6	-	25000
167	Ribor Nongrum	3	2	5	2	3	5	-do-		0.20	-	1	-	-	-	20000
168	Morningstar Nongrum	1	2	3	1	2	3	-do-		0.30	-	-	-	-	-	25000
169	Bringstar Nongrum	3	3	6	3	3	6	-do-		0.55	-	2	4	10	-	25000
170	Drop Suting	6	1	7	3	4	7	-do-		-	5	2	5	-	-	25000
171	Thud Nongspung	3	2	5	1	4	5	-do-		0.30	8	3		-	-	20000
172	Listar Rynjah	2	6	8	5	3	8	-do-		0.20	4	3	-	8	-	20000
173	Sirmon Nongpluh	2	5	7	3	4	7	-do-		0.20	-	-	-	4	-	15000
	TOTAL	292	242	534					-		74	117	72	314		
	<i>PDENGSHNONG</i>								-							
174	Dearlo Rynjah	4	3	7	3	4	7	-do-	-	-	-	3	-	-	-	10000
175	Kjet Rynjah	3	3	6	2	4	6	-do-	-	-	-	1	-	5	-	11000
176	Batilia Rynjah	1	1	2	1	1	2	-do-	-	-	-	2	-	6	-	9000
177	Trialinda Rynjah	1	1	2	1	1	2	-do-	-	0.20	-	1	-	-	-	8000
178	Jlian Rynjah	1	1	2	2	-	2	-do-	-	0.20	-	-	1	3	-	12000
179	Ailinda K. rymmai	4	3	7	4	3	7	-do-	-	0.50	-	1	-	6	-	12000
180	Dirontina Kharsohnoh	2	3	5	3	2	5	-do-	-	0.20	-	1	-	3	-	13000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
181	Sorilin Kharsohnoh	4	5	9	4	5	9	-do-	-	3.00	-	1	-	6	-	25000
182	Aisibon Suting	1	1	2	1	1	2	-do-	-	-	-	-	-	4	-	8000
183	Anti Suting	4	2	6	2	4	6	-do-	-	0.70	-	-	-	4	-	9000
184	Klarimon K.rymmai	3	3	6	2	4	6	-do-	-	0.30	2	2	-	6	-	10000
185	Risuklang Kharsohnoh	3	3	6	3	3	6	-do-	-	0.20	-	-	-	8	-	10000
186	Merida Kharsohnoh	3	2	5	4	1	5	-do-	-	-	-	-	-	5	-	19000
187	Darilin Kharsohnoh	1	3	4	2	2	4	-do-	-	-	-	-	-	4	-	8000
188	Dlomain Kharsohnoh	4	2	6	1	5	6	-do-	-	-	-	1	-	3	-	10000
189	Arbhilin K.rymmai	5	5	10	3	7	10	-do-	-	0.20	-	-	-	7	-	11000
190	Klida Rynjah	3	3	6	2	4	6	-do-	-	0.20	-	-	1	3	-	9000
191	Stiar Suting	4	5	9	4	5	9	-do-	-	-	-	-	-	-	-	10000
192	Khrar K.rymmai	3	4	7	1	6	7	-do-	-	-	-	-	-	-	-	11000
193	Jbian Rynjah	2	2	4	1	3	4	-do-	-	-	-	-	-	-	-	11000
194	Fultina Rynjah	1	3	4	2	2	4	-do-	-	.50	-	-	-	-	-	9000
195	Bariti Rynjah	3	2	5	2	3	5	-do-	-	.30	-	-	-	-	-	13000
196	Balahun Rynjah	1	3	4	2	2	4	-do-	-	.20	2	1	-	5	-	9000
197	Smiar Rynjah	3	4	7	2	5	7	-do-	-	0.30	-	-	3	3	-	10000
198	Thiarrimon Kharsohnoh	6	1	7	2	5	7	-do-	-	-	3	-	-	5	-	10000
199	Angela Kharmylliem	4	2	6	3	3	6	Farmer	-	1.00	-	-	-	4	-	12000
200	Phomilin Songthiang	6	6	10	7	5	10	-do-	-	-	-	3	-	6	-	20000
201	Bermon Songthiang	3	3	6	3	3	6	-do-	-	-	-	-	-	-	-	19000
202	Dlanda K.rymmai	4	5	9	2	7	9	-do-	-	-	-	1	-	3	-	10000
203	Marbilos Songthiang	1	1	2	1	1	2	-do-	-	0.40	-	-	-	7	-	8000
204	Industrial Songthiang	2	4	6	2	4	6	-do-	-	-	-	-	5	6	-	9000
205	Marbit Kharsohnoh	5	3	8	3	5	8	-do-	-	0.20	-	-	-	-	-	13000
206	Iniar Kharsohnoh	2	3	5	3	2	5	-do-	-	0.50	-	-	-	3	-	9000
207	Diarmar Kharsohnoh	2	3	5	1	4	5	-do-	-	-	2	4	-	5	-	9000
208	Kondwell Kharmylliem	4	2	6	2	4	6	-do-	-	0.20	-	3	-	8	-	13000
209	Wanbha K.rymmai	4	2	6	3	3	6	-do-	-	-	-	3	-	7	-	15000
210	Wonderful Songthiang	2	2	4	6	-	4	-do-	-	0.30	-	1	-	5	-	10000
211	Koplin Nongrum	4	4	8	5	3	8	-do-	-	1.00	-	2	-	3	-	11000
212	Iohkynti Nongrum	5	3	8	3	5	8	-do-	-	-	-	1	-	9	-	12000
213	Dearbon Kharmylliem	-	3	3	2	1	3	-do-	-	0.20	-	-	-	8	-	9000
214	Stian Kharmylliem	3	3	6	3	3	6	-do-	-	0.30	-	2	-	7	-	10000
215	Spailin Kharmylliem	1	1	2	1	1	2	-do-	-	0.40	5	3	-	5	-	8000
216	Phailin Nongrum	4	3	7	3	4	7	-do-	-	0.30	-	3	-	6	-	15000
217	Worfina Khongsngi	1	2	3	2	1	3	-do-	-	0.20	-	-	-	3	-	11000
218	Rot Nongpluh	2	4	6	2	4	6	-do-	-	0.20	-	-	1	3	-	15000
219	Kroming Rynjah	3	3	6	1	5	6	-do-	-	0.50	-	1	-	6	-	9000

1	2	3	4	5	6-	7	8	9	10	11	12	13	14	15	16	17
220	Twilsila Songthiang	3	5	8	6	2	8	-do-	-	0.20	-	1	-	3	-	13000
221	Betimon Songthiang	2	1	3	3	-	3	-do-	-	3.00	-	1	-	6	-	20000
222	Lusia Nongrum	1	1	2	1	1	2	-do-	-	-	-	-	-	4	-	9000
223	Doritsila Songthiang	3	5	8	8	-	8	-do-	-	0.70	-	-	-	4	-	14000
224	Biangmon	3	4	7	4	3	7	-do-	-	0.30	-	2	-	6	-	13000
225	Bilnadin Rynjah	1	2	3	2	1	3	-do-	-	0.20	1	-	-	8	-	9000
226	Trol Nongrum	1	-	1	-	1	1	-do-	-	-	-	-	-	5	-	8000
227	Indina Kharsohnoh	2	2	4	2	2	4	-do-	-	-	-	-	-	4	-	8000
228	Soimai Kharsohnoh	6	4	10	7	3	10	-do-	-	-	-	1	-	3	-	11000
229	Airiti Kharsohnoh	3	5	8	6	2	8	-do-	-	0.20	-	-	-	7	-	15000
230	Trolan Kharsohnoh	5	4	9	7	2	9	-do-	-	0.20	-	-	-	-	-	16000
231	Triarlinda Kharsohnoh	9	1	10	3	7	10	-do-	-	0.50	-	-	-	3	-	14000
232	Mistina Rynjah	4	5	9	5	4	9	-do-	-	-	2	4	-	5	-	17000
233	Labir Kshiar	3	2	5	3	2	5	-do-	-	0.20	-	3	-	8	-	26000
234	Endamery Rynjah	4	5	9	2	7	9	-do-	-	-	-	3	-	7	-	9000
235	Klinda Rynjah	3	3	6	2	4	6	-do-	-	0.30	-	1	-	5	-	9000
236	Malimon Songthiang	4	3	7	4	3	7	-do-	-	1.00	-	2	-	3	-	25000
237	Owen Tangsong	2	3	5	4	1	5	-do-	-	-	-	1	-	9	-	19000
238	Marlin Kharsohnoh	1	4	5	1	4	5	-do-	-	0.20	-	-	-	8	-	9000
239	Batiful Mukhim	4	5	9	-	9	9	Farmer	-	0.30	-	2	-	7	-	10000
240	Ibha Mukhim	1	1	2	1	1	2	-do-	-	0.40	5	3	-	5	-	8000
241	Poi Nongrum	3	2	5	1	4	5	-do-	-	0.30	-	3	-	6	-	10000
242	Thoda K.rymmai	4	3	7	3	4	7	-do-	-	0.20	-	-	-	-	-	10000
243	Mesiful Songthiang	1	2	3	1	2	3	-do-	-	0.50	-	-	-	3	-	11000
244	Aibrila Rynjah	2	4	6	4	2	6	-do-	-	-	2	4	-	5	-	9000
245	Sdalit Rynjah	4	8	12	7	5	12	-do-	-	0.20	5	3	-	10	-	30000
246	Armala Rynjah	2	2	4	3	1	4	-do-	-	0.20	-	-	-	4	-	10000
247	Rishisha K.rymmai	3	3	6	1	5	6	-do-	-	0.50	-	1	-	-	-	8000
248	Wanda Songthiang	2	2	4	2	2	4	-do-	-	0.20	-	-	-	-	-	10000
249	Dronda Songthiang	4	5	9	4	5	9	-do-	-	3.00	-	-	-	6	-	15000
250	Memorina Songthiang	-	1	1	1	-	1	-do-	-	0.30	-	-	-	5	-	8000
251	Iolinda Kharmylliem	1	1	2	1	1	2	-do-	-	0.70	-	-	-	3	-	8000
252	Dalimon Kharmylliem	1	1	2	2	-	2	-do-	-	0.30	-	4	-	-	-	8000
253	Motrina Rynjah	3	4	7	1	6	7	-do-	-	0.20	-	3	-	3	-	7000
254	Thrinda K.rymmai	4	2	6	2	4	6	-do-	-	-	-	3	-	-	-	10000
255	Brinbon K.rymmai	4	2	6	2	4	6	-do-	-	-	-	1	-	5	-	9000
256	Lanosha K.rymmai	3	3	6	2	4	6	-do-	-	-	-	2	-	6	-	9000
257	Klanrisha Rynjah	1	2	3	1	2	3	-do-	-	0.20	-	1	-	-	-	8000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
258	Sharbanda Rynjah	1	1	2	1	1	2	-do-	-	0.30	-	-	-	-	-	8000
259	Sirmon Nongpluh	2	4	6	2	4	6	-do-	-	0.55	-	2	4	10	-	10000
260	Aitlin Nongrum	2	3	5	4	1	5	-do-	-	-	5	3	5	-	-	13000
261	Mishida Nongrum	1	3	4	2	2	4	-do-	-	0.30	7	3	-	-	-	10000
262	Elias Songthiang	4	4	8	2	6	8	-do-	-	0.20	5	3	-	10	-	9000
263	Elbera K.Rymmai	2	1	3	1	2	3	-do-	-	0.20	-	-	-	4	-	8000
264	Spardamon K.rymmai	1	1	2	1	1	2	-do-	-	0.20	5	3	-	10	-	8000
265	Iaroh Mukhim	1	2	3	1	2	3	-do-	-	0.20	-	-	-	4	-	10000
266	Siola Kharsohnoh	2	1	3	-	3	3	-do-	-	0.50	-	1	-	-	-	7000
267	Jubina Kharsohnoh	4	4	8	1	7	8	-do-	-	0.20	-	-	-	-	-	7000
268	Rani K.rymmai	2	3	5	1	4	5	-do-	-	3.00	-	-	-	6	-	7000
269	Shimtinoris Kharsohnoh	4	2	6	1	5	6	-do-	-	-	-	-	-	-	-	8000
270	Angela Songthiang	-	3	3	1	2	3	-do-	-	-	-	-	-	-	-	15000
271	Balarihun K.rymmai	1	1	2	1	1	2	-do-	-	-	-	-	-	-	-	8000
272	Pdianghun Songthiang	1	2	3	1	2	3	-do-	-	-	-	-	-	-	-	8000
	TOTAL	267	275	544							52	105	21	400		
	<i>DONGSHLEM</i>							-do-								
273	Airalin Kharmyllem	3	8	1	3	8	11	-do-	-	-	-	3	-	-	-	16000
274	Mlibon Rynjah	2	2	4	-	4	4	-do-	1 acre	-	5	1	-	-	-	17000
275	Swinti Rynjah	5	5	10	3	7	10	-do-	¹ / ₂ acre	-	1	1	-	-	-	12000
276	Jwianda Rynjah	5	1	6	-	6	6	Farmer	-	-	-	-	-	-	-	13000
277	Shaidamon Rynjah	4	4	8	3	5	8	-do-	¹ / ₂ acre	-	-	1	-	-	-	15000
278	Istarbel Nonglyer	3	3	6	2	4	6	-do-	-	-	-	-	-	-	-	11000
279	Saphi Nonglyer	3	2	5	1	4	5	-do-	¹ / ₂ acre	-	6	1	-	-	-	16000
280	Iadalang Kharsohnoh	4	3	7	-	7	7	-do-	-	-	2	2	5	-	-	14000
281	Bertilin Nongrum	32	3	5	-	5	5	-do-	1 acre	-	7	2	-	-	-	16000
282	Blia Sohtun	3	3	6	2	4	6	-do-	-	-	-	1	-	-	-	11000
283	Landa Sohtun	5	4	9	4	5	9	-do-	-	-	-	-	-	-	-	15000
284	Stiar Sohtun	5	6	11	5	6	11	-do-	-1 acre	-	-	6	8	-	-	17000
285	Briar Kharmyllem	3	6	9	4	5	9	-do-	¹ / ₂ acre	-	-	1	-	-	-	15000
286	Thorir Suting	3	2	5	1	4	5	-do-	1 acre	-	7	1	-	-	-	16000
287	Blina Nongrum	3	4	7	2	5	7	-do-	-	-	-	-	-	-	-	11000
288	Sarada Suting	3	3	6	4	2	6	-do-	-	-	-	-	-	-	-	12000
289	Tarida Suting	2	2	4	1	3	4	-do-	-	-	-	-	-	-	-	11000
290	Sorilian Nongrum	3	4	7	2	5	7	-do-	-	-	-	5	5	-	-	16000
291	Klastu Sohtun	4	2	6	2	4	6	-do-	-	-	-	2	-	-	-	11000
292	Wantilang Kharsohnoh	5	4	9	4	5	9	-do-	1 ¹ / ₂ acre	-	5	1	-	-	-	17000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
293	Horil Rynjah	7	3	10	2	8	10	-do-	1/2 acre		-	1	6	-	-	16000
294	Marilian Nongrum	4	3	7	3	5	7	-do-	-		-	1	-	-	-	15000
295	Damera Nongrum	5	2	7	2	5	7	-do-	-		-	1	-	-	-	13000
296	Biroda Nongrum	1	3	4	1	3	4	-do-	-		-	2	-	-	-	14000
297	Drop Nongrum	5	3	8	-	8	8	-do-	1 acre		-		5	-	-	17000
298	Sibilin Rynjah	-	3	3	-	3	3	-do-	-		-		-	-	-	12000
299	Sharina Nongrum	5	3	8	2	6	8	-do-	1/2 acre		-	1	-	-	-	15000
300	Swiarda Nongrum	2	3	5	-	5	5	-do-	1/2 acre		-		-	-	-	13000
276	Bhalin Nongrum	5	1	6	2	4	6	-do-	1/2 acre		-	2	-	-	-	16000
277	Josina Songthiang	3	4	7	-	7	7	-do-	1/2 acre		-		4	-	-	16000
278	Aimirit rynjah	2	2	4	-	4	4	-do-	1 acre		1	1	10	-	-	17000
279	Aidolin Rynjah	1	2	3	-	3	3	-do-	-		-	-	-	-	-	16000
280	Shanrida Songthiang	1	1	2	-	2	2	-do-	-		-	-	-	-	-	13000
281	Mlidiar Rynjah	3	3	6	2	4	6	-do-	1/2 acre	-	2	3	9	-	-	17000
282	Krissila Suting	5	2	7	4	3	7	-do-	-	-	-	1	-	-	-	13000
283	Klorita Nongrum	3	3	6	2	4	6	-do-	1 acre	-	-		-	-	-	14000
284	Jril Suting	1	1	2	-	2	2	-do-	1/2 acre	-	-	1	-	-	-	12000
285	Jarbon Suting	5	4	9	-	9	9	-do-	-	-	-		-	-	-	11000
286	Mikrin Suting	1	3	4	-	4	4	-do-	-	-	2	1	-	-	-	15000
287	Bhamon Nongpluh	2	5	7	2	5	7	-do-	-	-	-	1		-	-	14000
288	Norila Suting	5	6	11	2	9	11	-do-	1 acre	-	2	8	10	-	-	17000
289	Darity Rynjah	4	4	8	2	6	8	-do-	1 acre	-	-	1	-	-	-	16000
290	Sorilian Rynjah	7	6	13	3	10	13	Farmer	1 1/2 acre	-	-	1	-	-	-	15000
291	Praida Suting	5	6	11	2	9	11	-do-	1 acre	-	5	-	-	-	-	14000
292	Alian Kharmylliem	5	8	13	5	8	13	-do-	-	-		-	-	-	-	16000
293	Ridashisha Rynjah	3	1	4	-	4	4	-do-	1/2 acre	-	3	5	5	-	-	13000
294	Iohieid Songthiang	2	3	5	2	3	5	-do-	-	-	-	1		-	-	15000
295	Rijied Songthiang	3	2	5	3	2	5	-do-	1 acre	-	-		50	-	-	17000
296	Riberty Nongrum	4	4	8	1	7	8	-do-	-	-	-	1	2	-	-	12000
297	Martilian Rynjah	4	7	11	3	8	11	-do-	-	-	-	1	-	-	-	16000
298	Jwelín Kharsohnoh	5	5	10	3	7	10	-do-	1 acre	-	1	2	-	-	-	17000
299	Khina Suting	4	3	7	2	5	7	-do-	-	-	-	1	4	-	-	15000
300	Kronti Suting	4	3	7	-	7	7	-do-	1/2 acre	-	-	-	-	-	-	13000
301	Mondahun Kharsohnoh	3	22	5	2	3	5	-do-	-	-	-	-	-	-	-	12000
302	Sherlin Nongrum	1	5	6	3	3	6	-do-	1/2 acre	-	-	-	-	-	-	13000
303	Pasilin Nongrum	1	2	3	1	2	3	-do-	1/2 acre	-	-	-	-	-	-	12000
304	Iarlinda Nongrum	3	1	4	2	2	4	-do-	1/2 acre	-	-	-	-	-	-	12000
305	Phlora Nongrum	2	5	7	5	2	7	-do-	1 acre	-	6	12	5	10	-	20000
306	Priel Nongrum	1	1	2	1	1	2	-do-	1 acre	-	-	-	-	-	-	12000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
307	Rilang Lyngdoh	2	2	4	2	2	4	-do-	1 acre	-	-	-	-	-	-	14000
308	Lesir Lyngdoh	-	2	2	1	1	2	-do-	1 acre	-	-	-	-	-	-	12000
309	Drotsibon Lyngdoh	1	1	2	2	-	2	-do-	1 acre	-	-	3	-	-	-	14000
310	Stiarbon Lyngdoh	4	3	7	2	5	7	-do-	1½ acre	-	-	-	12	-	-	12000
311	Aiti Lyngdoh	1	3	4	2	2	4	-do-	1½ acre	-	-	-	-	-	-	12000
312	Mela K.rymmai	3	3	6	4	2	6	-do-	1 acre	-	-	4	-	18	-	20000
313	Tngenlang K.rymmai	1	2	3	1	2	3	-do-	1½ acre	-	-	-	-	-	-	12000
314	Rihunlang K.rymmai	3	2	5	2	3	5	-do-	1½ acre	-	-	-	-	-	-	14000
	TOTAL	212	217	429							55	84	140	28		
	<i>NONGSHILLIANG</i>															
315	Blahun Nongrum	2	1	3	1	2	3	-do-	1½ acre	-	-	-	-	-	-	9000
316	Phril Suting	1	3	4	1	3	4	-do-	3 acre		3			15	-	14000
317	Phori Suting	3	2	5	2	3	5	-do-	1½ acre	-	-	-			-	12000
318	Rosphina Nongkhlaw	3	3	6	2	3	5	-do-	1 acre	-	-	-	8	30	-	16000
319	Karmon Nongrum	3	4	7	2	3	5	-do-	1 acre	-	-	-			-	14000
320	Nobar Suting	3	7	10	2	3	5	Farmer	1 acre	-	-	3	-	-	-	14000
321	Kongheh Rynjah	2	1	3	1	1	2	-do-	1 acre	-	-	-	-	-	-	10000
322	Klorida Rynjah	3	2	5	2	3	5	-do-	2 acre	-	7	-	5	-	-	16000
323	Raw Nongrum	1	2	3	1	1	2	-do-	1½ acre	-	-	-	-	-	-	14000
324	Ritjarain Songthiang	2	1	3	1	1	2	-do-	1½ acre	-	-	-	-	-	-	12000
325	Bral Suting	3	-	3	1	2	3	-do-	2 acre	-	8	-	-	-	-	14000
326	Phirit Rynjah	2	1	3	1	2	3	-do-	1 acre	-	-	-	-	-	-	10000
327	Theilin Kharbihkhiew	5	4	9	4	5	9	-do-	1½ acre	-	-	3	-	15	-	15000
328	Mom Suring	2	4	6	2	3	5	-do-	-	-	-	4	20	-	-	16000
329	Theiplin	4	3	7	2	3	5	-do-	1 acre	-	-	3	-	10	-	18000
330	Norin Songthiang	2	3	5	2	1	3	-do-	2 acre	-	-	-	-	15	-	18000
331	Pan Songthiang	4	2	6	2	2	4	-do-	3 acre	-	-	-	12	15	-	16000
332	Khwin Kharmyllem	6	3	9	1	3	4	-do-	4 acre	-	10	4	-	-	-	15000
333	Krolinda Sohtun	2	3	5	1	1	2	-do-	1 acre	-	3		-	20	-	14000
334	Kerlinda Kharsohnoh	3	2	5	2	3	5	-do-	1 acre	-		2	-	5	-	10000
335	Shatilang Kharmyllem	3	3	6	1	1	2	-do-	2 acre	-	3	1	-	5	-	14000
336	Lumlynti Kharumnuid	1	1	2	-	-	-	-do-	1½ acre	-	2	-	-	3	-	12000
337	Shidalin Kharsohnoh	2	2	4	2	2	4	-do-	1 acre	-	-	-	-		-	12000
338	Khamtilang Kharsohnoh	1	2	3	1	1	2	-do-	2 acre	-	-	-	8	15	-	10000
339	Spai Kharumnuid	2	2	4	1	1	2	-do-	4 acre	-	-	-	-	-	-	15000
340	Mortimai Mynsong	2	1	3	-	1	1	-do-	-	-	-	-	-	-	-	10000
341	Twensi Kharumnuid	3	3	6	1	2	3	-do-	1½ acre	-	-	-	-	-	-	16000
342	Batimon Kharumnuid	5	3	8	1	2	3	-do-	1½ acre	-	-	-	-	-	-	15000
343	Daiona Kharumnuid	5	3	8	3	2	5	-do-	1½ acre	-	-	-	10	40	-	16000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
344	Wanhun Kharumnuid	1	3	4	1	-	1	-do-	$\frac{1}{2}$ acre	-	6	-	-	15	-	15000
345	Phrial Kharumnuid	2	2	4	1	1	2	-do-	$\frac{1}{2}$ acre	-	14	-	-	15	-	16000
346	Wanlet Kharumnuid	1	-	1	-	-	-	-do-	$\frac{1}{2}$ acre	-	-	-	-	-	-	8000
347	Dyiar Kharumnuid	3	2	5	-	-	-	-do-	$\frac{1}{2}$ acre	-	-	2	-	10	-	14000
348	Ainola Kharmylliem	3	2	5	1	-	1	-do-	$\frac{1}{2}$ acre	-	-	1	7	5	-	12000
349	Pralin Nongkynrih	6	3	9	1	3	4	-do-	2 acre	-	5	-	-	-	-	16000
350	Salin Kharsohnoh	3	4	7	2	-	2	-do-	1 acre	-	-	-	10	-	-	17000
351	Phulnes Kharsahnoh	1	1	2	-	-	-	-do-	$\frac{1}{2}$ acre	-	-	-	-	-	-	10000
352	Raptilang Kharsahnoh	3	1	4	1	3	4	-do-	$\frac{1}{2}$ acre	-	1	-	-	-	-	9000
353	Kralin Warjri	3	5	8	2	3	5	-do-	3 acre	-	2	2	-	5	-	13000
354	Twonda Warjri	2	3	5	1	1	2	-do-	$\frac{1}{2}$ acre	-	-	1	-	3	-	12000
355	Armera Kharmylliem	2	1	3	1	1	2	-do-	-	-	-	-	-	-	-	10000
356	Bharina Kharmylliem	2	2	4	-	-	-	-do-	$\frac{1}{2}$ acre	-	-	-	3	3	-	12000
357	Dlina Kharmylliem	5	3	8	1	2	3	-do-	$\frac{1}{2}$ acre	-	-	-	4	2	-	13000
358	Mela Kharmylliem	3	2	5	1	2	-	-do-	1 acre	-	-	3	4	5	-	15000
359	Mastar Kharmylliem	1	-	1	-	-	-	-do-	1 acre	-	-	-	-	-	-	8000
360	Brota Nongrum	2	3	5	1	3	4	Farmer	$\frac{1}{2}$ acre	-	-	-	-	-	-	17000
361	Silit Warjri	-	1	1	-	-	-	-do-	2 acre	-	-	-	-	20	-	15000
362	Shimti Kharsahnoh	1	3	4	2	1	3	-do-	-	-	-	-	-	-	-	9000
363	Jloit Sohtun	4	2	6	1	2	3	-do-	2 acre	-	7	-	-	6	-	12000
364	Natrit Sohtun	4	3	7	1	3	4	-do-	4 acre	-	13	-	-	-	-	18000
365	Kishmel Sohtun	1	2	3	1	1	2	-do-	-	-	-	-	-	-	-	12000
366	Sorbiliang Nonglyer	2	4	6	2	4	6	-do-	$\frac{1}{2}$ acre	-	-	2	-	-	-	16000
367	Merinda Kharsahnoh	2	2	4	1	-	4	-do-	$\frac{1}{2}$ acre	-	-	2	-	-	-	14000
368	Belin Khongmalai	3	3	6	1	5	6	-do-	-	-	-	-	-	-	-	12000
369	Nibelles Kharsahnoh	2	4	6	3	1	4	-do-	$\frac{1}{2}$ acre	-	-	2	-	20	-	15000
370	Stailinda Nonglyer	1	1	2	-	2	2	-do-	-	-	-	-	-	-	-	12000
371	Sarbina Nonglyer	2	3	5	1	3	4	-do-	3 acre	-	-	-	-	-	-	15000
372	Nolis Nongkhlaw	2	3	5	1	3	4	Farmer	1 acre	-	-	-	-	-	-	13000
373	Aibilian Nongkhlaw	6	1	7	2	3	5	-do-	1 acre	-	-	2	8	-	-	16000
374	Brasilin Kharmullieh	4	3	7	3	2	5	-do-	1 acre	-	-	-	-	-	-	16000
375	Nohtilang Nongrum	2	1	3	1	2	3	-do-	-	-	-	-	-	-	-	12000
376	Dahun Kharsahnoh	2	1	3	1	1	2	-do-	1 acre	-	-	-	-	-	-	8000
377	Sonia Kharumnuid	1	1	2	1	1	2	-do-	-	-	-	-	-	-	-	10000
378	Aitimon Nonglyer	4	1	5	1	3	4	-do-	$\frac{1}{2}$ acre	-	-	-	-	-	-	15000
379	Ilisha Kharmylliem	5	2	7	2	2	4	-do-	$\frac{1}{2}$ acre	-	2	-	-	-	-	16000
380	Blenti Kharmulieh	5	2	7	2	1	3	-do-	$\frac{1}{2}$ acre	-	-	-	-	-	-	14000
381	Isrel Kharmulieh	4	3	7	2	2	4	-do-	$\frac{1}{2}$ acre	-	-	-	-	-	-	16000
382	Toris Kharbyngar	2	2	4	1	1	2	-do-	1 acre	-	4	-	-	-	-	15000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
383	Mili Kharsahnoh	3	2	5	2	3	5	-do-	1 acre	-	10	-	-	10	-	18000
384	Kjoin Nongkynrih	2	3	5	1	4	5	-do-	3 acre	-	8	-	-	16	-	16000
385	Tngenlang Nongkynrih	2	1	3	-	3	3	-do-	1 acre	-	9	-	-	12	-	14000
386	Shardahun Nongrum	2	2	4	1	3	4	-do-	1/2 acre	-		-	-	7	-	15000
387	Nancy Nongrum	4	2	6	2	4	6	-do-	1 acre	-		-	-	8	-	16000
388	Dro Nongrum	4	2		3		6	-do-	2 acre	-	9	-	-	6	-	12000
389	Risuklang Nongrum	2	3	5	1	4	5	-do-	1/2 acre	-	-	-	-	-	-	12000
390	Twency Nongrum	1	3	4	-	4	4	-do-	1/2 acre	-	-	1	6	-	-	1000
391	Maria Nongrum	3	1	4	1	3	4	-do-	1/2 acre	-	-	3	6	4	-	12000
392	Ribansuk Nongpluh	1	2	3	-	3	3	-do-	-	-	-	-	-	-	-	8000
393	Baiarlin Nongpluh	2	4	6	-	6	6	-do-	-	-	-	-	-	-	-	8000
394	Dril Nongpluh	2	2	4	-	4	4	-do-	2 acre	-	-	-	-		-	12000
395	Elip Nongpluh	3	2	5	-	5	5	-do-	4 acre	-	18	5	6	12	-	18000
396	Trophy Kharsohnoh	1	3	4	2	2	4	-do-	1 acre	-	6	3	-	10	-	15000
397	Dra Kharsahnoh	2	6	8	5	3	8	-do-	3 acre	-	-	3	-	8	-	18000
398	Ribhailin Kharsahnoh	1	4	5	5	-	5	-do-	2 acre	-	-	-	10	8	-	16000
399	Ro Nongrum	1	2	3	1	2	3	-do-	1 acre	-	6	2	-	-	-	15000
	TOTAL	219	201	420						-	156	54	127	404		
	WAHSHNONG															
400	Ailibon Kharmylliem	6	4	10	2	8	10	Farmer	1 acre	-	6	1	20	20	-	8000
401	Phorsibon Kharmylliem	1	3	4	1	3	4	-do-	1 acre	-	4	1	-	10	-	6000
402	Elisha Kharmylliem	2	5	7	1	6	7	-do-	1/2 acre	-	3	-	-	-	-	3000
403	Tngenda Kharbyngar	1	2	3	-	3	3	-do-	-	-	1	-	-	-	-	3000
404	Thron Kharmylliem	1	4	5	2	3	5	-do-	1/2 acre	-	-	-	-	-	-	4000
405	Basuklang Kharmylliem	1	3	4	-	4	4	-do-	1/2 acre	-	-	-	-	10	-	3000
406	Baaihunlang Kharmylliem	4	5	9	3	6	9	-do-	-	-	-	1	-	15	-	4000
407	Regina Kharmylliem	3	5	8	3	5	8	-do-	1/2 acre	-	1	-	-	-	-	4000
408	Orbilin Kharmylliem	4	2	6	1	5	6	-do-	1 acre	-	8	1	-	-	-	6000
409	Ribilin Kharmylliem	3	3	6	-	6	6	-do-	1/2 acre	-	6	1	10	6	-	5000
410	Aibilin Kharmylliem	1	3	4	-	4	4	-do-	1/2 acre	-	4	2	-	5	-	4000
411	Rikynti Kharmylliem	3	1	4	-	4	4	-do-	1/2 acre	-	1	-	-	-	-	3000
412	Riphilin Kharmylliem	4	1	5	-	5	5	-do-	-	-	1	-	-	6	-	3000
413	Sarbetstar K.rymmai	2	2	4	-	4	4	-do-	-	-	2	-	-	-	-	3000
414	Maham Kharmylliem	1	-	1	-	-	2	-do-	-	-	-	-	-	-	-	3000
415	Shatiak Kharmylliem	1	-	1	-	-	-	-do-	-	-	-	-	-	-	-	3000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
416	Sbiat Kharmuti	1	5	6	-	6	6	-do-		-	-	-	-	-	-	3000
417	Wiang Nongrum	3	2	5	1	4	5	-do-	1 acre	-	8	1	-	30	-	6000
418	Ila Nongrum	3	2	5	-	5	5	-do-	½ acre	-	9	2	16	-	-	4000
419	Ritamom K.rymmai	2	2	4	2	2	4	-do-	-	-	-	-	-	-	-	3000
420	Iorlinda K.rymmai	1	4	5	3	2	5	-do-	-	-	-	-	-	-	-	3000
421	Kneh Nongrum	3	7	10	1	9	10	-do-	½ acre	-	-	1	-	-	-	3000
422	Phlaris Sohtun	2	3	5	1	4	5	-do-	½ acre	-	8	-	-	-	-	4000
423	Daialin Kharsahnoh	3	2	5	1	5	5	-do-	-	-	-	-	-	-	-	3000
424	Skelinda Kharsahnoh	1	1	2	1	1	2	-do-	½ acre	-	-	-	-	-	-	4000
425	Nangphyrnai Kharmylliem	2	4	6	1	5	6	-do-	½ acre	-	-	-	-	-	-	3000
426	Kwirmon Nongpluh	3	2	5	2	3	5	-do-	-	-	-	-	-	-	-	3500
427	Kromon Nongpluh	1	3	4	-	4	4	-do-	½ acre	-	-	-	-	-	-	3000
428	Nobila Nongpluh	2	1	3	1	2	3	-do-	-	-	-	-	-	-	-	3000
429	Triainila Kharmylliem	2	5	7	2	5	7	-do-	½ acre	-	-	4	-	-	-	3500
430	Kiarda Kharmylliem	2	1	3	1	2	3	-do-	½ acre	-	-	1	-	-	-	3000
431	Kther Kharmylliem	4	2	6	1	5	6	-do-	½ acre	-	-	-	7	-	-	3000
432	Tiewlibel Kharmylliem	1	2	3	1	2	3	-do-	½ acre	-	9	1	-	-	-	3000
433	Sarilian Kharmylliem	3	5	8	-	8	8	-do-	-	-	4	3	-	6	-	3000
434	Saris Kharsahnoh	1	2	3	1	2	3	-do-	1 acre	-	6	-	-	-	-	6000
435	Shila Kharmylliem	2	8	10	1	9	10	-do-	-	-	-	-	-	-	-	4000
436	Donbor Kharsahnoh	1	-	1	-	1	1	-do-	-	-	2	-	-	-	-	3000
437	Blona Sohtun	1	1	2	-	2	2	-do-	½ acre	-	-	1	-	-	-	4000
438	Lisida Sohtun	1	6	7	-	-	7	-do-	-	-	-	-	2	-	-	3000
439	Melnit Nongpluh	3	4	7	-	7	7	-do-	-	-	-	-	-	-	-	3000
440	Kristila Nongpluh	3	2	5	-	5	5	-do-	-	-	3	-	-	-	-	4000
441	Twonsy Kharsahnoh	1	2	3	1	2	3	-do-	-	-	-	-	-	-	-	3000
442	Dlinda Kharsahnoh	5	3	8	-	8	8	-do-	-	-	4	-	10	-	-	4000
443	Mahajon Kharsahnoh	1	-	1	-	1	1	-do-	½ acre	-	-	-	-	-	-	3000
445	Bhashisha Nongkhlaw	1	1	2	1	1	2	-do-	-	-	-	1	-	-	-	3000
446	Dripsila Kharsahnoh	3	5	8	2	6	8	-do-	1 acre	-	7	1	-	13	-	8000
447	Bhantimon Nongkkhlaw	1	2	3	-	3	3	-do-	-	-	-	-	-	-	-	3000
448	Sphairin Kharmylliem	2	7	9	3	6	9	-do-	1 acre	-	6	1	-	-	-	10000
449	Nirin Kharmylliem	3	6	9	2	7	9	-do-	½ acre	-	5	1	-	-	-	8000
450	Sita Nongpluh	9	2	11	2	9	11	-do-	1 acre	-	8	-	-	-	-	10000
451	Horimai Kharmylliem	1	3	4	-	4	4	-do-	-	-	-	-	-	-	-	3000
452	Makrin Kharmylliem	2	3	5	1	4	5	-do-	½ acre	-	4	2	-	-	-	8000
453	Lahunlang Kharmylliem	1	1	2	-	2	2	-do-	-	-	-	-	-	-	-	3000
454	Baralin Kharbyngar	3	3	6	-	-	6	-do-	1 acre	-	5	1	-	-	-	7000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
455	Sinora Kharbyngar	2	1	3	-	3	3	-do-	-	-	-	-	-	-	-	3000
456	Pharmera K harbyngar	1	2	3	-	3	3	-do-	-	-	-	-	-	-	-	3000
457	Damoris Kharbyngar	3	4	7	-	7	7	-do-	-	-	4	-	-	-	-	4000
458	Wanshisha Kharmylliem	3	2	5	-	5	5	-do-	-	-	-	-	-	-	-	3000
459	Thirda Nongkkhlaw	2	5	7	1	6	7	-do-	-	-	-	1	-	6	-	4000
460	Sabina Nongkkhlaw	3	1	4	-	4	4	-do-	-	-	-	-	-	-	-	3000
461	Kidalin Nongkkhlaw	1	1	2	-	2	2	-do-	-	-	-	-	-	-	-	3000
462	Maidalin Nongkkhlaw	1	2	3	-	3	3	-do-	-	-	-	-	-	-	-	3000
463	Rophilin Nongkkhlaw	2	2	4	-	4	4	-do-	-	-	-	-	-	-	-	3000
464	Aimon Nongkkhlaw	6	5	11	-	11	11	-do-	-	-	-	-	-	-	-	3000
465	Nirit Nongkkhlaw	2	4	6	1	5	6	-do-	½ acre	-	-	1	-	-	-	4000
466	Skalada Nongkkhlaw	1	3	4	-	4	4	-do-	-	-	-	-	-	-	-	3000
467	Kongbih Nongkkhlaw	7	2	9	1	8	9	-do-	1 acre	-	-	-	-	-	-	4000
468	Ynda Kharmylliem	1	2	3	-	3	3	-do-	½ acre	-	2	2	-	10	-	3000
	TOTAL	157	193	350						-	135	30	66	137		
	GRAND TOTAL	1326	1349	2675							513	479	490	1552		

SOCIO – ECONOMIC DATA OF LAITKYRHONG VILLAGE UNDER UMPRAH WATERSHED – I

Sl No	Name of the Head of the Family	Population			Literacy			Occupation	Agriculture Area		Livestock					Annual Income
		Male	Female	Total	Literate	Illiterate	Total		Settled	Bun	Cow	Pig	Goat	Poultry	Horse	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
1	Dapbhalang Nongkhlaw	1	2	3	3	-	3	Farmer	-	0.20	-	-	-	-	-	10000
2	Aitihun Nongkhlaw	1	5	6	5	1	6	-do-	-	0.20	-	2	-	-	-	9800
3	Tilin Rynjah	1	3	4	-	4	4	-do-	-	0.30	-	-	-	-	-	11000
4	Bitsirial Buhphang	2	2	4	3	1	4	-do-	-	1.00	-	2	-	-	-	8000
5	Tri Buhphang	1	1	2	-	2	2	-do-	-	1.00	-	-	-	-	-	9000
6	Latina Buhphang	1	2	3	2	1	3	-do-	-	0.30	-	-	-	3	-	8500
7	Tiiorian Nongkynrih	1	4	5	3	2	5	-do-	-	0.20	3	-	-	5	-	10000
8	Dilinsinta Nongkynrih	2	4	6	3	3	6	-do-	-	-	-	-	-	4	-	8000
9	Pynskhemlang Nongkynrih	1	2	3	1	2	3	-do-	-	-	-	-	-	6	-	8500
10	Ledina Rynjah	4	1	5	2	3	5	-do-	-	0.40	-	3	-	-	-	12000
11	Lona Pyngrope	4	6	10	7	3	10	-do-	-	0.20	-	-	-	3	-	10000
12	Kwilinda Nongrum	1	2	3	2	1	3	-do-	-	0.50	-	1	-	7	-	8000
13	Ainelia Nongrum	2	3	5	2	3	5	-do-	-	-	-	-	-	6	-	9000
14	Jorisia Nongrum	1	6	7	4	3	7	-do-	-	0.20	-	-	-	-	-	8500
15	Dhila Pyngrope	4	1	5	2	3	5	-do-	-	0.40	-	-	-	3	-	9200
16	Linrida Nongkynrih	3	3	6	4	2	6	-do-	-	0.30	2	-	-	5	-	9500
17	Uphibon Nongkynrih	4	2	6	2	4	6	-do-	-	1.00	-	4	-	8	-	13000
18	Rihunlang Nongkynrih	1	3	4	3	1	4	-do-	-	-	-	3	-	7	-	9000
19	Liansida Nongkynrih	2	7	9	5	4	9	-do-	-	0.20	-	3	-	5	-	10000
20	Thitsida Nongkynrih	3	3	6	4	2	6	-do-	-	0.30	-	1	-	3	-	11000
21	Misida Nongkynrih	2	2	4	3	1	4	-do-	-	0.40	-	2	-	9	-	9000
22	Dretsweel Kurkalang	5	4	9	6	3	9	-do-	-	0.30	-	1	-	8	-	9500
23	Banrilin Nongkynrih								-	-	-	-	-		-	
24	Saila Rynjah	5	4	9	7	2	9	-do-	-	1.00	5	2	-	5	-	10200
25	Malkina Rynjah	1	1	2	-	2	2	-do-	-	0.20	-	3	-	6	-	11000
26	Bilinda Rynjah	6	4	10	8	2	10	-do-	-	0.40	-	3	-	7	-	12000
27	Phrisibon Pyngrope	3	2	5	4	1	5	-do-	-	0.40	2	3	-	7	-	13000
28	Aijingtngen Pyngrope	2	1	3	2	1	3	-do-	-	-	-	1	-	3	-	9000
29	Animai Pyngrope	4	5	9	6	3	9	-do-	-	1.00	-	3	-	9	-	14000
30	Shamera Pyngrope	4	3	7	5	2	7	-do-	-	5.00	-	2	-	4	-	17000
31	Pridian Myllem	2	2	4	2	2	4	-do-	-	0.60	2	2	-	5	-	11000
32	Dabilin Myllem	3	3	6	4	2	6	-do-	-	0.30	-	3	-	7	-	10000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
33	Rishailang Myllem	1	3	4	3	1	4	Farmer	-	0.20	-	-	-	6	-	9000
34	Phaida Myllem	4	3	7	4	3	7	-do-	-	0.20	-	-	-	-	-	10000
35	Shngie Nongkynrih	5	3	8	7	1	8	-do-	-	0.60	4	3	-	6	-	15000
36	Iela Nongkynrih	4	2	6	6	-	6	-do-	-	0.30	-	2	-	10	-	13000
37	Riskhemlang Nongkynrih	1	3	4	3	1	4	-do-	-	-	-	-	-	-	-	9000
38	Airisha Nongkynrih	2	2	4	2	2	4	-do-	-	-	-	-	-	-	-	8000
39	Dashisha Nongkynrih	1	1	2	2	-	2	-do-	-	-	-	-	-	-	-	18000
40	Daphisha Nongkynrih	1	2	3	2	1	3	-do-	-	-	-	-	-	-	-	11000
41	Tasi Kharumnuid	4	2	6	5	1	6	-do-	-	0.40	-	-	-	-	-	10000
42	Iarlin Kharumnuid	4	3	7	7	-	7	-do-	-	1.00	-	2	-	4	-	15000
43	Pyndaplang Kharumnuid	1	1	2	2	-	2	-do-	-	-	-	-	-	-	-	11500
44	Winalis Nongkynrih	3	3	6	5	1	6	-do-	-	0.20	2	3	-	5	-	11000
45	Tritsila Rynjah	2	4	6	4	2	6	-do-	-	0.60	-	2	-	6	-	14000
46	Laburomshisha Rynjah	7	1	8	5	3	8	-do-	-	0.70	-	2	-	6	-	13500
47	Aromsi Nongkynrih	4	3	7	4	3	7	-do-	-	0.85	-	2	3	4	-	12500
48	Phral Nongkynrih	1	-	1	-	1	1	-do-	-	-	-	-	-	-	-	10000
49	Iarap Rynjah	-	1	1	-	1	1	-do-	-	0.20	-	-	-	3	-	7500
50	Blidia Rynjah	2	3	5	5	-	5	-do-	-	-	-	-	-	3	-	8500
51	Blitia Rynjah	5	3	8	7	1	8	-do-	-	-	-	-	-	-	-	10000
52	Kyntiewlang Myllem	3	2	5	4	1	5	-do-	-	0.20	-	2	-	4	-	10000
53	Rikyntilang Myllem	2	2	4	2	2	4	-do-	-	0.20	-	-	-	3	-	11000
54	Badariti Nongkynrih	3	1	4	4	-	4	-do-	-	0.50	-	2	5	6	-	12000
55	Metartin Nongkyhih	2	1	3	2	1	3	-do-	-	0.20	-	-	-	-	-	9000
56	Brailin Khyriem	5	4	6	8	1	9	-do-	-	3.00	-	2	-	6	-	16000
57	Wandalang Khyriem	2	1	3	2	1	3	-do-	-	-	-	-	-	-	-	8000
58	Lasi Khyriem	4	6	10	8	2	10	-do-	-	0.70	4	2	-	7	-	12000
59	Mediar Khyriem	1	4	5	3	2	5	-do-	-	0.30	-	1	-	5	-	10000
60	Modial Khyriem	1	3	4	3	1	4	-do-	-	0.20	-	2	-	4	-	11000
61	Shailinda Khyriem	2	1	3	2	1	3	-do-	-	-	-	-	-	-	-	9000
62	MarlindaKhyriem	2	1	3	2	1	3	-do-	-	-	-	-	-	-	-	8000
63	Naphirin Khyriem	1	4	5	3	2	5	-do-	-	-	-	2	-	4	-	10000
64	Sairabalin Myllem	5	5	10	8	2	10	-do-	-	0.20	5	2	-	6	-	11000
65	Klorial Kharumnuid	4	7	11	10	1	11	-do-	-	0.30	-	2	-	4	-	13000
66	Shim Nongkynrih	7	2	9	8	1	9	-do-	-	0.55	-	2	-	-	-	12000
67	Bat Nongkynrih	-	1	1	1	-	1	-do-	-	-	-	-	-	-	-	8000
68	Kbian Kharkongor	5	3	8	5	3	8	-do-	-	0.30	-	-	1	2	-	10000
69	Bislinda Kharkongor	4	4	8	7	1	8	-do-	-	0.20	-	2	-	4	-	10000
70	Bradsila Myllem	3	6	9	8	1	9	-do-	-	2.00	4	-	-	5	-	16000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
71	Tredsli Nongrum	3	1	4	4	-	4	-do-	-	0.30	1	2	-	2	-	12000
72	Brien Rynjah	1	2	3	3	-	3	-do-	-	2.00	-	4	-	3	-	13000
73	Sidamon Rynjah	3	1	4	2	2	4	-do-	-	0.20	-	1	-	3	-	8000
74	Phidamon Rynjah	1	3	4	2	2	4	-do-	-	0.30	-	2	-	2	-	9000
75	Yud Myllem	5	4	9	8	1	9	-do-	-	0.40	-	3	-	3	-	12000
76	Khettribalin Myllem	3	2	5	4	1	5	-do-	-	0.20	-	-	-	2	-	10000
77	Thritina Myllem	1	2	3	3	-	3	-do-	-	1.00	1	-	-	2	-	16000
78	Wandashisha khyriem	2	5	7	6	1	7	-do-	-	0.20	-	1	-	-	-	10000
79	Phiar Khyriem	2	2	4	2	2	4	-do-	-	1.00	-	2	-	-	-	13000
80	Haidamon Khyriem	3	3	6	5	1	6	-do-	-	-	-	2	-	5	-	10000
81	Lerin Khyriem	6	3	9	8	1	9	Farmer	-	0.40	5	3	-	-	-	14000
82	Sidralin Khyriem	2	3	5	5	-	5	-do-	-	-	-	2	-	4	-	10000
83	Bilda Khyriem	2	3	5	3	2	5	-do-	-	3.00	8	-	-	6	-	14000
84	Kyntiewribha Khyriem	4	2	6	4	2	6	-do-	-	0.20	-	-	-	4	-	9000
85	Lanehbha Nongkynrih	1	7	8	6	2	8	-do-	-	0.30	-	-	-	4	-	9500
86	Phalin Nongkynrih	3	2	5	4	1	5	-do-	-	0.80	-	2	-	6	-	10000
87	Balumlang Nongkynrih	1	5	6	4	2	6	-do-	-	0.20	-	-	-	2	-	8000
88	Pynshailang Nongkynrih	3	2	5	4	1	5	-do-	-	0.20	-	-	-	4	-	10000
89	Dariphi Khongsngi	3	4	7	7	-	7	-do-	-	0.40	-	3	-	5	-	10000
90	Linda Khaongsngi	2	1	3	2	1	3	-do-	-	0.20	-	1	-	3	-	8000
91	Shom Nongrum	7	2	9	2	7	9	-do-	-	1.00	-	1	-	-	-	12000
92	Blasida Nongrum	3	7	10	9	1	10	-do-	-	0.40	-	-	-	3	-	11000
93	Warm Nongrum	-	2	2	1	1	2	-do-	-	0.30	-	-	-	-	-	8000
94	Philida Nongrum	5	8	13	12	1	13	-do-	-	0.30	-	2	-	-	-	13000
95	Som Nongrum	2	2	4	2	2	4	-do-	-	1.00	5	2	4	5	-	12000
96	Shitabon Nongkynrih	7	3	10	8	2	10	-do-	-	0.30	-	-	-	-	-	10000
97	Bihthei Nongkynrih	2	3	5	4	1	5	-do-	-	0.40	-	2	30	10	-	12000
98	Rida Nongkymrih	4	5	9	8	1	9	-do-	-	0.30	-	2	5	4	-	9000
99	Kyiontila Khongsngi	4	2	6	4	2	6	-do-	-	0.40	5	2	-	-	-	13000
100	Blateimon Khongsngi	2	3	5	4	1	5	-do-	-	0.20	-	1	-	-	-	10000
101	Batteimon Khongsngi	2	2	4	3	1	4	-do-	-	0.30	-	-	-	6	-	11000
102	Blarina Khongsngi	5	2	7	6	1	7	-do-	-	0.40	-	2	-	5	-	13000
103	Jngip Nongkynrih	1	2	3	2	1	3	-do-	-	0.30	1	2	-	3	-	10000
104	Philitsita Nongkynrih	3	4	7	5	2	7	-do-	-	0.20	-	-	-	-	-	8000
105	Milsila Nongkynrih	4	2	6	5	1	6	-do-	-	0.30	-	-	-	3	-	8000
106	Jngop Nongkynrih	3	3	6	5	1	6	-do-	-	0.40	-	2	-	-	-	10000
107	Lapynshailin Nongkynrih	1	2	3	2	1	3	-do-	-	-	-	-	-	5	-	9000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
108	Sngiarbon Nongkynrih	1	5	6	5	1	6	-do-	-	0.40	5	-	-	6	-	11000
109	Merial Kurkalang	2	9	11	9	2	11	-do-	-	0.50	7	2	-	-	-	14000
110	Kril Kurkalang	2	2	4	2	2	4	-do-	-	0.70	6		-	-	-	13000
111	Thoni Myllem	2	2	4	4	-	4	-do-	-	0.85	4	3	-	10	-	12000
112	Menoris Myllem	2	1	3	2	1	3	-do-	-	0.20	-	-	-	-	-	10000
113	Sitngenlang Myllem	1	3	4	2	2	4	-do-	-	0.20	-	-	-	-	-	10000
114	Lela Rynjah	9	2	11	10	1	11	-do-	-	0.50	-	3	-	4	-	13000
115	Nanda Rynjah	3	1	4	3	1	4	-do-	-	0.30	-	2	-	6	-	10000
116	Saramon Khongsngi	5	1	6	5	1	6	-do-	-	0.30	-	-	-	2	-	10000
117	Ailinda khongsngi	3	4	7	7	-	7	-do-	-	0.40	4	2	-	-	-	12000
118	Tibhalin Khongsngi	1	3	4	3	1	4	-do-	-	0.20		-	-	-	-	10000
119	Rildian Khongsngi	4	3	7	7	-	7	-do-	-	0.50	3	-	-	-	-	13000
120	Aisilian Kurkalang	5	8	13	12	1	13	-do-	-	0.40	-	2	-	-	-	12000
121	Airialsi Kurkalang	3	4	7	6	1	7	Farmer	-	0.40	-	-	-	-	-	10000
122	Naphilian Kurkalang	3	2	5	4	1	5	-do-	-	0.50	-	-	-	5	-	13000
123	Dabianglin Kurkalang	1	2	3	3	-	3	-do-	-	0.20	-	-	-	-	-	10000
124	Brila Kurkalang	2	3	5	3	2	5	-do-	-	1.00	5	-	-	4	-	12000
125	Aiphilian Kurkalang	1	3	4	4	-	4	-do-	-	0.30	-	-	-	6	-	10000
126	Disphilian Kurkalang	2	3	5	5	-	5	-do-	-	0.30	-	-	-	-	-	11000
127	Phildian Kurkalang	4	3	7	6	1	7	-do-	-	0.30	-	1	-	-	-	10000
128	Birmon Rynjah	2	4	6	5	1	6	-do-	-	0.50	4	2	-	6	-	12000
129	Melsida Kurkalang	2	1	3	2	1	3	-do-	-	2.00	-	2	-	6	-	13000
130	Arda Rynjah	3	5	8	6	2	8	-do-	-	0.40	-	-	-	7	-	10000
131	Kamsing	1	-	1	1	-	1	-do-	-	1.00	-	-	-	-	-	10000
132	Shamilin	1	1	2	2	-	2	-do-	-	0.20	-	-	-	-	-	10000
133	Stadbon Massar	3	9	12	11	1	12	-do-	-	1.00	8	3	-	10	-	14000
134	Theirit Massar	3	6	9	8	1	9	-do-	-	0.40	-	3	-	8	-	10000
135	Slabial Massar	3	4	7	5	2	7	-do-	-	0.50	-	-	-	7	-	12000
136	Aimon Massar	4	4	8	7	1	8	-do-	-	0.30	-	-	-	-	-	10000
137	Aibimon massar	2	1	3	2	1	3	-do-	-	0.20	-	-	-	-	-	9000
138	Rimonbha Maasar	3	2	5	4	1	5	-do-	-	0.30	-	-	-	-	-	8000
139	Kwein Massar	-	1	1	-	1	1	-do-	-	0.50	-	-	-	-	-	8000
140	On Marbaniang	1	4	5	5	-	5	-do-	-	1.00	-	3	-	4	-	12000
141	Rosemila Marbaniang	1	3	4	4	-	4	-do-	-	0.20	-	-	-	-	-	9000
142	Khwon Rynjah	3	3	6	5	1	6	-do-	-	0.40	-	2	-	5	-	12000
143	Baltina Rynjah	3	1	4	3	1	4	-do-	-	0.20	-	-	-	-	-	10000
144	Binaris buhphang	7	3	10	8	2	10	-do-	-	0.30	-	-	-	-	-	9500

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
145	Krissibon Tariang	3	6	9	9	-	9	-do-	-	0.50	-	2	-	5	-	11000
146	Skhirian Tariang	1	4	5	4	1	5	-do-	-	0.70	4	1	-	-	-	12000
147	Phidiang Tariang	3	4	7	5	2	7	-do-	-	0.80	3	-	-	-	-	11000
148	Sbian Kharumnuid	4	4	8	7	1	8	-do-	-	1.00	-	2	-	6	-	12000
149	Metisha Tariang	6	6	12	10	2	12	-do-	-	0.30	-	2	-	5	-	10000
150	Dwi Mylliem	2	2	4	4	-	4	-do-	-	1.00	-	2	-	4	-	15000
151	Darihun Mylliem	5	3	8	7	1	8	-do-	-	0.30	-	1	-	3	-	10000
152	Mirolin Mylliem	2	5	7	6	1	7	-do-	-	0.30	-	3	-	-	-	10000
153	Silet Rynjah	-	1	1	-	1	1	-do-	-	0.40	-	-	-	-	-	10000
154	Lomida Mylliem	5	3	8	7	1	8	-do-	-	0.70	-	-	-	6	-	12000
155	Blarisha Mylliem	1	3	4	4	-	4	-do-	-	0.30	-	-	-	-	-	10000
156	Slitsibon Mylliem	8	2	10	8	2	10	-do-	-	0.70	-	3	-	4	-	12000
157	Thiosa Rynjah	4	6	10	8	2	10	-do-	-	0.50	-	-	-	-	-	11000
158	Kbial Rynjah	4	7	11	10	1	11	Farmer	-	0.70	-	2	-	3	-	13000
159	Silbina Rynjah	2	5	7	6	1	7	-do-	-	0.40	-	-	-	-	-	10000
160	Phril Kurkalang	2	5	7	5	2	7	-do-	-	0.80	-	3	-	8	-	12000
161	Kontrimai Nongkynrih	4	4	8	8	-	8	-do-	-	2.00	4	2	-	5	-	15000
162	Lari Mylliem	-	2	2	1	1	2	-do-	-	1.00	-	2	-	8	-	12000
163	Brin Kurkalang	2	1	3	2	1	3	-do-	-	0.70	-	2	-	-	-	13000
164	Phirit Kharumnuid	4	3	7	5	2	7	-do-	-	0.30	-	-	-	-	-	10000
165	Airit Kharumnuid	4	2	6	5	1	6	-do-	-	0.30	-	-	4	-	-	10000
166	Swina Kharumnuid	1	3	4	3	1	4	-do-	-	1.00	7	2	-	6	-	12000
167	Blisha Kharumnuid	4	3	7	7	-	7	-do-	-	0.50	6	-	-	7	-	10000
168	Rimilian Kharumnuid	2	3	5	5	-	5	-do-	-	1.00	4	-	-	-	-	18000
169	Sidora Kurkalang	3	4	7	7	-	7	-do-	-	1.00	-	2	-	-	-	17000
170	Meda Kurkalang	3	4	7	6	1	7	-do-	-	0.80	-	-	-	-	-	15000
171	Mildalin Kurkalang	1	2	3	2	1	3	-do-	-	0.20	-	-	-	-	-	9000
172	Shembhalang Mylliem	5	3	8	8	-	8	-do-	-	0.30	-	2	-	-	-	10000
173	Trom Mylliem	-	1	1	-	1	1	-do-	-	0.80	6	-	-	10	-	10000
174	Norilin Mylliem	3	6	9	8	1	9	-do-	-	1.00	10	3	-	8	-	12000
175	Aikrinda Mylliem	2	2	4	2	2	4	-do-	-	0.20	-	-	-	-	-	10000
176	Kintila Kurkalang	2	4	6	5	1	6	-do-	-	0.30	-	-	-	-	-	10000
177	Sintila Kurkalang	7	2	9	7	2	9	-do-	-	0.40	-	3	-	10	-	12000
178	Trisida Kurkalang	4	3	7	5	2	7	-do-	-	0.30	-	1	-	7	-	9000
179	Metida Kurkalang	1	2	3	2	1	3	-do-	-	0.20	-	-	-	-	-	9000
180	Blon Kurkalang	5	4	9	7	2	9	-do-	-	1.00	5	3	-	-	-	13000
181	Tinola Kurkalang	4	1	5	3	2	5	-do-	-	0.20	-	-	-	-	-	10000
182	Lanol Kurkalang	1	2	3	3	-	3	-do-	-	0.70	-	-	-	-	-	11000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
183	Hisnora Kurkalang	2	4	6	5	1	6	Farmer	-	0.30	-	-	-	-	-	10000
184	Thrila Kurkalang	3	3	6	4	2	6	-do-	-	0.50	-	-	-	-	-	11000
185	Plaisi Kurkalang	7	3	10	9	1	10	-do-	-	0.30	-	-	-	-	-	12000
186	Salesha Kurkalang	7	3	10	8	2	10	-do-	-	0.20	-	-	-	5	-	10000
187	Mrida Kurkalang	4	5	9	7	2	9	-do-	-	1.70	-	-	-	7	-	11000
188	Airisha Kurkalang	3	2	5	5	-	5	-do-	-	0.30	-	-	-	-	-	9000
189	Rilian Nongkynrih	2	2	4	3	1	4	-do-	-	0.20	-	2	-	4	-	10000
190	Drialmai Rynjah	4	5	9	9	-	9	-do-	-	0.50	-	2	-	-	-	12000
191	Dapralti Kharkongor	3	5	8	6	2	8	-do-	-	1.00	-	3	-	-	-	13000
192	Jngoin Rynjah	7	7	14	12	2	14	-do-	-	1.00	-	2	-	8	-	15000
193	Mitsila Rynjah	4	5	9	8	1	9	-do-	-	0.70	-	-	-	5	-	13000
194	Nalin Khongsngi	2	2	4	2	2	4	-do-	-	0.50	-	-	-	6	-	12000
195	Yorit Khongsngi	1	5	6	6	-	6	-do-	-	1.00	6	-	-	10	-	13000
196	Narisha Khongsngi	3	2	5	4	1	5	-do-	-	0.20	-	-	-	-	-	9000
197	Mondalin Khongsngi	3	5	8	7	1	8	-do-	-	0.70	10	-	-	8	-	10000
198	Planti Khongsngi	6	4	10	8	2	10	-do-	-	0.75	8	2	-	9	-	13000
199	Knar Kharkongor	-	1	1	-	1	1	-do-	-	0.80	-	-	-	-	-	10000
200	Testbhalin Shadap	2	4	6	5	1	6	-do-	-	0.20	-	-	-	-	-	9000
201	Dril Dkhar	3	2	5	3	2	5	-do-	-	0.40	-	-	-	-	-	10000
202	Rishabha Dkhar	2	4	6	4	2	6	-do-	-	0.30	-	-	-	7	-	9000
203	Trissnoda Khongsngi	5	3	8	8	-	8	-do-	-	0.70	-	-	-	8	-	12000
204	Plimon Rynjah	1	1	2	1	1	2	-do-	-	1.00	5	-	-	7	-	12000
205	Kudbon Rynjah	5	3	8	8	-	8	-do-	-	1.00	2	3	-	10	-	15000
206	Jwied Rynjah	2	4	6	5	1	6	-do-	-	1.00	-	2	-	12	-	14000
207	Dorila Nongkynrih	3	1	4	2	2	4	-do-	-	-	-	-	-	-	-	9000
208	Ranilin Kharkongor	8	3	11	10	1	11	-do-	-	1.00	-	3	-	13	-	12000
209	Pril Nongkynrih	4	5	9	6	3	9	-do-	-	1.00	-	-	-	5	-	13000
210	Hillinda Nongkynrih	2	4	6	5	1	6	-do-	-	0.30	-	-	-	-	-	10000
211	Temple Marbaniang	3	5	8	6	2	8	-do-	-	0.30	-	-	-	6	-	10000
212	Aiphirit Kharkongor	2	4	6	5	1	6	-do-	-	0.50	-	2	-	5	-	13000
213	Sixtyfour Kharkongor	3	3	6	4	2	6	-do-	-	-	-	-	-	-	-	9000
214	Kontrisha Kharkongor	3	3	6	4	2	6	-do-	-	0.20	-	-	-	6	-	9000
215	Bleda Kharkongor	4	2	6	5	1	6	-do-	-	1.00	-	2	-	10	-	13000
216	Krintida Kharkongor	2	5	7	6	1	7	-do-	-	0.30	-	-	-	-	-	10000
217	Draisida Kharkongor	1	3	4	2	2	4	-do-	-	0.20	-	-	-	-	-	9000
218	Libon Sohtun	3	4	7	6	1	7	-do-	-	-	-	-	-	-	-	10000
219	Shimilin Myllem	4	5	9	7	2	9	-do-	-	0.70	-	2	-	7	-	11000
220	Aidmila Myllem	3	2	5	4	1	5	-do-	-	0.40	10	2	-	8	-	12000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
221	Sharngon Mylliem	5	8	13	9	4	13	-do-	-	0.80	-	2	-	5	-	13000
222	Biarmon Mylliem	2	4	6	4	2	6	-do-	-	0.20	-	2	-	-	-	12000
223	Shmirmon Mylliem	4	2	6	4	2	6	-do-	-	0.30	-	2	-	5	-	10000
224	Billomon Mylliem	2	4	6	6	-	6	-do-	-	0.30	-	2	-	4	-	11000
225	Bitstila Mylliem	2	3	5	4	1	5	-do-	-	2.00	-	3	-	6	-	16000
226	Winalis Mylliem	6	2	8	6	2	8	-do-	-	0.50	2	-	-	-	-	12000
227	Nitsila Mylliem	3	6	9	9	-	9	-do-	-	0.40	-	-	-	-	-	16000
228	Jngot Mylliem	5	8	13	11	2	13	-do-	-	2.00	13	-	-	9	-	17000
229	Banridashai Mylliem	1	2	3	2	1	3	-do-	-	0.20	-	-	-	-	-	10000
230	Badashai Mylliem	-	2	2	2	-	2	-do-	-	0.30	-	-	-	-	-	10000
231	Rijilis Mylliem	2	3	5	4	1	5	-do-	-	0.20	-	-	-	9	-	10000
232	Biolis Mylliem	2	3	5	4	1	5	-do-	-	0.20	-	-	-	9	-	10000
233	Marrila Mylliem	4	4	8	5	3	8	-do-	-	0.30	-	2	-	3	-	11000
234	Aibhashisha Mylliem	3	3	6	4	2	6	-do-	-	-	-	-	-	-	-	9000
235	Shalinda Mylliem	2	1	3	2	1	3	-do-	-	-	-	-	-	-	-	12000
236	Sharki Mylliem	1	2	3	2	1	3	Farmer	-	0.30	-	-	-	-	-	10000
237	Iahunlang Mylliem	1	3	4	3	1	4	-do-	-	0.30	-	-	-	-	-	10000
238	Trailin Mylliem	4	4	8	6	2	8	-do-	-	0.30	5	2	-	3	-	11000
239	Dariphina Mylliem	1	3	4	2	2	4	-do-	-	0.30	-	-	-	-	-	9000
240	Barishisha Mylliem	3	1	4	1	3	4	-do-	-	0.20	-	-	-	-	-	8000
241	Philda Nongrum	1	3	4	2	2	4	-do-	-	0.40	5	2	-	8	-	12000
242	Shailin Nongrum	3	1	4	2	2	4	-do-	-	0.20	-	-	-	-	-	10000
243	Thori Mylliem	5	2	7	5	2	7	-do-	-	0.50	8	2	-	6	-	12000
244	Kratsita Mylliem	2	7	9	8	1	9	-do-	-	0.20	-	2	-	5	-	12000
245	Tinoris Mylliem	1	3	4	3	1	4	-do-	-	0.20	-	-	-	4	-	10000
246	Britsida Khongsngi	1	3	4	2	2	4	-do-	-	0.30	-	-	-	-	-	10000
247	Kwinsida Khongsngi	1	1	2	2	-	2	-do-	-	-	-	-	-	-	-	10000
248	Neh Khongsngi	1	2	3	2	1	3	-do-	-	-	-	-	-	-	-	10000
249	Risilin Kurkalang	1	1	2	2	-	2	-do-	-	-	-	-	-	-	-	10000
250	Ritdalín Kurkalang	1	1	2	2	-	2	-do-	-	-	-	-	-	-	-	10000
251	Driat Mylliem	5	3	8	6	2	8	-do-	-	0.50	-	-	-	6	-	12000
252	Aitisha Khongsngi	4	4	8	6	2	8	-do-	-	0.30	-	-	-	3	-	10000
253	Prin Khongsngi	4	2	6	6	-	6	-do-	-	0.30	-	2	-	7	-	11000
254	Pyndaplin Khongsngi	2	2	4	2	2	4	-do-	-	0.20	-	-	-	-	-	10000
255	Brit Kurkalang	5	2	7	7	-	7	-do-	-	1.00	-	-	-	5	-	15000
256	Bharida Kurkalang	2	4	6	5	1	6	-do-	-	0.30	-	-	-	-	-	10000
257	Pyllon Nongkynrih	1	4	5	2	3	5	-do-	-	0.50	6	2	4	-	-	12000
258	Sitalin Nongkynrih	3	3	6	4	2	6	-do-	-	-	-	-	-	-	-	10000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
259	Iainehtibon Nongkynrih	2	1	3	2	1	3	-do-	-	-	-	-	-	-	-	9000
260	Phristida Lyngdoh	5	4	9	9	-	9	-do-	-	0.70	-	3	-	6	-	13000
261	Tishamon Lyngdoh	2	2	4	2	2	4	-do-	-	0.30	-	-	-	3	-	10000
262	Martrisha Lyngdoh	3	2	5	5	-	5	-do-	-	0.30	-	-	-	-	-	10000
263	Thewiswanmon Myllem	4	4	8	6	2	8	-do-	-	0.80	8	2	-	7	-	12000
264	Aidora Kharumnuid	3	3	6	6	-	6	-do-	-	0.90	-	-	-	-	-	13000
265	Hydralin Kharumnuid	2	2	4	3	1	4	-do-	-	0.20	-	-	-	2	-	9000
266	Silinda Kharumnuid	1	1	2	2	-	2	-do-	-	-	-	-	-	-	-	9000
267	Nahmon Myllem	3	4	7	7	-	7	-do-	-	0.80	3	-	-	5	-	13000
268	Aitimon Lyngdoh	3	1	4	2	2	4	-do-	-	0.20	-	1	-	-	-	10000
269	Stirinda Lymba	1	5	6	5	1	6	-do-	-	0.30	-	-	-	-	-	11000
270	Eplinda Lymba	3	4	7	7	-	7	-do-	-	0.30	-	-	-	-	-	12000
271	Aitilin Nongkynrih	2	3	5	4	1	5	-do-	-	0.30	-	-	-	-	-	10000
272	Sumarbha Nongkynrih	2	3	5	3	2	5	-do-	-	0.30	-	-	-	-	-	10000
273	Airis Rynjah	3	2	5	3	2	5	-do-	-	0.20	-	-	-	2	-	10000
274	Iadalin Rynjah	3	6	9	9	-	9	-do-	-	0.30	-	-	-	-	-	11000
275	Latisha Rynjah	3	3	6	4	2	6	-do-	-	0.30	-	-	-	5	-	9000
276	Shantimai Myllem	6	4	10	8	2	10	Farmer	-	0.30	4	-	-	3	-	13000
277	Banrishisha Myllem	2	2	4	2	2	4	-do-	-	-	-	-	-	-	-	9000
278	Nashisha Myllem	5	4	9	7	2	9	-do-	-	0.40	5	2	4	2	-	13000
279	Bashishalin Myllem	-	2	2	1	1	2	-do-	-	-	-	-	-	-	-	10000
280	Maltina Myllem	2	2	4	4	-	4	-do-	-	0.40	5	2	-	6	-	12000
281	Pyntngenlang Myllem	1	2	3	2	1	3	-do-	-	-	-	-	-	-	-	10000
282	Ibawanlang Myllem	1	2	3	2	1	3	-do-	-	0.20	-	-	-	-	-	10000
283	Slina Myllem	5	3	8	6	2	8	-do-	-	0.30	-	-	-	-	-	11000
284	Batisha Myllem	3	1	4	2	2	4	-do-	-	-	-	-	-	-	-	11000
285	Barisha Kharumnuid	5	2	7	5	2	7	-do-	-	0.30	-	1	-	4	-	10000
286	Plintimai Kharumnuid	-	4	4	4	-	4	-do-	-	0.40	-	2	-	6	-	10000
287	Iadalang Kharumnuid	1	3	4	2	2	4	-do-	-	0.30	-	1	-	2	-	9000
288	Kyntiewrida Kharumnuid	1	2	3	2	1	3	-do-	-	-	-	-	-	-	-	9000
289	Diarimon Kurkalang	4	2	6	4	2	6	-do-	-	0.30	-	2	-	4	-	10000
290	Aidap Tariang	2	2	4	2	2	4	-do-	-	0.30	-	-	-	-	-	11000
291	Aiphilin Kurkalang	5	2	7	5	2	7	-do-	-	1.00	10	-	-	5	-	12000
292	Rijudia Kharumnuid	1	5	6	6	-	6	-do-	-	0.40	-	-	-	3	-	11000
293	Missilin Kharumnuid	2	2	4	2	2	4	-do-	-	0.20	-	-	-	-	-	9000
294	Wandalin Kharumnuid	2	1	3	2	1	3	-do-	-	0.20	-	-	-	-	-	9000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
295	Syntiewbashisha K.umnuid	4	2	6	4	2	6	-do-	-	0.30	-	-	-	4	-	10000
296	Iolin Kurkalang	1	4	5	5	-	5	-do-	-	0.40	5	2	4	-	-	12000
297	Tralin Kurkalang	3	3	6	4	2	6	-do-	-	0.20	-	-	5	-	-	10000
298	Ubhalin Kurkalang	2	1	3	1	2	3	-do-	-	-	-	-	-	-	-	9000
299	Thrial Kurkalang	1	1	2	1	1	2	-do-	-	0.70	8	-	5	4	-	10000
300	Jngorda Nongrum	2	3	5	3	2	5	-do-	-	0.30	-	2	-	3	-	12000
301	Betila Dkhar	2	3	5	2	3	5	-do-	-	0.20	-	-	-	-	-	9000
302	Risuklang Dkhar	1	2	3	2	1	3	-do-	-	-	-	-	-	-	-	9000
303	Aimilian Kharumnuid	3	1	4	4	-	4	-do-	-	0.30	2	-	5	-	-	10000
304	Bisnora Rynjah	3	5	8	5	3	8	-do-	-	0.20	-	2	14	-	-	10000
305	Battilin Rynjah	-	3	3	2	1	3	-do-	-	0.40	5	-	10	-	-	10000
306	Kristina Lyngdoh	1	6	7	5	2	7	-do-	-	0.70	-	-	12	5	-	12000
307	Pritsila Lyngdoh	3	4	7	6	1	7	-do-	-	0.70	-	2	-	-	-	13000
308	Bahunlang Nongkynrih	2	1	3	2	1	3	-do-	-	0.20	-	-	-	-	-	9000
309	Khriar Rynjah	2	4	6	4	2	6	-do-	-	0.80	-	-	-	-	-	12000
310	Shimtilang Rynjah	3	5	8	7	1	8	-do-	-	0.30	-	-	-	-	-	10000
311	Wied Warbah	6	4	10	8	2	10	-do-	-	2.00	-	2	-	10	-	16000
312	Aibhamon Warbah	1	4	5	5	-	5	-do-	-	0.40	-	-	-	5	-	10000
313	Ngeitlang Rynjah	2	1	3	2	1	3	-do-	-	-	-	-	-	-	-	10000
314	Bharida Tariang	4	4	8	8	-	8	-do-	-	0.40	-	-	-	-	-	17000
315	Jngud Rynjah	6	5	11	10	1	11	-do-	-	1.00	4	2	-	-	-	15000
316	Ridian Rynjah	-	2	2	1	1	2	-do-	-	0.40	-	-	-	-	-	10000
317	Kwiem Lymba	2	3	5	3	2	5	Farmer	-	0.40	-	2	-	5	-	10000
318	Makrisha Lymba	4	2	6	5	1	6	-do-	-	0.20	-	-	-	-	-	9000
319	Airina Rynjah	3	4	7	7	-	7	-do-	-	0.30	-	2	-	-	-	12000
320	Phlorial Rynjah	2	4	6	6	-	6	-do-	-	0.40	-	2	-	5	-	11000
321	Sirian Rynjah	5	3	8	7	1	8	-do-	-	0.80	5	-	6	-	-	13000
322	Balinda Kharumnuid	1	1	2	2	-	2	-do-	-	0.40	-	2	-	3	-	10000
323	Jlian Khyriem	5	3	8	7	1	8	-do-	-	2.00	-	2	-	8	-	16000
324	Makrina Khyriem	1	3	4	2	2	4	-do-	-	0.30	-	-	-	5	-	9000
325	Buromlang Khyriem	3	1	4	2	2	4	-do-	-	0.30	-	-	-	4	-	10000
326	Dwela Khyriem	2	1	3	1	2	3	-do-	-	0.70	-	2	-	-	-	12000
327	Jngian Khyriem	1	4	5	4	1	5	-do-	-	0.85	-	-	-	-	-	13000
328	Thrian Khyriem	5	3	8	8	-	8	-do-	-	0.70	-	2	-	-	-	12000
329	Tibhalang Khyriem	2	3	5	4	1	5	-do-	-	0.30	-	2	-	2	-	10000
330	Memrina Khyriem	4	4	8	6	2	8	-do-	-	0.30	-	-	-	-	-	9000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
331	Bina Khyriem	6	3	9	6	3	9	-do-	-	0.30	-	-	-	-	-	9000
332	Phiiona Khyriem	3	2	5	1	4	5	-do-	-	0.40	-	1	-	3	-	10000
333	Arbilin Rynjah	1	1	2	2	-	2	-do-	-	0.30	-	-	-	-	-	10000
334	Biladsbon Kharkongor	6	2	8	8	-	8	-do-	-	0.30	-	-	-	-	-	13000
335	Kridalin Kharkongor	1	2	3	2	1	3	-do-	-	0.30	-	-	-	3	-	9000
336	Kridalin Kharkongor	1	4	5	5	-	5	-do-	-	0.50	-	-	-	5	-	12000
337	Aibhalin Kharkongor	2	2	4	2	2	4	-do-	-	-	-	-	-	-	-	10000
338	Shimtilin Rynjah	1	8	9	6	3	9	-do-	-	0.30	-	-	-	-	-	12000
339	Pharkin Rynjah	3	2	5	5	-	5	-do-	-	1.00	-	5	-	4	-	17000
340	Tensing Rynjah	3	1	4	3	1	4	-do-	-	0.50	-	-	-	-	-	11000
341	Jorisha Rynjah	3	1	4	4	-	4	-do-	-	-	-	-	-	-	-	13000
342	Smilda Rynjah	3	2	5	5	-	5	-do-	-	5.00	5	-	-	14	-	18000
343	Bhashisha Rynjah	3	6	9	8	1	9	-do-	-	0.30	-	2	-	10	-	12000
344	Ailinda Rynjah	2	3	5	3	2	5	-do-	-	-	-	-	-	-	-	10000
345	Shmilinda Rynjah	-	2	2	2	-	2	-do-	-	-	-	-	-	-	-	10000
346	Kyntiewnam Rynjah	1	2	3	2	1	3	-do-	-	-	-	-	-	-	-	10000
347	Barinam Rynjah	1	2	3	2	1	3	-do-	-	-	-	-	-	-	-	10000
348	Trial Pyngrope	1	2	3	3	-	3	-do-	-	1.00	6	1	-	2	-	13000
349	Aiiona Pyngrope	3	3	6	4	2	6	-do-	-	0.20	-	-	-	-	-	9000
350	Aibida Pyngrope	3	4	7	5	2	7	-do-	-	0.30	-	2	-	6	-	9000
351	Barisha Pyngrope	2	4	6	4	2	6	-do-	-	0.30	-	1	-	4	-	10000
352	Ridahun Pyngrope	3	2	5	3	2	5	-do-	-	-	-	-	-	-	-	10000
353	Aidashisha Pyngrope	6	3	9	8	1	9	-do-	-	0.30	-	-	-	10	-	12000
354	Dapbianglin Pyngrope	3	4	7	7	-	7	-do-	-	0.30	-	-	-	5	-	13000
355	Haidalin Pyngrope	8	3	11	9	2	11	-do-	-	1.00	-	2	-	5	-	15000
356	Krislin Nongkynrih	4	3	7	5	2	7	-do-	-	1.00	-	-	-	6	-	15000
	Total	976	1073	2055	1595	456	2051		-		316	310	121	1002		

SOCIO – ECONOMIC DATA OF LAITLUM VILLAGE UNDER MIDDLE UMLEW WATERSHED (2010-2011) P-VIII

Sl No	Name of the Head of the Family	Population			Literacy			Occupation	Agriculture Area		Livestock					Annual Income
		Male	Female	Total	Literate	Illiterate	Total		Settled	Jhum	Cow	Pig	Goat	Poultry	Horse	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
1	Jloin Myllem	3	3	6	4	2	6	Farmer	-	-	14	2	-	7	-	10000
2	Drian Khyriem	3	3	6	1	5	6	-do-	-	-	-	1	-	10	-	6000
3	Stian Warbah	3	2	5	-	5	5	-do-	-	-	-	-	-	5	-	5000
4	Loven Nongspung	1	1	2	-	2	5	Labour	-	-	-	-	-	-	-	7000
5	Overwell Synrem	4	3	7	1	6	7	-do-	-	-	-	1	-	-	-	8000
6	Akostin Nongspung	5	3	8	1	7	8	-do-	-	-	-	-	-	4	-	10000
7	Sahun Songthiang	6	4	10	2	8	10	Farmer	-	-	9	1	-	-	-	7000
8	Phrangbor Myllem	3	3	6	-	6	6	Labour	-	-	-	2	-	-	-	6000
9	Prisca Kharkongor	2	1	3	2	1	3	-do-	-	-	-	-	-	-	-	7000
10	Mieh Kharkongor	4	3	7	-	7	7	-do-	-	-	-	1	-	-	-	5000
11	Rilin Kharumnuid	2	4	6	3	3	6	-do-	-	-	-	-	8	8	-	12000
12	Shidalin Nongspung	1	3	4	1	3	4	-do-	-	-	-	-	-	-	-	8000
13	Thrie Kharkongor	2	2	4	-	4	4	-do-	-	-	-	-	-	3	-	7000
14	Balin Kharkongor	1	1	2	-	2	2	-do-	-	-	-	2	-	-	-	8000
15	Thrier Kharkongor	1	1	2	-	2	2	-do-	-	-	-	-	-	-	-	10000
16	Surwel Nongspung	2	2	4	-	4	4	-do-	-	-	-	1	-	-	-	7000
17	Ryngkat Kharumnuid	2	3	5	2	3	5	-do-	-	-	-	2	-	3	-	10000
18	Melli Nongspung	2	2	4	1	3	4	Farmer	-	-	-	2	4	6	-	8000
19	Drawel Nongspung	1	3	4	-	4	4	Labour	-	-	-	-	-	2	-	7000
20	Kynmaw Nongkynrih	3	1	4	-	4	4	Farmer	-	-	-	-	-	5	-	8000
21	Isnel Kharmyndai	5	2	7	-	7	7	-do-	-	-	10	1	-	-	-	8000
22	Karsing Kharkongor	3	1	4	-	4	4	-do-	-	-	-	-	-	-	-	10000
23	Klomity Nongspung	2	5	7	3	4	7	Labour	-	-	-	-	-	2	-	12000
24	Phillip Myllem	6	4	10	10	-	10	Farmer	-	-	-	-	-	-	-	12000
25	Shanbor Nongkynrih	1	-	1	-	1	1	Labour	-	-	-	-	-	-	-	8000
26	Jrur Myllem	1	3	8	-	8	8	Farmer	-	-	-	-	-	3	-	7000
27	Shrud Nongrum	2	1	2	1	1	2	-do-	-	-	-	1	-	-	-	8000
28	Triffina Nongspung	3	1	2	2	-	2	Teacher	-	-	-	-	-	-	-	12000
29	Rangajied Nongspung	4	3	5	1	4	5	Labour	-	-	-	-	-	5	-	8000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
30	Traswel Nongspung	3	3	6	1	5	6	-do-	-	-	-	1	-	-	-	10000
31	Bina Nongspung	4	1	5	1	4	5	Farmer	-	-	-		-	-	-	6000
32	Kwiansila Myllem	3	2	5	2	3	5	-do-	-	-	-	2	-	-	-	10000
33	Khibon Nongspung	2	1	3	-	3	3	-do-	-	-	-	-	-	6	-	6000
34	Plung Nonglyer	4	4	8	2	6	8	-do-	-	-	-	-	8	-	-	10000
35	Kena Nongspung	1	4	5	1	4	5	Labour	-	-	4	6		-	-	8000
36	Khlosila Nongspung	2	2	4	1	3	4	Farmer	-	-	1	-	5	-	-	7000
37	Bani nongspung	4	2	6	1	5	6	Labour	-	-	-	-	-	-	-	5000
38	Trilin Myllem	1	2	3	-	3	3	Farmer	-	-	-	-	-	-	-	6000
39	Dibhalang Myllem	4	3	7	1	6	7	Labour	-	-	1	-	-	-	-	7000
40	Roken Nongspung	2	2	4	-	4	4	Farmer	-	-	1	-	-	-	-	10000
41	Rita Nongspung	2	3	5	-	5	5	Labour	-			-	-	-	-	6000
42	Kjiek Nongspung	2	2	4	-	4	4	-do-	-	-	3	1	-	-	-	8000
43	Khror Kharkongor	3	4	7	1	6	7	-do-	-	-	1	1	-	-	-	6000
44	Darihun Nongspung	1	1	2	-	2	2	-do-	-	-	-	-	-	-	-	7000
45	Barihun Nongspung	1	2	3	-	3	3	Labour	-	-	-	-	-	-	-	10000
46	Pholding Shadap	3	3	6	2	4	6	-do-	-	-	-	-	-	-	-	8000
47	Sarian Nongspung	1	4	5	1	4	5	Labour	-	-	-	-	-	-	-	9000
48	Sidalis Nongspung	2	3	5	-	5	5	-do-	-	-	-	-	-	-	-	5000
49	Bandalin Nongspung	1	1	2	-	2	2	Labour	-	-	-	-	-	-	-	10000
50	Droila Nongspung	2	4	6	1	5	6	-do-	-	-	-	-	-	-	-	8000
51	Justina Nongspung	-	1	1	-	1	1	-do-	-	-	-	-	-	-	-	8000
52	Swiar Nongspung	1	2	3	1	2	3	-do-	-	-	-	-	-	-	-	7000
53	Kyrhon Songthiang	3	4	7	3	4	7	-do-	-		6	2	9	12	-	10000
54	Lisamon Nongspung	2	4	6	2	4	6	Labour	-	-	2	1	-	-	-	8000
55	Phatstar Rynjah	2	2	4	-	4	4	-do-	-	-	5	1	-	-	-	8000
56	Mon Nongkynrih	3	4	7	2	5	7	-do-	-	-		2	4	-	-	6000
57	Darina Nongspung	2	1	3	-	3	3	-do-	-	-		-	-	-	-	15000
58	Iralin Nongspung	1	1	2	-	2	2	-do-	-	-	1	-	-	-	-	6000

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
59	Daphira Kharumnuid	1	1	2	2	-	2	Teacher	-	-	-	-	-	-	-	10000
60	Risdalin Nongspung	1	2	3	1	2	3	-do-	-	-	-	-	-	-	-	8000
61	Ruphilin Nongspung	1	1	2	-	2	2	Labour	-	-	-	1	-	-	-	10000
62	Teimon Myllem	2	3	5	-	5	5	-do-	-	-	-	-	-	-	-	18000
63	Philet Nongrum	3	3	6	4	2	6	Labour	-	-	-	-	-	-	-	12000
64	Koswon Nongspung	1	-	1	1	-	1	-do-	-	-	-	-	-	-	-	6000
65	Disishon Myllem	9	4	13	2	11	13	-do-	-	-	2	2	-	-	-	13000
66	Sibon Nongspung	1	2	3	1	2	3	Farmer	-	-	-	-	-	3	-	6000
67	Sipiro Nongspung	2	1	3	-	3	3	-do-	-	-	-	-	-	-	-	8000
68	Lyhen Nongkynrih	1	1	2	-	2	2	-do-	-	-	-	-	-	-	-	18000
69	Shek Myllem	3	1	4	-	4	4	Labour	-	-	-	1	-	-	-	8000
70	Sbunbha Kharumnuid	4	4	8	2	6	8	-do-	-		-	2	-	-	-	10000
71	Rosina Nongspung	1	2	3	1	2	3	Farmer	-	-	6	2	3	-	-	6000
	TOTAL	169	165	334							66	49	53	83		

ANNEXURE III

COST AND ESTIMATES

MODEL NORMS PER HECTARE FOR AGRO – HORTICULTURE WITH TEMPERATE FRUIT (PLUM) (INTEGRATED WATERSHED MANAGEMENT PROGRAMME)

Spacing - 8m x 6.3m

Plant Density - 200 Nos.

A. Preliminary works

I. Site clearance		
3 mandays @ Rs.100/- per manday	-	Rs. 300.00
II. Pit digging (pit size 0.45m x 0.45m x 0.45m)		
160 Nos. @ Rs.5/- each	-	<u>Rs. 800.00</u>
Total	-	Rs.1100.00

B. First year Planting

I. Cost of planting materials		
200 Nos. @ Rs.26/- each	-	Rs.5200.00
II. Cost of planting 160 Nos. @ Rs. 3/- each	-	Rs. 480.00
III. Weeding two times		
20 mandays @ Rs.100/- per manday	-	<u>Rs.2000.00</u>
Total	-	Rs.7680.00

C. Second year Planting

I. Refilling vacancy (10%)	-	Rs. 370.00
II. Weeding two times		
20 mandays @ Rs.100/- per manday	-	<u>Rs.2000.00</u>
Total	-	Rs.2370.00

Grand Total A+B+C = Rs.1100.00 + Rs.7680.00 + Rs.2370.00 = Rs.11150.00

(Rupees Eleven thousand one hundred fifty) only.

COST NORMS FOR EARTHEN PERIPHERAL BUND WITH LIVE VEGETATION PER METRE
(INTEGRATED WATERSHED MANAGEMENT PROGRAMME)
(Rate as per PWD, SOR for R&B 2008 – 2009)

A. PERIPHERAL BUNDS SPECIFICATION & COSTS

Top Width	=	1.0 m
Bottom Width	=	1.2 m
Height	=	1.0 m

1/3 (a) Earthwork in excavation etc. in ordinary soil etc.



$$1.0\text{m} \times \frac{1.0+1.2}{2} \text{m} \times 1.0\text{m} = 1.10\text{m}^3$$

$$@ \text{Rs.}39.00/\text{m}^3 = \text{Rs.}43.00$$

2. Supplying and planting of live hedges on toe of bunds
 with local shrubs/cutting etc.
 per Running metre in L.S

	=	<u>Rs. 7.00</u>
Total	=	Rs.50.00

(Rupees Fifty) only.

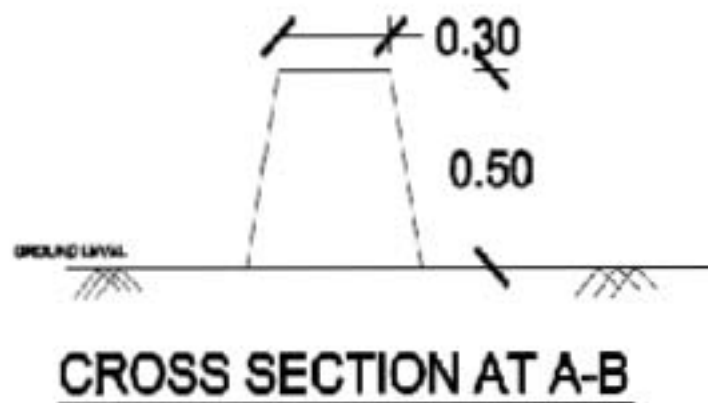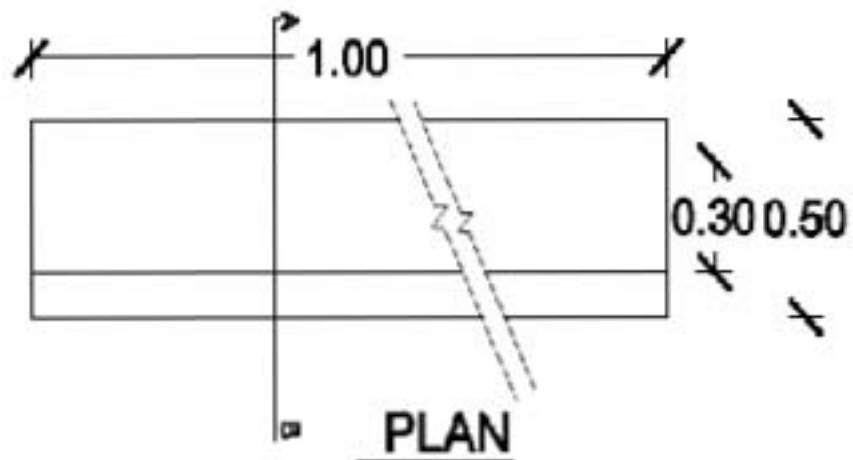

**DRAWING OF
PERIPHERAL BUND.**

NOT TO SCALE
All dimensions are in metres
DRAWN BY

COST NORMS FOR EARTHEN CONTOUR BUND (INTEGRATED WATERSHED MANAGEMENT PROGRAMME)
(Rate as per PWD, SOR for R&B 2008 – 2009)

A. CONTOUR BUNDS SPECIFICATION & COSTS

Top Width	=	0.5 m
Bottom Width	=	1.0 m
Height	=	0.77 m
Spacing	=	20 m
Total Length	=	5 x 100 = 500 m

1/3 (a) Earthwork in excavation etc. in ordinary soil etc.

$$500\text{m} \times \frac{0.5+1.0}{2} \text{m} \times 0.77 = 288.5\text{m}^3$$

$$@ \text{Rs.}26.00/ \text{m}^3 = \text{Rs.}7500.00$$

$$\text{Total} = \text{Rs.}7500.00$$

(Rupees Seven Thousand Five Hundred) only.

MODEL NORMS PER HECTARE FOR AGRO – FORESTRY WITH PINE/NON-PINE (INTEGRATED WATERSHED MANAGEMENT PROGRAMME)

Spacing 6m x 5.5m

Plant Density – 300 Nos.

A. <u>Preliminary works</u>			
I. Jungle clearance etc. 5 mandays @ Rs.100/- per manday	-	Rs.	500.00
II. Pit digging (pit size 0.30m x 0.30m x 0.30m) 300 Nos. @ Rs.4/- each	-	<u>Rs.</u>	<u>1200.00</u>
Total	-	Rs.	1700.00
B. <u>First year Planting</u>			
I. Cost of planting materials 300 Nos. @ Rs.8/- each	-	Rs.	2400.00
II. Cost of planting 300 Nos. @ Rs. 2/- each	-	Rs.	600.00
IV. Weeding two times 20 mandays @ Rs.100/- per manday	-	Rs.	2000.00
IV. Fire protection measures 5 mandays @ Rs.100/- per manday	-	<u>Rs.</u>	<u>500.00</u>
Total	-	Rs.	5500.00
C. <u>Second year Planting</u>			
I. Vacancy refilling (10%)	-	Rs.	400.00
II. Weeding two times 20 mandays @ Rs.100/- per manday	-	Rs.	2000.00
III. Fire protection measures 5 mandays @ Rs.100/- per manday	-	<u>Rs.</u>	<u>500.00</u>
Total	-	Rs.	2900.00
Grand Total A+B+C = Rs.1700.00 + Rs.5500.00 + Rs.2900.00 = Rs.10100.00			


(Rupees Ten thousand one hundred) only.

MODEL ESTIMATE FOR CONSTRUCTION OF PROTECTION WALL
(The rate based as per M.P.W.D Schedule of rates for Roads, Bridges and
E & D Works 2008 - 2009)

1/6	Earthwork in excavation for foundation of Hume pipe culvert, slab drain, retaining wall, face wall up to the desired founding level i/c. dewatering, bailing out of water to keep the foundation dry and protecting the sides of foundation by adequate shoring, scaffolding. The foundation is leveled both longitudinally and transversely as directed.	$1 \times 10.00 \times 1.00 \times 0.65 = 6.50 \text{ m}^3$ @ Rs.93.00/m ³	Rs. 604.50
2/26	Providing cement concrete work in proportion 1:4:8 with hard broken stone aggregates 40mm down graded, including necessary carriage of stone and sand within a distance of 200m and curing, complete as directed.	$10.00 \times 1.00 \times 0.10 = 1.00 \text{ m}^3$ @ Rs.2136.00/m ³	Rs. 2136.00
3/20 (a)	Providing regular stone masonry work in returning walls, breast walls and wing walls with hammer dressed or blunt chisel dressed stones of heavy section with proper key stones each not less than 25cm X 25cm X 75cm, in cement mortar 1:6 including carriage of stone within 200m complete as directed.	$10.00 \times 0.90 \times 0.55 = 4.95 \text{ m}^3$ $10.00 \times \frac{0.50 + 0.90}{2} \times 2.00 = \underline{14.00 \text{ m}^3}$ 18.95 m ³ @ Rs.1060.00/m ³	<u>Rs.20087.00</u> Rs.22827.50
TOTAL:			
Say			Rs.22,830.00

(Rupees Twenty two thousand eight hundred thirty) only.

Submitted:-

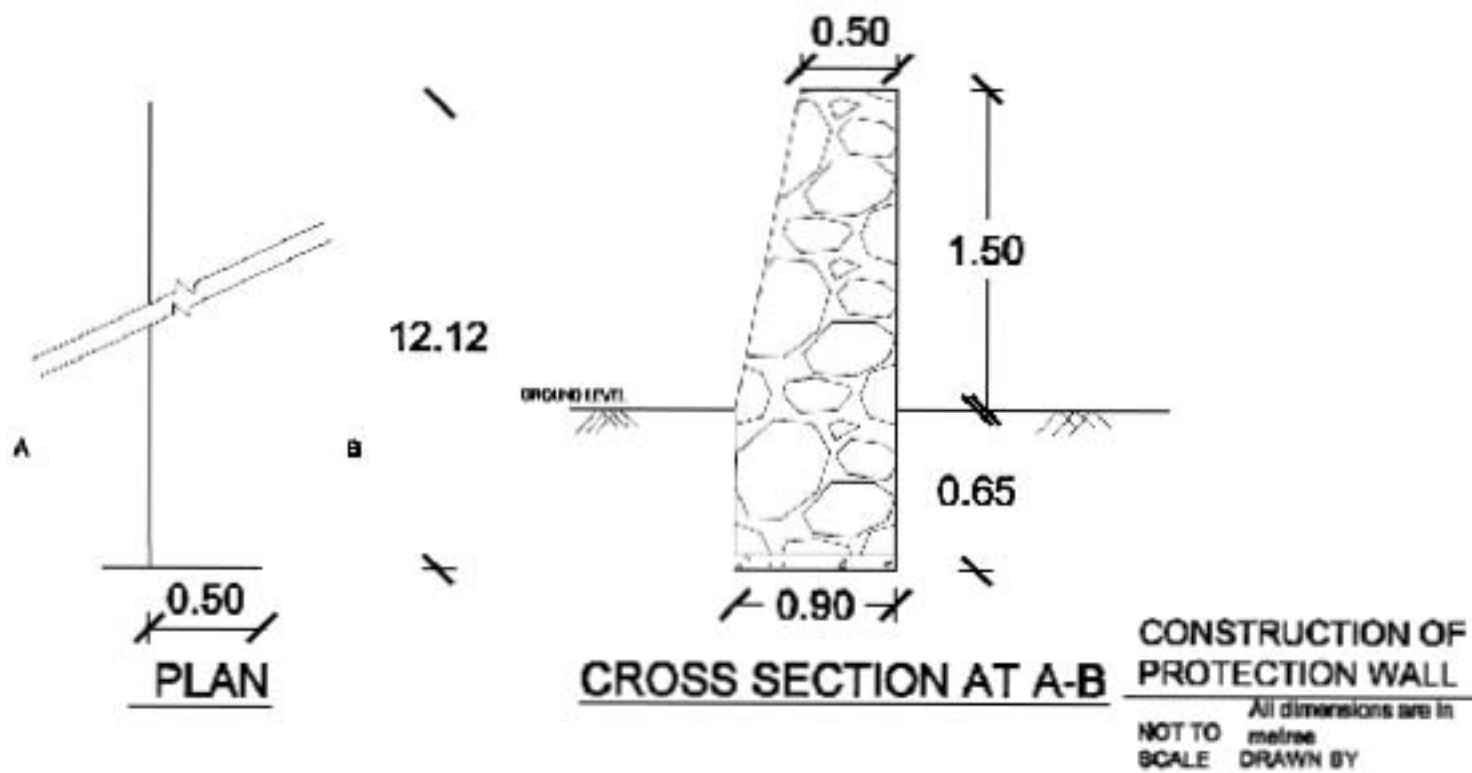

MODEL ESTIMATE FOR CONSTRUCTION OF C.C. CHECK DAM
 (The rate based as per P.W.D Schedule of rates for Roads, Bridges and
 E & D Works 2008 - 2009)

- 1/5 (a) Earthwork in excavation for abutment and wing walls of bridges and culverts, up to the desired founding level including dewatering, bailing out of water and protecting the foundation sides by adequate shoring, scaffolding and including leveling the foundation longitudinally and transversely etc.

$$\begin{aligned} 1 \times 5.80 \times 1.00 \times 0.50 &= 2.90 \text{ m}^3 \\ 1 \times 4.85 \times 1.50 \times 0.30 &= \underline{2.18 \text{ m}^3} \\ &5.08 \text{ m}^3 \\ &\text{@ Rs.124.00/m}^3 \end{aligned}$$

Rs. 629.92

- 2/26 Providing cement concrete work in proportion 1:4:8 with hard broken stone aggregates 40mm down graded, including necessary carriage of stone and sand within a distance of 200m and curing, complete as directed.

$$\begin{aligned} 1 \times 5.80 \times 1.00 \times 0.10 &= 0.58 \text{ m}^3 \\ &\text{@ Rs.2136.00/m}^3 \end{aligned}$$

Rs. 1238.88

- 3/41 (a) Providing shuttering with dressed planks not less than 25mm thick properly joined including battens, props to the proper level and removing the same after the concrete hardened.

$$\begin{aligned} 1 \times 5.80 \times 1.10 &= 6.38 \text{ m}^2 \\ 1 \times 5.80 \times 1.20 &= 6.96 \text{ m}^2 \\ 2 \times 3.50 \times 0.40 &= 2.80 \text{ m}^2 \\ 1 \times 7.85 \times 0.05 &= \underline{0.39 \text{ m}^2} \\ &16.53 \text{ m}^2 \\ &\text{@ Rs.295.00/m}^2 \end{aligned}$$

Rs. 7876.35

- 4/28 Providing cement concrete work in abutments, wing walls and return walls in proportion 1:3:6 with hard broken stone aggregates 40mm down graded including necessary carriage of stone and sand within a distance of 200m etc.

$$1 \times 5.80 \times 1.00 \times 0.40 = 2.32 \text{ m}^3$$

$$1 \times 5.80 \times \frac{1.00 + 0.50}{2} \times 1.10 = 4.78 \text{ m}^3$$

$$2 \times 1.50 \times 0.50 \times 0.40 = 0.60 \text{ m}^3$$

$$1 \times 4.85 \times 1.50 \times 0.10 = \frac{0.73 \text{ m}^3}{8.43 \text{ m}^3}$$

$$@ \text{Rs.}2344.00/\text{m}^3$$

Rs.19759.92

- 5/24 Providing stone pitching with one man size boulders not less than 25cm X 25cm X 30cm long including filling the interstices with spoils and carriage of stone within a distance of 200m complete as directed.

$$1 \times 4.85 \times 1.50 \times 0.25 = 1.82 \text{ m}^3$$

$$@ \text{Rs.}512.00/\text{m}^3$$

Rs. 931.84

- 6/27 Providing 12mm thick cement plastering including cleaning surface, curing and carriage of sand within 200m complete.

$$1 \times 5.80 \times 1.10 = 6.38 \text{ m}^2$$

$$1 \times 5.80 \times 1.20 = 6.96 \text{ m}^2$$

$$2 \times 3.50 \times 0.40 = 2.80 \text{ m}^2$$

$$1 \times 5.80 \times 0.50 = 2.90 \text{ m}^2$$


$$1 \times 4.85 \times 1.50 = \frac{7.28 \text{ m}^2}{26.32 \text{ m}^2}$$

$$@ \text{Rs.}93.00/\text{m}^2$$

TOTAL: Rs. 2447.76
Rs.29884.67

Say Rs.29,900.00

(Rupees Twenty nine thousand nine hundred) only.

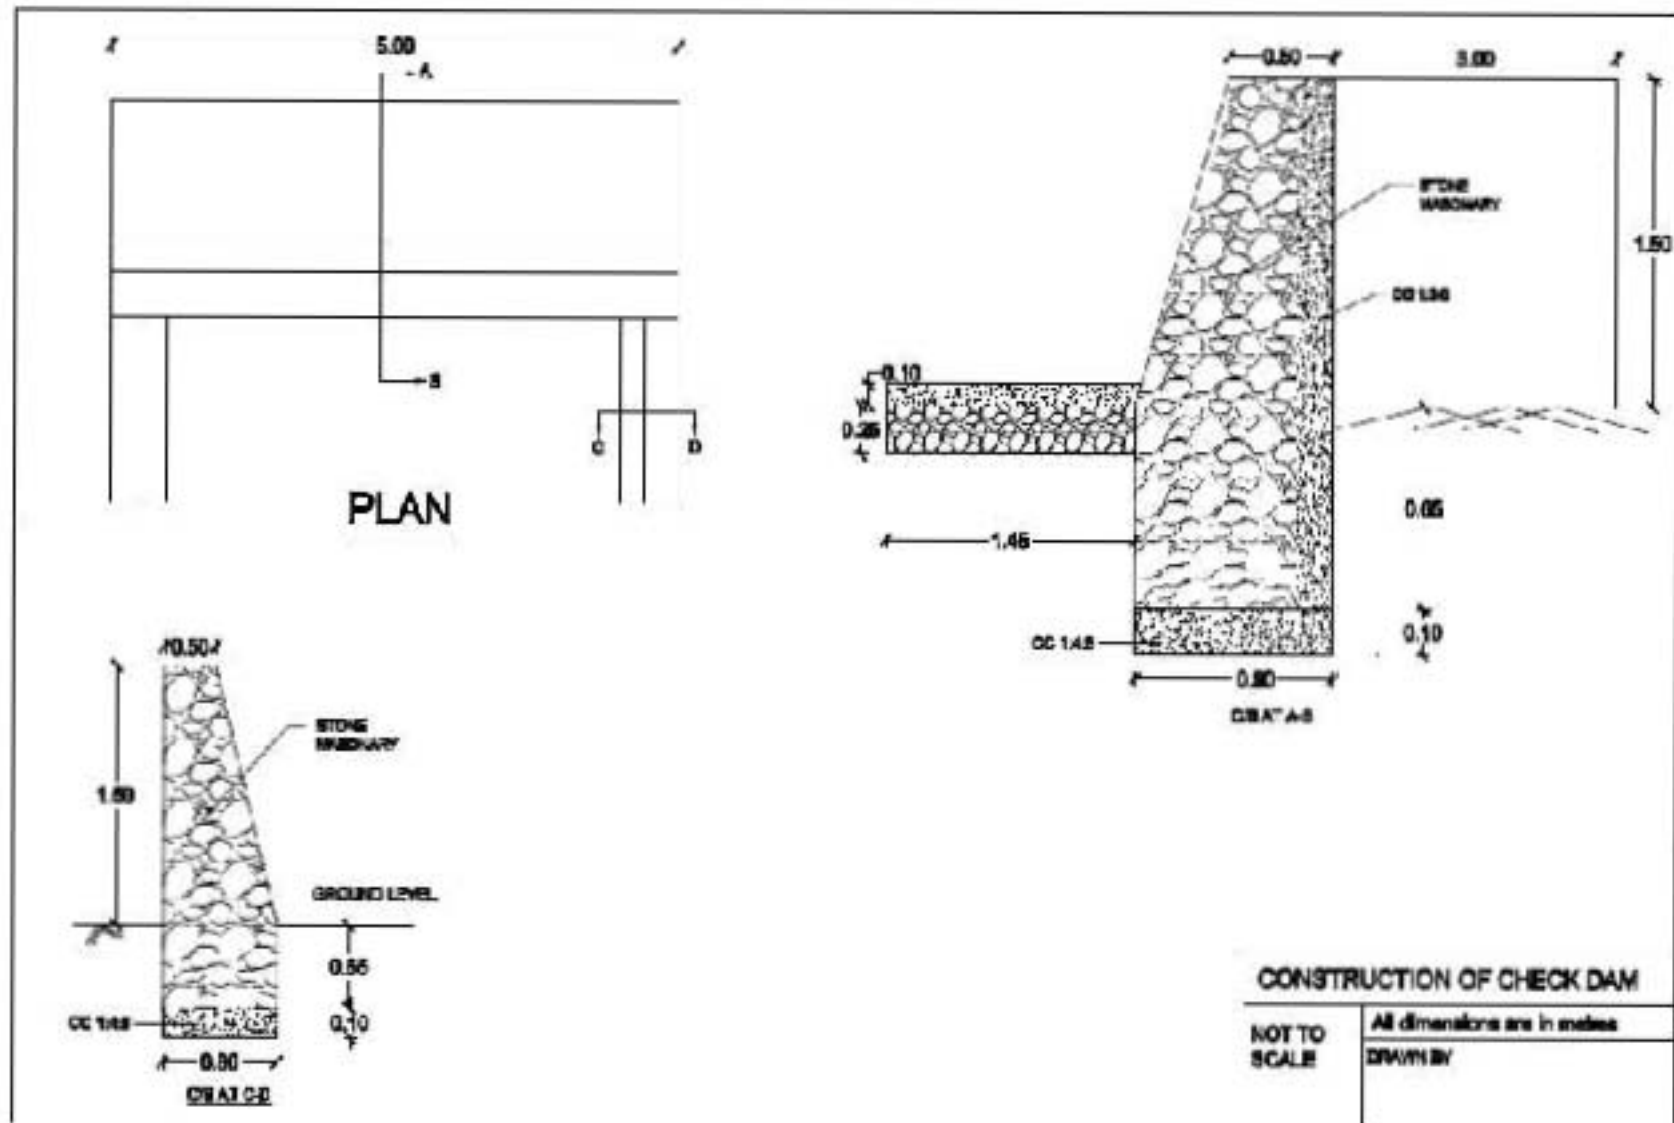

MODEL ESTIMATE FOR CONSTRUCTION OF WATER HARVESTING STRUCTURE

(The rate based as per P.W.D Schedule of rates for Roads, Bridges and
E & D Works 2008 - 2009)

- 1/5 (a) Earthwork in excavation for abutment and wing walls of bridges and culverts, up to the desired founding level including dewatering, bailing out of water and protecting the foundation sides by adequate shoring, scaffolding and including leveling the foundation longitudinally and transversely etc.

$$\begin{aligned} 1 \times 6.00 \times 1.00 \times 0.50 &= 3.00 \text{ m}^3 \\ 1 \times 1.90 \times 1.50 \times 0.35 &= 0.99 \text{ m}^3 \\ 1 \times 1.90 \times 0.20 \times 0.30 &= 0.11 \text{ m}^3 \\ &\underline{4.10 \text{ m}^3} \end{aligned}$$

@ Rs.124.00/m³

Rs. 508.40

- 2/26 Providing cement concrete work in proportion 1:4:8 with hard broken stone aggregates 40mm down graded, including necessary carriage of stone and sand within a distance of 200m and curing, complete as directed.

$$1 \times 6.00 \times 1.00 \times 0.10 = 0.60 \text{ m}^3$$

@ Rs.2136.00/m³

Rs. 1281.60

- 3/41 Providing shuttering with dressed planks not less than 25mm thick properly joined including battens, props to the proper level and removing the same after the concrete hardened.

$$\begin{aligned} 1 \times 6.00 \times 1.10 &= 6.60 \text{ m}^2 \\ 1 \times 6.00 \times 1.20 &= 7.20 \text{ m}^2 \\ 2 \times 5.00 \times 0.40 &= 4.00 \text{ m}^2 \\ 4 \times 1.70 \times 0.30 &= 2.40 \text{ m}^2 \\ 4 \times 1.20 \times 0.30 &= 1.44 \text{ m}^2 \\ 4 \times 0.40 \times 0.30 &= 0.48 \text{ m}^2 \\ 2 \times 1.20 \times 0.20 &= 0.48 \text{ m}^2 \\ 2 \times 0.40 \times 0.20 &= 0.16 \text{ m}^2 \\ 2 \times 1.90 \times 0.20 &= 0.76 \text{ m}^2 \\ &\underline{23.16 \text{ m}^2} \end{aligned}$$

@ Rs.295.00/m²

Rs. 6832.20

- 4/28 Providing cement concrete work in abutments, wing walls and return walls in proportion 1:3:6 with hard broken stone aggregates 40mm down graded including necessary carriage of stone and sand within a distance of 200m etc.

$$1 \times 6.00 \times 1.00 \times 0.40 = 2.40 \text{ m}^3$$

$$1 \times 6.00 \times \frac{1.00+0.50}{2} \times 1.10 = 4.95 \text{ m}^3$$

$$2 \times 2.25 \times 0.50 \times 0.40 = 0.90 \text{ m}^3$$

$$2 \times 1.70 \times 0.50 \times 0.20 = 0.34 \text{ m}^3$$

$$2 \times 1.20 \times 0.30 \times 0.20 = 0.14 \text{ m}^3$$

$$2 \times 0.40 \times 0.30 \times 0.20 = 0.05 \text{ m}^3$$

$$1 \times 1.90 \times 0.50 \times 0.20 = 0.19 \text{ m}^3$$

$$1 \times 1.90 \times 1.50 \times 0.10 = 0.28 \text{ m}^3$$

$$9.25 \text{ m}^3$$

$$@ \text{Rs.}2344.00/\text{m}^3$$

Rs.21682.00

- 5/24 Providing stone pitching with one man size boulders not less than 25cm X 25cm X 30cm long including filling the interstices with spoils and carriage of stone within a distance of 200m complete as directed.

$$1 \times 1.90 \times 1.50 \times 0.25 = 0.71 \text{ m}^3$$

$$@ \text{Rs.}512.00/\text{m}^3$$

Rs. 363.52

- 6/27 Providing 12mm thick cement plastering including cleaning surface, curing and carriage of sand within 200m complete.

$$1 \times 6.00 \times 1.10 = 6.60 \text{ m}^2$$

$$1 \times 6.00 \times 1.20 = 7.20 \text{ m}^2$$

$$2 \times 5.00 \times 0.40 = 4.00 \text{ m}^2$$

$$4 \times 1.70 \times 0.30 = 2.04 \text{ m}^2$$

$$4 \times 1.20 \times 0.30 = 1.44 \text{ m}^2$$

$$4 \times 0.40 \times 0.30 = 0.48 \text{ m}^2$$

$$2 \times 1.20 \times 0.20 = 0.48 \text{ m}^2$$

$$2 \times 0.40 \times 0.20 = 0.16 \text{ m}^2$$

$$2 \times 1.90 \times 0.20 = 0.76 \text{ m}^2$$

$$23.16 \text{ m}^2$$

$$@ \text{Rs.}93.00/\text{m}^2$$

Rs. 2153.88


TOTAL:

Rs.32821.60

Say

Rs.32,800.00

(Rupees Thirty two thousand eight hundred) only

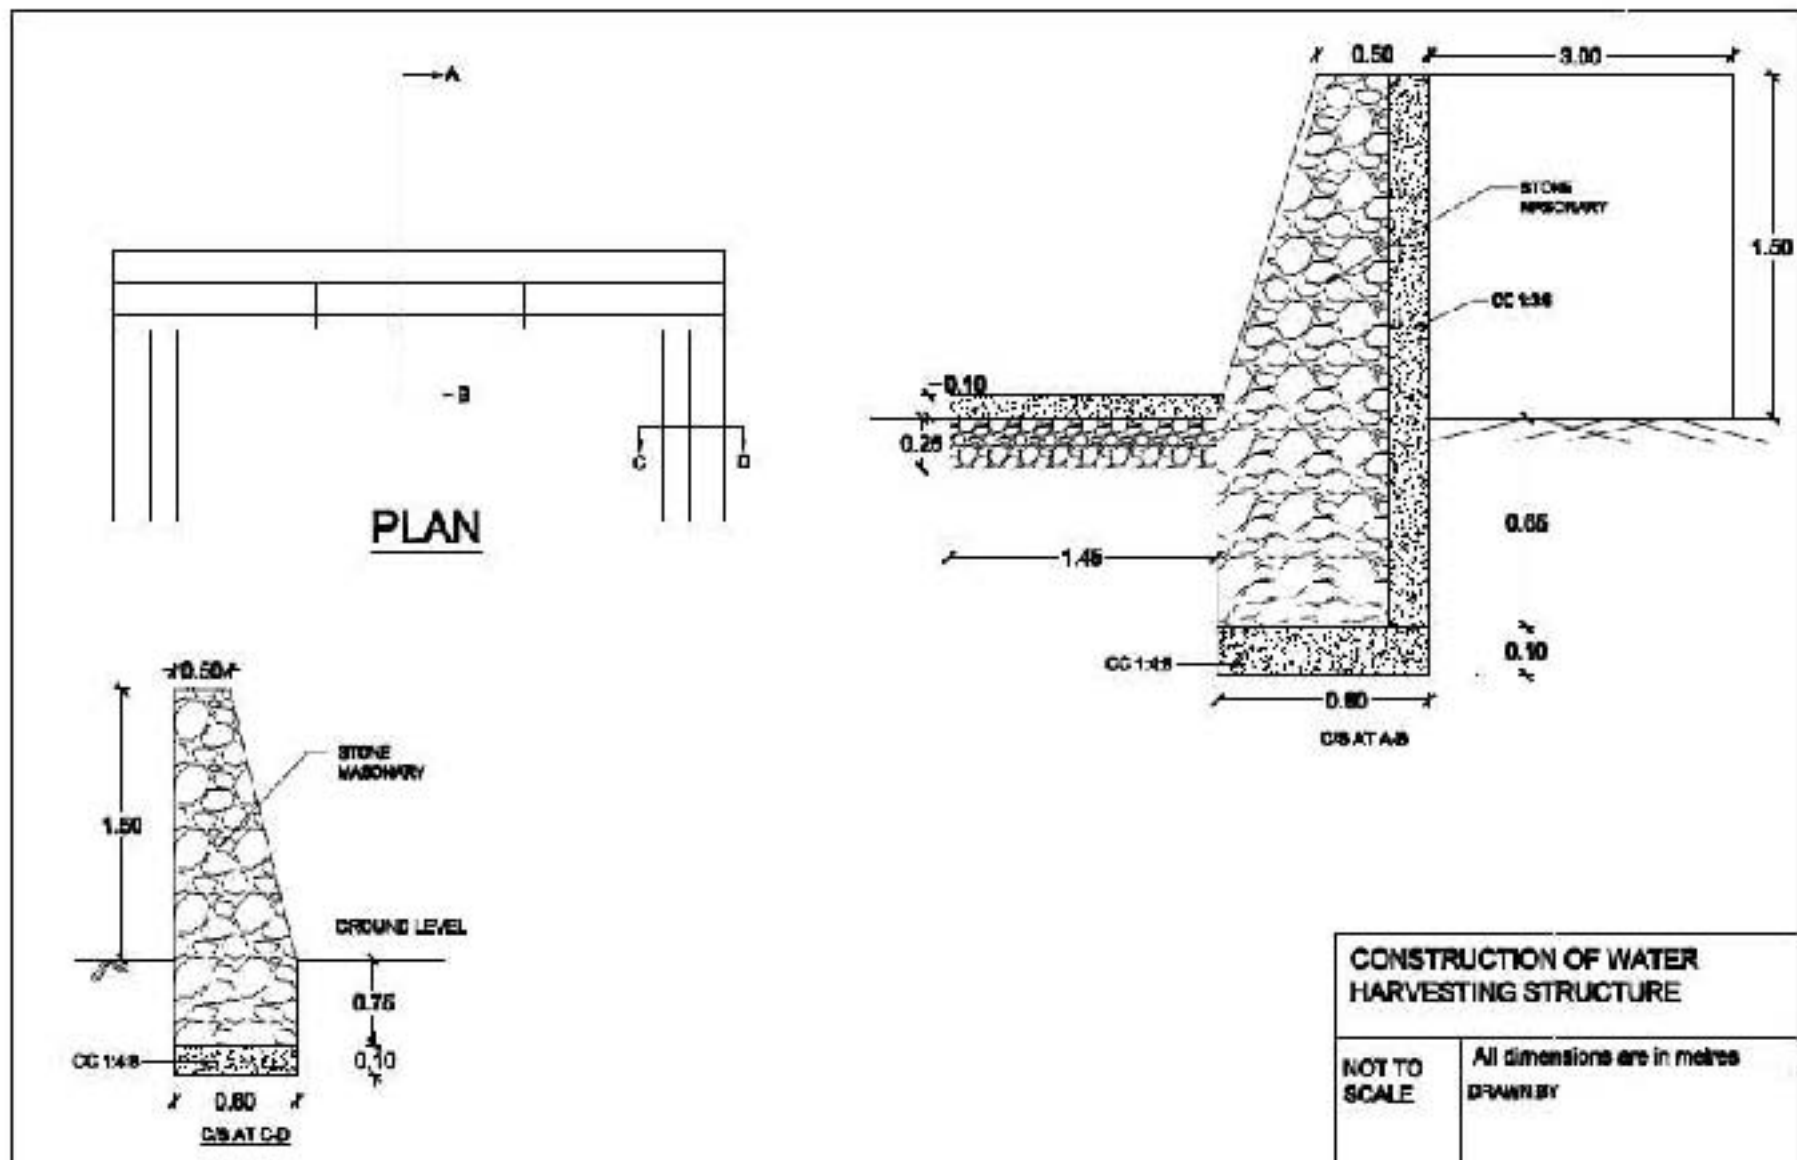

ESTIMATE FOR CONSTRUCTION OF DUG OUT POND.

(Rate Based as per MPWD scheduled or rates for Roads and Bridges for Eastern circle, Shillong for the year 2008-09)

HEIGHT : 2.0 m.




Sl no	PARTICULARS	NO	DIMENSION			QTY	UNIT	RATE (Rs)	AMOUNT (RS)
			L	B	H				
1/3 (b)	Earthwork in excavation to the proper grade including light dressing, providing cambering and super elevation as directed and removal of spoil up to 30m lead and all lift.	1	20	19	0.25	95.00	cu.m		
		4	17	16	0.25	272.00	cu.m		
		1	14	13	0.25	45.50	cu.m		
		TOTAL				412.50	cu.m	39	16087.50

**GRAND
TOTAL**

16087.50

**SAY :- ₹
16,000.00**

RUPEES SIXTEEN THOUSAND ONLY.

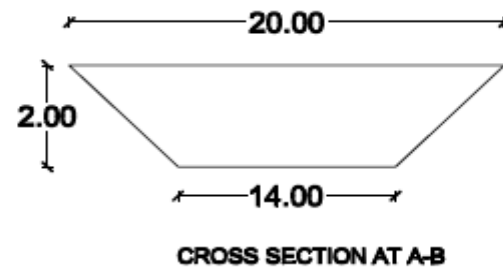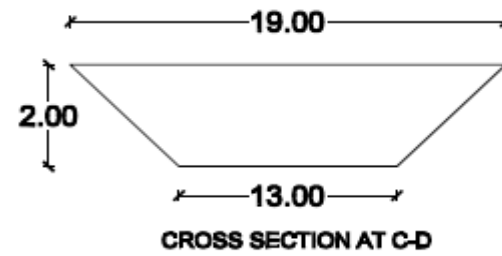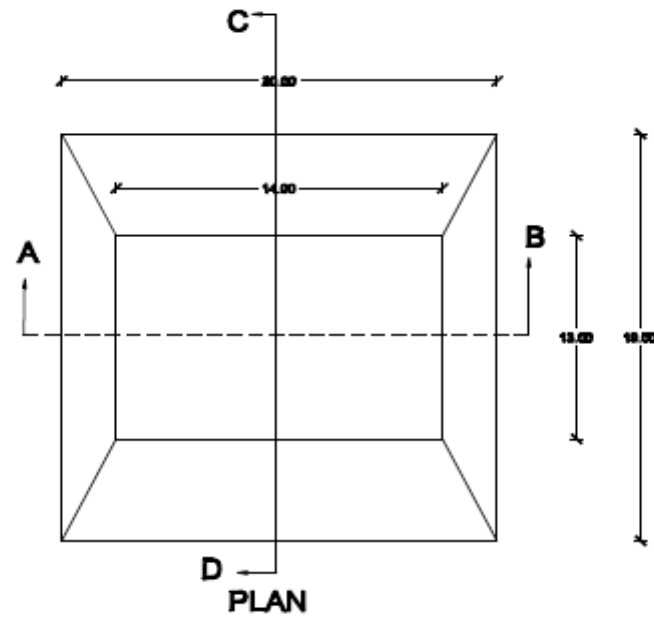

DUG-OUT POND

NOT TO
SCALE

All dimensions are in
metres

DRAWN BY

ESTIMATE FOR CONSTRUCTION OF CONTOUR BUNDING.

WIDTH - (0.50 + 0.30)/2

(Rate Based as per MPWD scheduled or rates for Roads and Bridges for Eastern circle, Shillong for the year 2008-09)



SI no	PARTICULARS	NO	DIMENSION			QTY	UNIT	RATE (Rs)	AMOUNT (RS)
			L	B	H				
1/8	Earthwork in filling with approved earth like sandy soil, moorum etc, in an embankment in layers not exceeding 20cm thick including breaking clods, dressing and ramming and lead upto 30m and lift upto 150cm	1	400	0.4	0.35	56.00	cu.m		
		TOTAL				56.00	cu.m	134	7504.00

GRAND TOTAL

7504.00

Say ₹ 7,500.00 Per Hectare

(RUPEES SEVEN THOUSAND FIVE HUNDRED) ONLY.

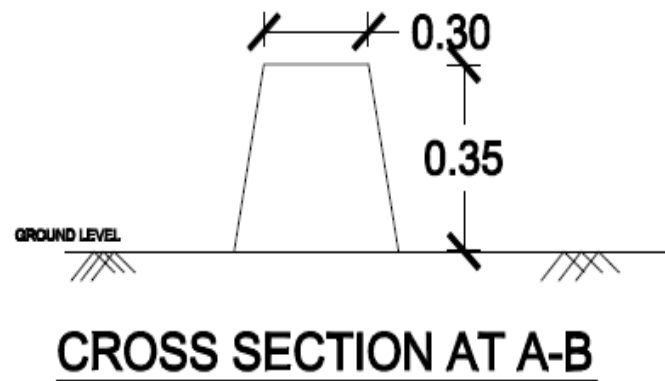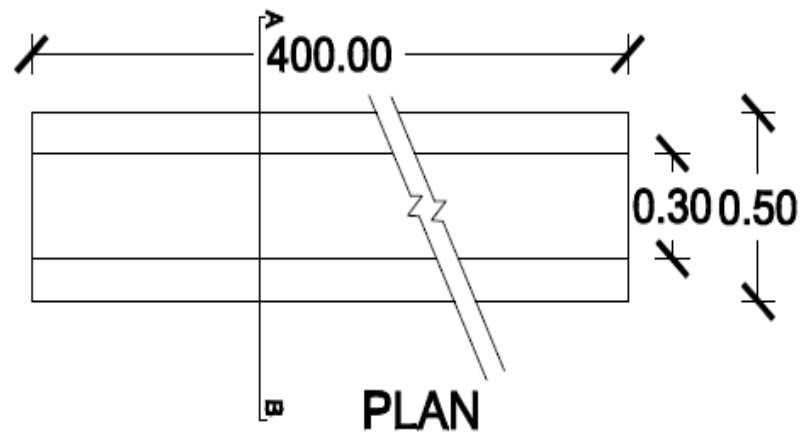

DRAWING OF CONTOUR BUND.

NOT TO
SCALE

All dimensions are in
metres
DRAWN BY

ANNEXURE IV

CERTIFICATE OF REGISTRATION, N.O.C. ETC..



Certificate of Registration of Societies

ACT 12 OF 1983

No. E.16/5/ of 2010/105

I hereby certify that Middle Umalew Watershed Committee
IWMP (2010-11) Project-VIII

has this day been registered under Meghalaya Societies Registration Act,
12 of 1983.

Given under my hand at Shillong
this 11th day of March

Two thousand and eleven

Registration fee of Rs. Two hundred and fifty only.


Registrar of Societies,
Meghalaya, Shillong.



Certificate of Registration of Societies

ACT 12 Of 1983

No. E.16/5/ of 2010/156

I hereby certify that Umprah Watershed Committee
IWMP (2010-11) Project-VIII

has this day been registered under Meghalaya Societies Registration Act,
12 of 1983.

Given under my hand at Shillong
this 11th day of March

Two thousand and eleven

Registration fee of Rs. Two hundred and fifty only.


Registrar of Societies,
Meghalaya, Shillong.

NO OBJECTION CERTIFICATE

This is to certify that the proposed area under Middle Uniew Watershed Committee IWMP – 2010 – 2011 Project – VIII of Mawkynrew C & RD Block, East Khasi Hills District, Meghalaya as indicated in its project proposal (IWMP Scheme) is correct and true as per findings.

Therefore, we certify that we do not have any object to the implementation of this Project as mentioned above.


S. K. D.
Sondur S. K. D.

NO OBJECTION CERTIFICATE


This is to certify that the proposed area under Umprah Watershed IWMP – Project – VIII of Mawkynrew C & RD Block, East Khasi Hills District, Meghalaya as indicated in its project proposal (IWMP Scheme) is correct and true as per findings.

Therefore, we certify that we do not have any object to the implementation of this project as mentioned above.

Sordar/ Rangbah Shnong


SORDAR
Shnong Laitlum
Khyrim Syiemship

Secretary.


H.E. Secretary, Shnong Laitlum
Local Govt. Office
Village Office
Date

NO OBJECTION CERTIFICATE

This is to certify that the proposed area under Umprah Watershed IWMP – Project – VIII of Mawkynrew C & RD Block, East Khasi Hills District, Meghalaya as indicated in its project proposal (IWMP Scheme) is correct and true as per findings.

Therefore, we certify that we do not have any object to the implementation of this project as mentioned above.


Rangbah Shnong
Laltshyhong
Khyrim Sylenship.

Sordar/ Rangbah Shnong


Secretary
Laltshyhong
Khyrim Sylenship
Secretary.
